



Odoo Job Costing and Contracting Bundle

Document Version :

1.1.3

Prepared By :

Probuse Consulting Service Pvt. Ltd.

Office Address:

SAKAR IX, Beside Old Reserve Bank of India, Near City
Gold Cinema, Ashram Road, Ahmedabad,
Gujarat - India 380009

Email:

contact@probuse.com

Website:

www.probuse.com

Contact:

+91-9601119434



User Manual (English)

Contents:

1. [Job Cost Sheets](#) (odoo_job_costing_management)
2. [Actual Cost on Job Cost Sheet](#) (job_costing_cost_actual)
3. [Job Cost Sheet Integration with Material Planning of Job Order](#)(job_order_link_cost_sheet)
4. [Material Purchase Requisition and Cost Sheet Integration](#)(material_requisition_cost_sheet)
5. [Estimation for Jobs - Material / Labour / Overheads](#)(job_cost_estimate_customer)
6. [Sales Estimate Create from Job Cost Sheet](#)(job_cost_and_estimate_relation)
7. [Progress Billing to Customer](#)(odoo_customer_progress_billing)
8. [Customer Invoice from Job Cost Sheet](#)(odoo_job_costing_progress_billing)
9. [Website Job/Work Order Form and Portal](#)(job_workorder_website_request)
10. [Change Order in Job Contracting and Construction](#)(construction_contracting_change_order)
11. [Budget for Job Contracting and Construction Projects](#)(job_costing_budget_contracting)
12. [Equipment and Maintenance Request for Job Work Order](#)(job_equipments_maintenance_request)
13. [Instruction and Quality Checklist on Job Order](#)(job_order_card_instruction)
14. [Expense Integration Job Orders for Project](#)(job_work_order_expense)
15. [Subcontracting in Job Order / Construction / Contracting Industry](#)(job_order_subcontracting)
16. [Construction Projects on Website](#)(website_construction_project_page)
17. [Payroll for Construction and Contracting Industry](#)(construction_contracting_payroll)
18. [Request for Information \(Construction and Contracting Business\)](#)(project_request_for_information)
19. [Job Order / Work Order Inspection](#)(job_inspection)



20. [Project by Phases](#)(odoo_project_phases)
21. [Meeting Minutes for Construction and Contracting Projects](#)(project_meeting_minutes)
22. [Issue Tracking System for Construction and Contracting](#)(construction_contracting_issue_tracking)
23. [Job Drawing Construction and Contracting Business](#)(job_drawing_construction_contracting)
24. [Employee Portal for Issue Tracking System](#)(issue_tracking_employee_portal)
25. [Notes on My Account / Portal / Mobile / Tablets](#)(project_notes_mobile_tablet)
26. [Job Drawing Image Construction and Contracting Business](#)(job_drawing_image_contracting)
27. [Dashboard for Project for Construction and Job Contracting](#)(job_costing_dashboard)
28. [Project Team for Construction and Contracting](#)(odoo_project_team)
29. [Document Management for Job Contracting and Construction](#)(job_costing_contracting_document)
30. [Transmittals / Submittals for Construction and Contracting](#)(transmittals_communication_document)
31. [Construction and Contracting with Equipment & Maintenance](#)(construction_maintenance_equipment)
32. [Work Package for Construction and Contracting](#)(job_costing_work_package)
33. [Repair App for Construction and Contracting](#)(construction_contracting_repair)
34. [Waste Management for Construction and Contracting](#)(construction_waste_management)
35. [Job Costing / Contracting Volumn Trends Report](#)(job_costing_volumn_trend)
36. [Job Costing / Contracting Costing Report](#)(job_cost_trend)
37. [P&L for Job Costing \(Profit and Loss Report\)](#)(job_costing_profit_loss)
38. [Material Consumption on Job Order / Work Order](#)(job_order_material_consumption)
39. [Job Order Material Requisition](#) (job_order_material_requisition)
40. [Job Issue Capture Photo](#)(job_issue_capture_photo)
41. [Risk Managment for construction and contracting projects](#)(job_contracting_construction_risk)
42. [Job Cost Sheet Import from Excel](#)(job_costsheet_import)



Job Cost Sheet

Job cost sheet is a document used to record costs and is prepared by companies that use job-order costing system to compute and allocate costs to products and services.

- ❖ A separate job cost sheet is prepared for each individual job. All necessary details about the job and costs incurred to complete the job are written on the job cost sheet.



Job Cost Sheets / COST-SHEET/00001

Edit Create Print Action Done Create Estimation Cancel Draft Confirmed Approved Done 1 / 1 < >

COST-SHEET/00001

Name	New	Create Date	01/01/2019						
Project	Construction of Hypol Heights	Closed Date							
Analytic Account	Hypol Heights - The Jackson Group	Created By	Mitchell Admin						
Job Order	Project Initiation	Company	YourCompany						
Customer	Lumber Inc	Currency	USD						
Description		Sale Reference							
Materials		Labours	Overhead						
Date	Job Type	Product	Description	Reference	Planned Qty Uom	Cost / Unit	Actual Purchased Quantity	Actual Vendor Bill Quantity	Cost Price Sub Total
01/01/2019	Site-Preparation-MAT	Cement	Cement		50.00 Unit(s)	350.00	200.00	40.00	\$ 17,500.00
01/02/2019	Site-Preparation-MAT	Bricks	Bricks		2,000.00 Unit(s)	10.00	2,000.00	30.00	\$ 20,000.00
01/03/2019	Site-Preparation-MAT	Tiles	Tiles		500.00 Unit(s)	40.00	570.00	200.00	\$ 20,000.00
01/04/2019	Site-Preparation-MAT	Iron	Iron		500.00 kg	35.00	500.00	45.00	\$ 17,500.00
01/04/2019	Site-Preparation-MAT	White Cement	White Cement		100.00 Unit(s)	35.00	45.00	40.00	\$ 3,500.00
01/08/2019	Site-Preparation-MAT	Door	Door		25.00 Unit(s)	2,000.00	1.00	25.00	\$ 50,000.00

❖ **Job Cost Sheet - Materials:** Select Job type with Materials Tabs part of the finished product. The cost of materials constitutes a major portion of the total costs of a job. Therefore, the actual cost of materials used for job is directly charged to the specific job.



Job Cost Sheets / COST-SHEET/00001

		Description Sale Reference									
Materials			Labours			Overhead					
Date	Job Type	Product	Description	Reference	Planned Qty Uom	Cost / Unit	Actual Purchased Quantity	Actual Vendor Bill Quantity	Cost Price Sub Total		
01/01/2019	Site-Preparation-MAT	Cement	Cement		50.00 Unit(s)	350.00	200.00	40.00	\$ 17,500.00		
01/02/2019	Site-Preparation-MAT	Bricks	Bricks		2,000.00 Unit(s)	10.00	2,000.00	30.00	\$ 20,000.00		
01/03/2019	Site-Preparation-MAT	Tiles	Tiles		500.00 Unit(s)	40.00	570.00	200.00	\$ 20,000.00		
01/04/2019	Site-Preparation-MAT	Iron	Iron		500.00 kg	35.00	500.00	45.00	\$ 17,500.00		
01/04/2019	Site-Preparation-MAT	White Cement	White Cement		100.00 Unit(s)	35.00	45.00	40.00	\$ 3,500.00		
01/08/2019	Site-Preparation-MAT	Door	Door		25.00 Unit(s)	2,000.00	1.00	25.00	\$ 50,000.00		
					3,175.00	2,470.00	3,316.00	380.00	128,500.00		

Job Cost Details

Total Material Cost:	\$ 128,500.00
Total Labour Cost:	\$ 2,760.00
Total Overhead Cost:	\$ 640.00

❖ **Job Cost Sheet - Labours:** The information of labour costs are obtained from various records like job Costsheets, time cards or piece work cards. The time of commencement of work and the time of stopping the work are recorded on the Job Costsheet.



Job Cost Sheets / COST-SHEET/00001

Edit Create Print Action

COST-SHEET/00001								
Name	New	Create Date	01/01/2019					
Project	Construction of Hypol Heights	Closed Date						
Analytic Account	Hypol Heights - The Jackson Group	Created By	Mitchell Admin					
Job Order	Project Initiation	Company	YourCompany					
Customer	Lumber Inc	Currency	USD					
Description	Sale Reference							
Materials	Labours	Overhead						
Date	Job Type	Product	Description	Reference	Hours	Cost / Unit	Actual Timesheet Hours	Cost Price Sub Total
01/09/2019	Site-Preparation-LAB	Ground Floor Wages	Ground Floor Wages		08:00	100.00	26:00	\$ 800.00
01/16/2019	Site-Preparation-LAB	Tiles Feeting	Tiles Feeting		08:00	120.00	24:00	\$ 960.00
01/18/2019	Site-Preparation-LAB	Waterproofing	Waterproofing		08:00	100.00	08:00	\$ 800.00
01/17/2019	Site-Preparation-LAB	Italian Marble Fixing	Italian Marble Fixing		08:00	25.00	00:00	\$ 200.00
					32:00	345.00	58:00	2,760.00
Job Cost Details Total Material Cost: \$ 128,500.00 Total Labour Cost: \$ 2,760.00 Total Overhead Cost: \$ 640.00 Total Cost: \$ 131,900.00								

❖ **Job Cost Sheet - Overhead:** Overhead rate is used to charge Costsheet overhead. Likewise, administration, selling and distribution overheads by each job costsheet on suitable basis. The total cost of collected overheads are on job cost sheet.



Jobs Job Costs Project Issues Projects Job Orders Sub Contractors Waste Reporting Materials / BOQ Change Orders Analytic Account Invoicing Reports Configuration C Mitchell Admin

Job Cost Sheets / COST-SHEET/00001

Edit Create Print Action 1 / 1

COST-SHEET/00001											
Name	New	Create Date	01/01/2019								
Project	Construction of Hypol Heights	Closed Date									
Analytic Account	Hypol Heights - The Jackson Group	Created By	Mitchell Admin								
Job Order	Project Initiation	Company	Your Company								
Customer	Lumber Inc	Currency	USD								
Description	Sale Reference										
Materials	Labours	Overhead									
Date	Job Type	Product	Description	Reference	Basis	Planned Qty Uom	Cost / Unit	Actual Purchased Quantity	Actual Vendor Bill Quantity	Cost Price Sub Total	
01/08/2019	Site-Preparation-OHD	Electricity Bill	Electricity Bill			1.00 Unit(s)	200.00	1.00	1.00	\$ 200.00	
01/29/2019	Site-Preparation-OHD	[EXP_CTD] Car Travel Expenses	Car Travel Expenses			1.00 km	300.00	1.00	1.00	\$ 300.00	
01/24/2019	Site-Preparation-OHD	Truck Rent	Truck Rent			1.00 Unit(s)	120.00	1.00	1.00	\$ 120.00	
01/23/2019	Site-Preparation-OHD	Wiring Works	Wiring Works			1.00 Unit(s)	20.00	1.00	1.00	\$ 20.00	
							4.00	640.00	4.00	4.00	640.00

Job Cost Details Total Material Cost: \$ 128,500.00

❖ **Job Types:** Job types define on Material, Labour and Overhead Tab.



Jobs Job Costs Project Issues Projects Job Orders Sub Contractors Waste Reporting Materials / BOQ Change Orders Analytic Account Invoicing + C ⚡ * Mitchell Admin (apps12_jobcosting_bundle)

Job Type Search... Filters ▾ Group By ▾ Favorites ▾

Create Import 1-12 / 12 < >

Name	Code	Type
<input type="checkbox"/> Paint-Labour	PT-LABOUR	Labour
<input type="checkbox"/> Paint-Material	PT-MATERIAL	Material
<input type="checkbox"/> Paint-Overhead	PT-OVERHEAD	Overhead
<input type="checkbox"/> Electrical Material	ELMAT-01	Material
<input type="checkbox"/> Electrical Labour	ELLAB-02	Labour
<input type="checkbox"/> Electrical Overhead	ELOHD-03	Overhead
<input type="checkbox"/> Kitchen Material	KITCHEN-MAT	Material
<input type="checkbox"/> Kitchen Overhead	KITCHEN-OHD	Overhead
<input type="checkbox"/> Kitchen Labour	KITCHEN-LAB	Labour
<input type="checkbox"/> Site-Preparation-LAB	SITE-LAB	Labour
<input type="checkbox"/> Site-Preparation-MAT	SITE-MAT	Material
<input type="checkbox"/> Site-Preparation-OHD	SITE-OHD	Overhead

❖ **Timesheet :** On timesheet filling Select the Job Cost Center and Job Cost Line.



All Timesheets												Search...								
												Filters ▾ Group By ▾ ★ Favorites ▾								
	Date	Employee	Description	Start Time	End Time	Job Cost Center	Job Cost Line	Project	Task	Project Issue	Billable	Time In	Time Out	Machine Repair	Work Type	Start Time	End Time	Is Billable	Is Paid	Durat (Hour)
<input type="checkbox"/>	01/08/2019	Anita Oliver	Site Preparation	00:00	00:00	COST-SHEET/00001	Ground Floor Wages	Construction of Hypol Heights	Project Initiation	<input checked="" type="checkbox"/>	00:00	00:00			00:00	00:00	<input type="checkbox"/>	<input type="checkbox"/>	0E	
<input type="checkbox"/>	01/04/2019	Mitchell Admin	Ground Flooring Works	00:00	00:00	COST-SHEET/00001	Ground Floor Wages	Construction of Hypol Heights	Flooring Works	<input checked="" type="checkbox"/>	00:00	00:00			00:00	00:00	<input type="checkbox"/>	<input type="checkbox"/>	0E	
<input type="checkbox"/>	01/03/2019	Mitchell Admin	Ground Flooring Works	00:00	00:00	COST-SHEET/00001	Ground Floor Wages	Construction of Hypol Heights	Flooring Works	<input checked="" type="checkbox"/>	00:00	00:00			00:00	00:00	<input type="checkbox"/>	<input type="checkbox"/>	0E	
<input type="checkbox"/>	01/03/2019	Anita Oliver	Resource planning and management	00:00	00:00	COST-SHEET/00001	Tiles Feeling	Construction of Hypol Heights	Project Initiation	<input checked="" type="checkbox"/>	00:00	00:00			00:00	00:00	<input type="checkbox"/>	<input type="checkbox"/>	0E	
<input type="checkbox"/>	01/02/2019	Mitchell Admin	Ground Flooring Works	00:00	00:00	COST-SHEET/00001	Tiles Feeling	Construction of Hypol Heights	Flooring Works	<input checked="" type="checkbox"/>	00:00	00:00			00:00	00:00	<input type="checkbox"/>	<input type="checkbox"/>	0E	
<input type="checkbox"/>	01/01/2019	Mitchell Admin	Ground Flooring Works	00:00	00:00	COST-SHEET/00001	Tiles Feeling	Construction of Hypol Heights	Flooring Works	<input checked="" type="checkbox"/>	00:00	00:00			00:00	00:00	<input type="checkbox"/>	<input type="checkbox"/>	0E	
<input type="checkbox"/>	01/01/2019	Anita Oliver	Site Preparation	00:00	00:00	COST-SHEET/00001	Waterproofing	Construction of Hypol Heights	Project Initiation	<input checked="" type="checkbox"/>	00:00	00:00			00:00	00:00	<input type="checkbox"/>	<input type="checkbox"/>	0E	
<input type="checkbox"/>	12/30/2018	Mitchell Admin	Requirements analysis	00:00	00:00	COST-SHEET/00001	Ground Floor Wages	Research & Development	<input checked="" type="checkbox"/>	00:00	00:00			00:00	00:00	<input type="checkbox"/>	<input type="checkbox"/>	0E		
<input type="checkbox"/>	12/30/2018	Mitchell Admin	Design	00:00	00:00			Research & Development	<input checked="" type="checkbox"/>	00:00	00:00			00:00	00:00	<input type="checkbox"/>	<input type="checkbox"/>	01		
<input type="checkbox"/>	12/30/2018	Mitchell Admin	Quality analysis	00:00	00:00			Research & Development	<input checked="" type="checkbox"/>	00:00	00:00			00:00	00:00	<input type="checkbox"/>	<input type="checkbox"/>	03		
<input type="checkbox"/>	12/30/2018	Mitchell Admin	Quality analysis	00:00	00:00			Research & Development	<input checked="" type="checkbox"/>	00:00	00:00			00:00	00:00	<input type="checkbox"/>	<input type="checkbox"/>	01		
<input type="checkbox"/>	12/30/2018	Mitchell Admin	Delivery	00:00	00:00			Research & Development	<input checked="" type="checkbox"/>	00:00	00:00			00:00	00:00	<input type="checkbox"/>	<input type="checkbox"/>	01		

❖ **Purchase Order:** Selected Job Costsheet and cost line on purchase order line affected on Job Costsheet Material and Overhead.



Purchase Purchase Control Reporting Configuration

Mitchell Admin (apps12_jobcosting_bundle)

Requests for Quotation / PO00008

Edit Create Print Action

5 / 12 RFQ RFQ Sent Purchase Order

Receive Products Send PO by Email Create Bill Cancel Lock

PO00008										1 Vendor Bills	1 Receipt			
Vendor	Gemini Furniture			Order Date	01/01/2019 15:33:10									
Vendor Reference				Stock Picking Company	YourCompany									
Sub Contractor Job														
Currency	USD													
Products Other Information														
Product	Description	Job Cost Center	Job Cost Line	Scheduled Date	Company	Analytic Account	Analytic Tags	Quantity	Received Qty	Billed Qty	Unit Measure	Product Unit Price	Taxes	Subtotal
Bricks	Bricks	COST-SHEET/00001	Bricks	01/01/2019 15:34:51	YourCompany	Hypol Heights - The Jackson Group		2,000.000	0.000	0.000	Unit(s)	10.00	(Tax 15.00%)	\$ 20,000.00
Cement	Cement	COST-SHEET/00001	Cement	01/01/2019 15:35:05	YourCompany	Hypol Heights - The Jackson Group		200.000	0.000	0.000	Unit(s)	350.00	(Tax 15.00%)	\$ 70,000.00
Iron	Iron	COST-SHEET/00001	Iron	01/01/2019 15:36:00	YourCompany	Hypol Heights - The Jackson Group		500.000	0.000	0.000	kg	200.00	(Tax 15.00%)	\$ 100,000.00
													Untaxed Amount:	\$ 190,000.00

❖ **Vendor Bill:** Selected Job Costsheet and Costsheet line on bill that affected on Job Costsheet Material, Overhead Tab.



Invoicing Overview Customers Vendors Accounting Reporting Configuration

Vendor Bills / BILL/2019/0002

Edit Create Print Action

5 / 11 Mitchell Admin (apps12_jobcosting_bundle)

Register Payment Ask for a Credit Note Draft Open Paid

Bill BILL/2019/0002											
Vendor Vendor Reference		Gemini Furniture				Bill Date					
						01/10/2019	Due Date	01/10/2019	Currency	USD	Bank Account
											00987654322
Bill	Other Info										
Product	Description	Job Cost Center	Job Cost Line	Account	Analytic Account	Analytic Tags	Unit of Measure	Unit Price	Discount (%)	Taxes	Amount
Tiles	Tiles	COST-SHEET/00001	Tiles	101120 Stock Interim Account (Received)	Hypol Heights - The Jackson Group		200.000 Unit(s)	60.00	0.00	Tax 15.00%	\$ 12,000.00
Cement	Cement	COST-SHEET/00001	Cement	220000 Expenses	Hypol Heights - The Jackson Group		40.000 Unit(s)	20.00	0.00	Tax 15.00%	\$ 800.00
Bricks	Bricks	COST-SHEET/00001	Bricks	101120 Stock Interim Account (Received)	Hypol Heights - The Jackson Group		30.000 Unit(s)	30.00	0.00	Tax 15.00%	\$ 900.00
White Cement	White Cement	COST-SHEET/00001	White Cement	220000 Expenses	Hypol Heights - The Jackson Group		40.000 Unit(s)	20.00	0.00	Tax 15.00%	\$ 800.00
Door	Door	COST-SHEET/00001	Door	101120 Stock Interim Account (Received)	Hypol Heights - The Jackson Group		25.000 Unit(s)	2,000.00	0.00	Tax 15.00%	\$ 50,000.00
Iron	Iron	COST-SHEET/00001	Iron	101120 Stock Interim Account (Received)	Hypol Heights - The Jackson Group		45.000 kg	35.00	0.00	Tax 15.00%	\$ 1,575.00



❖ **Projects** : Project with define Costsheets to record and analyze actual expenditures on a job. On large or long-term projects, unit costs can vary over time. Project that associate task or job orders.

Jobs Job Costs Project Issues Projects Job Orders Sub Contractors Waste Reporting Materials / BOQ Change Orders + G ? * Mitchell Admin (apps12_jobcosting_bundle)

Projects / Construction of Hypol Heights

Edit Create Print Action 1 / 3 < >

Share

Construction of Hypol Heights

Name of the tasks : Tasks Allow timesheets

	0 Documents		5 Tasks		Timesheets
	Active		1 Jobcosts		8 Notes
	Phases	More ▾			

Settings Description Brochures Construction Site Detail More Project Images Gallery Images Project Features And Amenities Specification Contact Us

Project Floor Plan Project Location Plan Timesheet Employee Users

Project Manager	Camron Grill
Privacy	Visible by following customers
Customer	Azure Interior
Analytic Account	Hypol Heights - The Jackson Group
Price / Rate (Company Currency)	55,000,000.00
Product	[Deposit] Deposit
Reference	No rating
Customer(s) Ratings	
Sub-task Project	Construction of Hypol Heights



❖ **Job Orders / Task:** Project management, a task is an activity that needs to be accomplished within a defined period of time or by a deadline to work towards work-related goals. It is a small essential piece of a job that serves as a means to differentiate various components of a project.

Jobs Job Costs Project Issues Projects Job Orders Sub Contractors Waste Reporting Materials / BOQ Change Orders Analytic Account Invoicing + Mitchell Admin (apps12_jobcosting_bundle)

Job Orders / Project Initiation Edit Create Print Action 5 / 9

Project Initiation			
Project	Construction of Hypol Heights	Deadline	
Project Phase	Planning/Design phase	Tags	
Assigned to	Mitchell Admin	12/31/2020	
Starting Date	12/31/2018 18:13:23	Need Assistance New Feature	
Ending Date	01/31/2019 11:12:56		
Job Number			
Description	Waste Materials	Material Plannings	
Website	Purchase Requisitions	Subtasks	
Consumed Materials	Material Requisitions	Timesheets	
Extra Info	Timesheet Employee Users		
Planned Hours	40:00	Progress <div style="width: 60%;">60%</div>	
Date	Employee	Description	Duration (Hour(s))
01/01/2019	Anita Oliver	Site Preparation	08:00
01/03/2019	Anita Oliver	Resource planning and management	08:00
01/08/2019	Anita Oliver	Site Preparation	08:00
			Hours Spent: 24:00




❖ **Project - Project Notes:** Add notes to a project or to the project schedule. To include additional or supporting information, you can add a note to project, resource, assignment to the entire project.

A screenshot of a software application interface titled "Jobs". The top navigation bar includes links for Job Costs, Project Issues, Projects, Job Orders, Sub Contractors, Waste Reporting, Materials / BOQ, Change Orders, and user authentication ("Mitchell Admin (apps12_jobcosting_bundle)"). The main content area is titled "Notes" and contains four columns: "New", "Meeting Minutes", "Notes", and "Todo". Each column has a "Create" button and a "Search" bar. The "New" column contains one item: "Construction Start". The "Meeting Minutes" column contains one item: "Red Room Detail". The "Notes" and "Todo" columns are currently empty. There are buttons for "Filters", "Group By", and "Favorites" at the top of the list area, and a "Add a Column" button on the right.



❖ **Job Order - Job Notes:** Add notes to a job order or project. To include additional or supporting information, you can add a note to a job order.

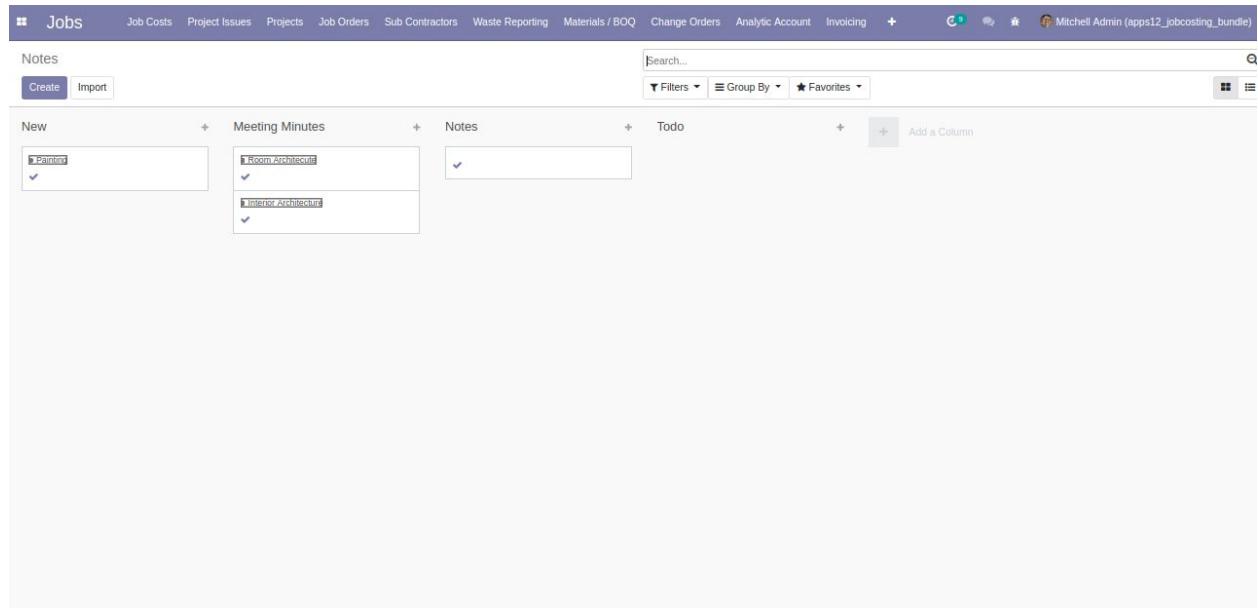

A screenshot of the Odoo Notes module interface. The top navigation bar includes links for Jobs, Job Costs, Project Issues, Projects, Job Orders, Sub Contractors, Waste Reporting, Materials / BOQ, Change Orders, Analytic Account, Invoicing, and a user profile for Mitchell Admin (apps12_jobcosting_bundle). The main area is titled 'Notes' and shows four columns: 'New', 'Meeting Minutes', 'Notes', and 'Todo'. The 'New' column contains a list with 'Painter' checked. The 'Meeting Minutes' column contains a list with 'Room Architecture' and 'Interior Architecture' checked. The 'Notes' and 'Todo' columns are currently empty. There are search, filter, group by, and favorite buttons at the top of the list view, along with an 'Add a Column' button.



Job Cost Sheet Integration with Material Planning of Job Order

- ❖ Allow you to Create / Edit Job Costsheet Material Plannings from Job Order. Job cost software activities like purchasing materials and to a job, collecting labor through either Labor Collection or Job Planning.

JOB/0004

Flooring Works

Sub-tasks	Active	Jobcosts
0	0	0

Stock Moves	Notes	Subcontractor Jobs
0	0	0

Purchase Re...	More
0	

Description	Waste Materials	Material Plannings	Website	Purchase Requisitions	Subtasks	Consumed Materials	Material Requisitions	Timesheets
Bricks	Bricks	50 Unit(s)						
Cement	Cement	20 Unit(s)						
Tiles	Tiles	30 Unit(s)						

Send message Log note Schedule activity

January 1, 2019



❖ Create or Edit Job Costsheet on Job Order or Task.

Screenshot of Odoo software interface showing the creation of a Job Cost Sheet for a Job Order.

The main menu bar includes: Jobs, Job Costs, Project Issues, Projects, Job Orders, Sub Contractors, Waste Reporting, Materials / BOM, Change Orders, Analytic Account, Invoicing, Reports, Costing Reports, Configuration.

The sub-menu for Job Orders shows: Edit, Create, Share, Create Subtasks, Create Subcontractor Job, Create Repair Job, Send by Email.

The Job Order details are as follows:

- Project:** Construction of Hypol Heights
- Project Phase:** Flooring Works
- Assigned to:** Mitchell Admin
- Starting Date:** 01/02/2019 11:00:42
- Ending Date:** 03/03/2019 11:30:42
- Job Number:** JOB/00006

The Material Planning section shows:

Description	Waste Materials	Material Planning	Website	Purchase Requisitions	Subtasks	Consumed Materials	Material Requisitions	Timesheets
Extra info Timesheet Employee Users								
Product	Description	Quantity	Unit of Measure	Job Cost Sheet				
Bricks	Bricks	50	Unit(s)					
Cement	Cement	20	Unit(s)					
Tiles	Tiles	30	Unit(s)					

Buttons at the bottom include: Send message, Log note, Schedule activity, Following, 2.

The date January 1, 2019 is displayed at the bottom center.



❖ Created Job Costsheet on Job Order or Task.

Screenshot of Odoo Job Cost Sheet creation interface:

Job Orders / Flooring Works / Job Cost Sheets / COST-SHEET/00002

COST-SHEET/00002

Name	New	Create Date	01/03/2019
Project	Construction of Hypol Heights	Closed Date	
Analytic Account	Hypol Heights - The Jackson Group	Created By	Mitchell Admin
Job Order	Flooring Works	Company	Your Company
Customer	Azure Interior	Currency	USD
Description	Sale Reference		

Materials	Labours	Overhead											
Date	Job Type	Product	Description	Reference	Planned Qty	Uom	Cost / Unit	Actual Requisition Quantity	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Cost Price Sub Total
01/03/2019		Bricks	Bricks		50.00	Unit(s)	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00
01/03/2019		Cement	Cement		20.00	Unit(s)	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00
01/03/2019		Tiles	Tiles		30.00	Unit(s)	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00
								100.00	0.00	0.00	0.00	0.00	0.00

Job Cost Details

Total Material Cost:	\$ 0.00
Total Labour Cost:	\$ 0.00
Total Overhead Cost:	\$ 0.00
Total Cost:	\$ 0.00



❖ Job Costsheet reference set on Job Order Material Planning Tab.

The screenshot shows the Odoo interface for managing job orders. The top navigation bar includes links for Jobs, Job Costs, Project Issues, Projects, Job Orders, Sub Contractors, Waste Reporting, Materials / BOQ, Change Orders, Analytic Account, Invoicing, Reports, Costing Reports, and Configuration. The current user is Mitchell Admin (appos12_jobcosting_bundle).

The main view displays Job 0004 for Flooring Works. Key details shown include:

- Project:** Construction of Hypol Heights
- Project Phase:** Flooring Works
- Assigned to:** Mitchell Admin
- Starting Date:** 01/02/2019 11:00:42
- Ending Date:** 03/30/2019 11:30:42
- Job Number:** JOB/00006
- Deadline:** 06/30/2019
- Tags:** Flooring

On the right, a summary table provides quick access to related data:

0 Sub-tasks	1 Active	1 Jobcosts
0 Stock Moves	0 Notes	Subcontractor
0 Purchase Re...	More	Jobs

The **Material Planning** tab is currently selected, displaying a list of products and their details:

Product	Description	Quantity	Unit of Measure	Job Cost Sheet
Bricks	Bricks	50	Unit(s)	COST-SHEET/00002
Cement	Cement	20	Unit(s)	COST-SHEET/00002
Tiles	Tiles	30	Unit(s)	COST-SHEET/00002

At the bottom, there are buttons for Send message, Log note, and Schedule activity, along with a Following status indicator and a date filter set to January 1, 2019.



❖ Need New material on job order or task.

Screenshot of Odoo Job Orders / Flooring Works interface:

- Job Order Details:** JOB/0004, Project: Construction of Hypol Heights, Phase: Flooring Works, Assigned to: Mitchell Admin, Starting Date: 01/02/2019 11:00:42, Ending Date: 03/30/2019 11:30:42, Job Number: JOB/00006.
- Material Planning:** Shows a table of materials with descriptions, quantities, unit of measure, and job cost sheet links.
- Job Cost Sheet:** A modal window titled "# Create or Edit Job Cost Sheet of Material Planning" is open, showing options to "Create Job Cost Sheet" or "Update Job Cost Sheet".
- Timeline:** January 1, 2019.

❖ Edit or Update Material on Job Costsheets from Job Order.

Screenshot of Odoo Job Orders / Flooring Works interface, showing the "Create or Edit Job Cost Sheet of Material Planning" modal window:

- Job Order Details:** JOB/0004, Project: Construction of Hypol Heights, Phase: Flooring Works, Assigned to: Mitchell Admin, Starting Date: 01/02/2019 11:00:42, Ending Date: 03/30/2019 11:30:42, Job Number: JOB/00006.
- Material Planning:** Shows a table of materials with descriptions, quantities, unit of measure, and job cost sheet links.
- Job Cost Sheet:** The modal window shows the "Job Cost Sheet" dropdown set to "COST-SHEET/00002".
- Buttons:** Execute or Cancel.
- Timeline:** January 1, 2019.



❖ Add or Update Material on Costsheet from Job Order Material.

Screenshot of Odoo Job Cost Sheet interface:

Job Orders / Flooring Works / Job Cost Sheets / COST-SHEET/00002

COST-SHEET/00002

Name	New	Create Date	01/03/2019																																																																																																					
Project	Construction of Hypol Heights	Closed Date																																																																																																						
Analytic Account	Hypol Heights - The Jackson Group	Created By	Mitchell Admin																																																																																																					
Job Order	Flooring Works	Company	YourCompany																																																																																																					
Customer	Azure Interior	Currency	USD																																																																																																					
Description		Sale Reference																																																																																																						
<table border="1"> <thead> <tr> <th>Materials</th> <th>Labours</th> <th>Overhead</th> </tr> <tr> <th>Date</th> <th>Job Type</th> <th>Product</th> <th>Description</th> <th>Reference</th> <th>Planned Qty</th> <th>Uom</th> <th>Cost / Unit</th> <th>Actual Requisition Quantity</th> <th>Actual Purchased Quantity</th> <th>Actual Purchased Cost</th> <th>Actual Vendor Bill Quantity</th> <th>Actual Vendor Bill Cost</th> <th>Cost Price Sub Total</th> </tr> </thead> <tbody> <tr> <td>01/03/2019</td> <td></td> <td>Bricks</td> <td>Bricks</td> <td></td> <td>50.00</td> <td>Unit(s)</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>\$ 0.00</td> </tr> <tr> <td>01/03/2019</td> <td></td> <td>Cement</td> <td>Cement</td> <td></td> <td>20.00</td> <td>Unit(s)</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>\$ 0.00</td> </tr> <tr> <td>01/03/2019</td> <td></td> <td>Tiles</td> <td>Tiles</td> <td></td> <td>30.00</td> <td>Unit(s)</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>\$ 0.00</td> </tr> <tr> <td>01/03/2019</td> <td></td> <td>Iron</td> <td>Iron</td> <td></td> <td>40.00</td> <td>kg</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>\$ 0.00</td> </tr> <tr> <td>01/03/2019</td> <td></td> <td>White Cement</td> <td>White Cement</td> <td></td> <td>50.00</td> <td>kg</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>0.00</td> <td>\$ 0.00</td> </tr> <tr> <td colspan="14" style="text-align: right;">190.00 0.00 0.00 0.00 0.00 0.00</td> </tr> </tbody> </table>				Materials	Labours	Overhead	Date	Job Type	Product	Description	Reference	Planned Qty	Uom	Cost / Unit	Actual Requisition Quantity	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Cost Price Sub Total	01/03/2019		Bricks	Bricks		50.00	Unit(s)	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00	01/03/2019		Cement	Cement		20.00	Unit(s)	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00	01/03/2019		Tiles	Tiles		30.00	Unit(s)	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00	01/03/2019		Iron	Iron		40.00	kg	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00	01/03/2019		White Cement	White Cement		50.00	kg	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00	190.00 0.00 0.00 0.00 0.00 0.00													
Materials	Labours	Overhead																																																																																																						
Date	Job Type	Product	Description	Reference	Planned Qty	Uom	Cost / Unit	Actual Requisition Quantity	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Cost Price Sub Total																																																																																											
01/03/2019		Bricks	Bricks		50.00	Unit(s)	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00																																																																																											
01/03/2019		Cement	Cement		20.00	Unit(s)	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00																																																																																											
01/03/2019		Tiles	Tiles		30.00	Unit(s)	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00																																																																																											
01/03/2019		Iron	Iron		40.00	kg	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00																																																																																											
01/03/2019		White Cement	White Cement		50.00	kg	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00																																																																																											
190.00 0.00 0.00 0.00 0.00 0.00																																																																																																								
Job Cost Details Total Material Cost: \$ 0.00 Total Labour Cost: \$ 0.00 Total Overhead Cost: \$ 0.00 Total Cost: \$ 0.00																																																																																																								



Material Purchase Requisition and Cost Sheet Integration

- ❖ Allow you to integrate between Job Costsheet and Material Purchase Requisition lines.

Screenshot of the Odoo application interface showing a Purchase Requisition (EPR00001) details page.

Header:

- Purchase Requisitions / EPR00001
- Actions: Edit, Create, Print, Action
- User: Mitchell Admin (apps12_jobcosting_bundle)
- Status: 1 / 1

Requisition Details:

Employee	Mitchell Admin	Requisition Date	01/01/2019
Department	Management	Received Date	01/03/2019
Company	YourCompany	Requisition Deadline	
Requisition Responsible	Abigail Peterson	Analytic Account	Hypol Heights - The Jackson Group
Maintenance Request			
Job Order	Project Initiation		
Project	Construction of Hypol Heights		
Task / Job Order	Project Initiation		
Task / Job Order User	Mitchell Admin		
Project	Construction of Hypol Heights		

Requisitions Lines:

Requisition Action	Product	Job Cost Center	Job Cost Line	Description	Quantity	Unit of Measure	Vendors
Purchase Order	Cement	COST-SHEET/00001	Cement	Cement	50.00	Unit(s)	Wood Corner
Purchase Order	Bricks	COST-SHEET/00001	Bricks	Bricks	2,000.00	Unit(s)	Wood Corner, Ron Gibson
Purchase Order	Tiles	COST-SHEET/00001	Tiles	Tiles	500.00	Unit(s)	Azure Interior, Nicole Ford
Internal Picking	Iron	COST-SHEET/00001	Iron	Iron	500.00	kg	
Internal Picking	White Cement	COST-SHEET/00001	White Cement	White Cement	50.00	Unit(s)	

Reason for Requisitions:

Send message Log note

Following 1 Today



- ❖ Actual Purchase Requisition Cost are Update on Job Costsheet Material Tab.

COST-SHEET/00001													
Materials				Labours				Overhead					
Date	Job Type	Product	Description	Reference	Planned Qty	Uom	Cost / Unit	Actual Requisition Quantity	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Cost Price Sub Total
01/01/2019	Site-Preparation-MAT	Cement	Cement		50.00	Unit(s)	350.00	50.00	200.00	70,000.00	40.00	800.00	\$ 17,500.00
01/02/2019	Site-Preparation-MAT	Bricks	Bricks		2,000.00	Unit(s)	10.00	2,000.00	2,000.00	20,000.00	30.00	900.00	\$ 20,000.00
01/03/2019	Site-Preparation-MAT	Tiles	Tiles		500.00	Unit(s)	40.00	500.00	570.00	25,400.00	200.00	12,000.00	\$ 20,000.00
01/04/2019	Site-Preparation-MAT	Iron	Iron		500.00	kg	35.00	500.00	500.00	100,000.00	45.00	1,575.00	\$ 17,500.00
01/04/2019	Site-Preparation-MAT	White Cement	White Cement		100.00	Unit(s)	35.00	50.00	45.00	675.00	40.00	800.00	\$ 3,500.00
01/08/2019	Site-Preparation-MAT	Door	Door		25.00	Unit(s)	2,000.00	0.00	1.00	2,500.00	25.00	50,000.00	\$ 50,000.00



Estimation for Jobs - Material / Labour / Overheads

- ❖ All jobs require different job estimation amounts of material, labor, and overhead. Therefore, each job has a unique total cost. Materials, Labours and Oveheads are easy to assign jobs.

Sales Orders To Invoice Products Reporting Configuration

Job Estimates / Quotations
Edit Create
Orders
Sales Teams
Customers
Job Estimates
Contracts

Print Action

Draft Estimate Sent Confirmed Approved Quotation Created

1 / 1 < >

JOB/EST/0001

Customer: Azure Interior
Address: 3404 Edgewood Road
City: Jonesboro AR 72401
Country: United States

Date: 01/03/2019
Company: YourCompany
Currency: USD

Pricelist: Public Pricelist (USD)
Payment Terms: End of Following Month

Project: Construction of Hypol Heights
Analytic Account: Hypol Heights - The Jackson Group
Job Types: Hypol Heights - Material, Hypol Heights - Labour, Hypol Heights

Material Estimation Labour Estimation Overhead Estimation Other Info Additional Notes

Type	Product	Description	Quantity	Unit of Measure	Unit Price	Discount (%)	Subtotal
Material	Cement	Cement	25.000	Unit(s)	350.00	0.00	8,750.00
Material	Bricks	Bricks	2,000.000	Unit(s)	10.00	0.00	20,000.00
Material	Iron	Iron	500.000	kg	45.00	0.00	22,500.00
Material	White Cement	White Cement	50.000	Unit(s)	10.00	0.00	500.00

Description of Jobs Estimate

Total Material Estimate: \$ 51,750.00
Total Labour Estimate: \$ 840.00
Total Overhead Estimate: \$ 1,150.00
Total Job Estimate: \$ 53,740.00



- ❖ Sales Quotation from the Job Estimation. Created Sales Quotation based on Job Estimation.

Sales Orders To Invoice Products Reporting Configuration

Job Estimates / JOB/EST/0001 / SO020

Edit Create Print Action

Send by Email Send PRO-FORMA Invoice Print Confirm Preview Cancel

Quotation Quotation Sent Sales Order

SO020

Customer	Azure Interior 3404 Edgewood Road Jonesboro AR 72401 United States	Validity Pricelist	Public Pricelist (USD)
Invoice Address	Azure Interior	Payment Terms	
Delivery Address	Azure Interior	Recurring Period	0
Quotation Template			

Order Lines	Optional Products	Other Information							
Product	Description	Ordered Qty Unit of Measure	Analytic Tags	Route	Unit Price	Taxes	Discount (%)	Subtotal	Total
Cement	Cement	25.000 Unit(s)			350.00	(Tax 15.00%)	0.00	\$ 8,750.00	\$ 10,062.50
Bricks	Bricks	2,000.000 Unit(s)			10.00	(Tax 15.00%)	0.00	\$ 20,000.00	\$ 23,000.00
Iron	Iron	500.000 kg			45.00	(Tax 15.00%)	0.00	\$ 22,500.00	\$ 25,875.00
White Cement	White Cement	50.000 Unit(s)			10.00	(Tax 15.00%)	0.00	\$ 500.00	\$ 575.00
Ground Floor Wages	Ground Floor Wages	7.000 Unit(s)			120.00	(Tax 15.00%)	0.00	\$ 840.00	\$ 966.00
Electricity Bill	Electricity Bill	1.000 Unit(s)			1,000.00	(Tax 15.00%)	0.00	\$ 1,000.00	\$ 1,150.00
Truck Rent	Truck Rent	1.000 Unit(s)			150.00	(Tax 15.00%)	0.00	\$ 150.00	\$ 172.50

Untaxed Amount: \$ 53,740.00
Taxes: \$ 8,061.00

Probuse Consulting Service PVT Ltd.



Sales Estimate Create from Job Cost Sheet

- ❖ Allow you to create Job Estimates from Job Cost Sheets. It is easy to calculate the total cost of direct materials based on the materials used in the job. Companies use job cost sheets to record the cost of materials use, labour charges and overhead expenses.

Jobs Job Costs Project Issues Projects Job Orders Sub Contractors Waste Reporting Materials / BOQ Change Orders Analytic Account Invoicing + Mitchell Admin (apps12_jobcosting_bundle)

Job Cost Sheets / COST-SHEET/00002

Edit Create Print Action

Confirm Create Estimation Cancel Draft Confirmed Done

COST-SHEET/00002																						
<table border="1"> <tr> <td><input type="button" value="Purchase Order"/></td> <td>0</td> <td><input type="button" value="HR Timesheet"/></td> <td>0</td> <td><input type="button" value="Vendor Invoicing"/></td> <td>0</td> </tr> <tr> <td><input type="button" value="Issues"/></td> <td></td> <td><input type="button" value="Job Estimations"/></td> <td>0</td> <td><input type="button" value="Requisitions"/></td> <td>0</td> </tr> </table>											<input type="button" value="Purchase Order"/>	0	<input type="button" value="HR Timesheet"/>	0	<input type="button" value="Vendor Invoicing"/>	0	<input type="button" value="Issues"/>		<input type="button" value="Job Estimations"/>	0	<input type="button" value="Requisitions"/>	0
<input type="button" value="Purchase Order"/>	0	<input type="button" value="HR Timesheet"/>	0	<input type="button" value="Vendor Invoicing"/>	0																	
<input type="button" value="Issues"/>		<input type="button" value="Job Estimations"/>	0	<input type="button" value="Requisitions"/>	0																	
Name	New	Create Date	01/03/2019																			
Project	Construction of Hypol Heights	Closed Date																				
Analytic Account	Hypol Heights - The Jackson Group	Created By	Mitchell Admin																			
Job Order	Flooring Works	Company	YourCompany																			
Customer	Azure Interior	Currency	USD																			
Description	Sale Reference																					
Materials	Labours	Overhead																				
Date	Job Type	Product	Description	Reference	Planned Qty	Uom	Cost / Unit	Actual Requisition Quantity	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Cost Price Sub Total									
01/03/2019	Bricks	Bricks			50.00	Unit(s)	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00									
01/03/2019	Cement	Cement			20.00	Unit(s)	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00									
01/03/2019	Tiles	Tiles			30.00	Unit(s)	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00									
01/03/2019	Iron	Iron			40.00	kg	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00									
01/03/2019	White Cement	White Cement			50.00	kg	0.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00									
					190.00		0.00	0.00	0.00	0.00	0.00	0.00										



- ❖ A Created Job Estimation contain Material, Overhead and Labour on Job Costsheet.

Screenshot of Odoo Job Cost Sheet interface for Job/EST/0003:

Job Cost Sheets / COST-SHEET/00002 / Job Estimates / JOB/EST/0003

JOB/EST/0003

Customer	Azure Interior 3404 Edgewood Road Jonesboro AR 72401 United States	Date	01/03/2019
Pricelist	Public Pricelist (USD)	Company	YourCompany
Payment Terms		Currency	USD
Customer Reference		Project	Construction of Hypol Heights
		Analytic Account	Hypol Heights - The Jackson Group
		Job Types	(Hypol Heights - Material) (Hypol Heights - Labour) (Hypol Heights)

Material Estimation

Type	Product	Description	Quantity	Unit of Measure	Unit Price	Discount (%)	Subtotal
Material	Bricks	Bricks	50.000	Unit(s)	0.00	0.00	0.00
Material	Cement	Cement	20.000	Unit(s)	0.00	0.00	0.00
Material	Tiles	Tiles	30.000	Unit(s)	0.00	0.00	0.00
Material	Iron	Iron	40.000	kg	0.00	0.00	0.00
Material	White Cement	White Cement	50.000	kg	0.00	0.00	0.00

Description of Jobs Estimate

Total Material Estimate: \$ 0.00
Total Labour Estimate: \$ 0.00
Total Overhead Estimate: \$ 0.00



Progress Billing to Customer

❖ **Analytic Account / Project:** Set the Total Progress Billing Amount on the Analytic Account / Project. Total project cost is defined as all costs specific to a project incurred through startup.

Jobs Dashboard Job Costs Project Issues Inspections Projects Request for Information Job Orders Sub Contractors + Mitchell Admin (apps12_jobcosting_bundle)

Analytic Accounts / Hypol Heights - The Jackson Group Edit Create Print Action 14 / 29

Generate Invoice Lock

Hypol Heights		\$ Cost/Revenue	1 Projects	Active																																				
Reference Customer	The Jackson Group	Currency	0 Invoices																																					
Total Progress Billing	\$ 55,000,000.00	Order/Invoice																																						
Recurring Period	0	Currency																																						
Contracts Expiration Reminder(Days)	10	Start Date																																						
Date of Next Invoice	01/29/2019	End Date																																						
		Stage																																						
Budget Items		Projects																																						
<table border="1"> <thead> <tr> <th>Budget</th> <th>Budgetary Position</th> <th>Start Date</th> <th>End Date</th> <th>Paid Date</th> <th>Planned Amount</th> <th>Practical Amount</th> <th>Theoretical Amount</th> <th>Achievement</th> </tr> </thead> <tbody> <tr> <td>Construction of Hypol Heights</td> <td>Cost & Expense</td> <td>01/01/2019</td> <td>12/31/2020</td> <td></td> <td>100,000.00</td> <td>-6,100.00</td> <td>1,025.23</td> <td>-594.99</td> </tr> <tr> <td>Construction of Hypol Heights</td> <td>Cost & Expense</td> <td>01/01/2019</td> <td>01/09/2019</td> <td></td> <td>800.00</td> <td>-4,500.00</td> <td>748.42</td> <td>-601.27</td> </tr> <tr> <td>Construction of Hypol Heights</td> <td>Cost & Expense</td> <td>01/01/2019</td> <td>01/09/2019</td> <td></td> <td>200.00</td> <td>-4,500.00</td> <td>187.10</td> <td>-2,405.07</td> </tr> </tbody> </table>		Budget	Budgetary Position	Start Date	End Date	Paid Date	Planned Amount	Practical Amount	Theoretical Amount	Achievement	Construction of Hypol Heights	Cost & Expense	01/01/2019	12/31/2020		100,000.00	-6,100.00	1,025.23	-594.99	Construction of Hypol Heights	Cost & Expense	01/01/2019	01/09/2019		800.00	-4,500.00	748.42	-601.27	Construction of Hypol Heights	Cost & Expense	01/01/2019	01/09/2019		200.00	-4,500.00	187.10	-2,405.07	YourCompany		
Budget	Budgetary Position	Start Date	End Date	Paid Date	Planned Amount	Practical Amount	Theoretical Amount	Achievement																																
Construction of Hypol Heights	Cost & Expense	01/01/2019	12/31/2020		100,000.00	-6,100.00	1,025.23	-594.99																																
Construction of Hypol Heights	Cost & Expense	01/01/2019	01/09/2019		800.00	-4,500.00	748.42	-601.27																																
Construction of Hypol Heights	Cost & Expense	01/01/2019	01/09/2019		200.00	-4,500.00	187.10	-2,405.07																																



❖ **Customer Invoice with Progress Billing :** Define the Progress Billing Title on Invoice and display the Progress Billing Amounts.

Screenshot of the Odoo application interface showing an invoice for Job Cost Sheets / COST-SHEET/00001 / Invoices / INV/2019/0001.

The invoice details are as follows:

Customer	Lumber Inc 3202 Hannah Street Asheville NC 28801 United States	Invoice Date	01/03/2019
Delivery Address	Andrew Smith	Due Date	02/02/2019
Payment Terms	30 Net Days	Salesperson	Mitchell Admin
Progress Billing Title	Residential Construction	Job Cost Sheet	COST-SHEET/00001
Project	Hypol Heights - The Jackson Group	Sales Team	Europe
Cash Rounding Method		Currency	USD

The invoice lines show two items:

Product	Description	Account	Analytic Account	Analytic Tags	Quantity	Unit of Measure	Price	Disc (%)	Taxes	Subtotal	Total
Cement	Cement	200000 Product Sales			40.000	Unit(s)	350.00	0.00	<u>Tax 15.00%</u>	\$ 14,000.00	\$ 16,100.00
Bricks	Bricks	200000 Product Sales			30.000	Unit(s)	35.00	0.00	<u>Tax 15.00%</u>	\$ 1,050.00	\$ 1,207.50



Jobs Dashboard Job Costs Project Issues Inspections Projects Request for Information Job Orders Sub Contractors + Mitchell Admin (apps12_jobcosting_bundle)

Job Cost Sheets / COST-SHEET/00001 / Invoices / INV/2019/0001

Edit Create Print Action

Costs							
	Iron	Iron	200000 Product Sales	45.000 kg	45.00	0.00	Tax 15.00% \$ 2,025.00 \$ 2,328.75
	White Cement	White Cement	200000 Product Sales	40.000 Unit(s)	1.00	0.00	Tax 15.00% \$ 40.00 \$ 46.00
	Door	Door	200000 Product Sales	25.000 Unit(s)	2,500.00	0.00	Tax 15.00% \$ 62,500.00 \$ 71,875.00
	Ground Floor Wages	Ground Floor Wages	200000 Product Sales	26.000 Unit(s)	120.00	0.00	Tax 15.00% \$ 3,120.00 \$ 3,588.00
	Tiles Feeting	Tiles Feeting	200000 Product Sales	24.000 Unit(s)	100.00	0.00	Tax 15.00% \$ 2,400.00 \$ 2,760.00
	Waterproofing	Waterproofing	200000 Product Sales	8.000 Unit(s)	120.00	0.00	Tax 15.00% \$ 960.00 \$ 1,104.00
	Electricity Bill	Electricity Bill	200000 Product Sales	1.000 Unit(s)	500.00	0.00	Tax 15.00% \$ 500.00 \$ 575.00
	[EXP_CT] Car Travel Expenses	[EXP_CT] Car Travel Expenses	200000 Product Sales	1.000 km	400.00	0.00	Tax 15.00% \$ 400.00 \$ 460.00
	Truck Rent	Truck Rent	200000 Product Sales	1.000 Unit(s)	150.00	0.00	Tax 15.00% \$ 150.00 \$ 172.50
	Wiring Works	Wiring Works	200000 Product Sales	1.000 Unit(s)	30.00	0.00	Tax 15.00% \$ 30.00 \$ 34.50
							Untaxed Amount: \$ 97,175.00
							Tax: \$ 14,576.25

Job Cost Sheets / COST-SHEET/00001 / Invoices / INV/2019/0001

Edit Create Print Action

Total:		\$ 111,751.25
Amount Due:		\$ 111,751.25

Progress Billing Information

Total Progress Billing	\$ 55,000,000.00	Previously Invoiced	\$ 0.00
Invoice To Date	\$ 0.00	Previously Invoiced Due	\$ 0.00
Remaining Progress Billing	\$ 55,000,000.00	Current Invoiced	\$ 111,751.25
		Less Paid Amount	\$ 111,751.25
		Total Due Now	\$ 111,751.25

Send message Log note Schedule activity Following Today 2

YourCompany, Mitchell Admin - 2 minutes ago
Invoice validated
Status: Draft → Open



Customer Invoice from Job Cost Sheet

- ❖ Allow you to create customer invoice from Job Costsheet based on actual qty on vendor bill. Job costing involves the accumulation of the costs of materials, labor and overhead for a specific job. Create Invoice based on Customer Invoice Billable Method is Based on Actual Purchase Qty, Actual Vendor Bill Qty, Based Manual Invoice.

Screenshot of the Odoo application interface showing the creation of a Customer Invoice from a Job Cost Sheet.

The main window displays a Job Cost Sheet for "COST-SHEET/0000". The "Create Customer Invoice" wizard is open, showing the following details:

- Customer:** Lumber Inc
- Invoice Date:** 01/03/2019
- Include Material Lines:** Checked
- Include Labour Lines:** Checked
- Include Overhead Lines:** Checked

The wizard notes: "This wizard will create customer invoice for selected customer."

At the bottom of the wizard are "Create Invoice" and "Cancel" buttons.

The main interface shows a table of cost sheet data:

Date	Job Type	Product	Description	Reference	Planned Qty	Uom	Cost / Unit	Sale Price / Unit	Actual Requisition Quantity	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Actual Cost Price Sub Total	Manual Invoiced Qty	Cus Im
01/01/2019	Site-Preparation-MAT	Cement	Cement		50.00	Unit(s)	350.00	400.00	50.00	200.00	70,000.00	40.00	800.00	\$ 17,500.00	0.00	
01/02/2019	Site-Preparation-MAT	Bricks	Bricks		2,000.00	Unit(s)	10.00	15.00	2,000.00	20,000.00	30.00	900.00	\$ 20,000.00	0.00		



❖ Created Invoice on Job Costsheets With Material, Labour and Overhead.

Screenshot of Odoo Job Costing module showing a draft invoice for a job cost sheet.

Header:

- Jobs, Job Costs, Project Issues, Projects, Job Orders, Sub Contractors, Waste Reporting, Materials / BOQ, Change Orders, Analytic Account, Invoicing, +
- Mitchell Admin (apps12_jobcosting_bundle)
- Job Cost Sheets / COST-SHEET/00001 / Invoices / Invoice
- Edit, Create, Print, Action, 1 / 1, Draft, Open, Paid
- Validate, Preview

Draft Invoice Details:

Customer	Lumber Inc 3202 Hannah Street Asheville NC 28801 United States	Invoice Date	01/03/2019
Delivery Address		Due Date	
Payment Terms		Salesperson	Mitchell Admin
Progress Billing Title		Job Cost Sheet	COST-SHEET/00001
Project		Sales Team	Europe
Cash Rounding Method		Currency	USD

Invoice Lines:

Product	Description	Account	Analytic Account	Analytic Tags	Quantity	Unit of Measure	Price	Disc (%)	Taxes	Subtotal	Total
Cement	Cement	200000 Product Sales			40.000	Unit(s)	0.00	0.00	\$ 0.00	\$ 0.00	
Bricks	Bricks	200000 Product Sales			30.000	Unit(s)	0.00	0.00	\$ 0.00	\$ 0.00	
Tiles	Tiles	200000 Product Sales			200.000	Unit(s)	0.00	0.00	\$ 0.00	\$ 0.00	
Iron	Iron	200000 Product Sales			45.000	kg	0.00	0.00	\$ 0.00	\$ 0.00	
White Cement	White Cement	200000 Product Sales			40.000	Unit(s)	0.00	0.00	\$ 0.00	\$ 0.00	
Door	Door	200000 Product Sales			25.000	Unit(s)	0.00	0.00	\$ 0.00	\$ 0.00	
Ground Floor Wages	Ground Floor Wages	200000 Product Sales			25.000	Unit(s)	0.00	0.00	\$ 0.00	\$ 0.00	
Tiles Feeding	Tiles Feeding	200000 Product Sales			24.000	Unit(s)	0.00	0.00	\$ 0.00	\$ 0.00	
Waterproofing	Waterproofing	200000 Product Sales			8.000	Unit(s)	0.00	0.00	\$ 0.00	\$ 0.00	
Electricity Bill	Electricity Bill	200000 Product Sales			1.000	Unit(s)	0.00	0.00	\$ 0.00	\$ 0.00	



❖ Set Customer Invoice Qty on Job Costsheet .

Job Cost Sheets / COST-SHEET/00001

Edit Create Print Action 1 / 2

Description Sale Reference Customer Invoice Billable Method													Based On Actual Vendor Bill Qty			
Materials			Labours			Overhead										
Type	Product	Description	Reference	Planned Qty	Uom	Cost / Unit	Sale Price / Unit	Actual Requisition Quantity	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Customer Cost Price Sub Total	Manual Invoiced Qty	Customer Invoiced Qty	Is Billable
Cement	Cement			50.00	Unit(s)	350.00	400.00	50.00	200.00	70,000.00	40.00	800.00	\$ 17,500.00	0.00	40.00	Billable
Bricks	Bricks			2,000.00	Unit(s)	10.00	15.00	2,000.00	2,000.00	20,000.00	30.00	900.00	\$ 20,000.00	0.00	30.00	Billable
Tiles	Tiles			500.00	Unit(s)	40.00	45.00	500.00	570.00	25,400.00	200.00	12,000.00	\$ 20,000.00	0.00	200.00	Billable
Iron	Iron			500.00	kg	35.00	40.00	500.00	500.00	100,000.00	45.00	1,575.00	\$ 17,500.00	0.00	45.00	Billable
White Cement	White Cement			100.00	Unit(s)	35.00	40.00	50.00	45.00	675.00	40.00	800.00	\$ 3,500.00	0.00	40.00	Billable
Door	Door			25.00	Unit(s)	2,000.00	2,500.00	0.00	1.00	2,500.00	25.00	50,000.00	\$ 50,000.00	0.00	25.00	Billable
				3,175.00		2,470.00	3,040.00	3,100.00	3,316.00		380.00		128,500.00	0.00	380.00	



Website Job/Work Order Form and Portal

- ❖ Allow your customer/visitor to create request for job order or task from your website. You can create an entirely new job order, or you can create a task.

The screenshot shows a web-based job order form. At the top, there's a navigation bar with 'WEBSITE', 'Pages', 'Customize', 'Promote', 'My Website', 'New', and 'Edit'. The main form area has fields for 'Your Name' (containing 'Mitchell Admin'), 'Your Email' (containing 'admin@yourcompany.example.com'), 'Your Phone' (containing '+1 555-555-5555'), 'Subject' (containing 'Flooring works'), 'Project Code' (containing 'FW:WORK'), and 'Description' (with a note about floor covering). Below these are dropdowns for 'Priority' (set to 'Normal') and 'Job Order Category' (set to 'New Request'). There's also an 'Attach Files' section with a 'Choose File' button. At the bottom are 'Submit' and 'Cancel' buttons. The footer contains sections for 'Our Products & Services' (with a 'Home' link), 'Connect with us' (listing 'Contact us', phone number '+1 555 123 8009', email 'info@yourcompany.example.com', and social media links for Facebook, Twitter, LinkedIn, YouTube, and Instagram), and 'Your Company' (with a 'About us' link, a mission statement, and a note about products being designed for small to medium size companies).



❖ Created Job Order on Website Portal.

Project Projects All Tasks Project Phases Reporting Configuration

Print Action 8 / 24

JOB/0005

☆ Flooring works

Project	Andrew Smith	Deadline	Sub-tasks	0	Jobs
Project Phase		Tags	Stock Moves	0	Subcontractor
Assigned to		Website Customer	Notes		Jobs
Starting Date	01/03/2019 19:13:36	Name	Purchase Re...		
Ending Date		Email			
Job Number	JOB/0007	Website Customer			
		Phone			
		Job Order Category	New Request		
Description Waste Materials Material Plannings Website Purchase Requirements Subtasks Consumed Materials Material Requisitions Extra Info					
Timesheet Employee Users					
Website Customer	YourCompany, Mitchell Admin	Website Customer	0	Notes	Subcontractor
Name	Mitchell Admin	Name	0	Jobs	Jobs
Email	admin@yourcompany.example.com	Email			
Website Customer	+1 555-555-5555	Phone			
Phone		Job Order Category	New Request		
Job Order Category		Is Job Order	<input type="checkbox"/>		



❖ Job Order / Task List - Portal My Account



Change Order in Job Contracting and Construction

- ❖ Allow you to manage Change Order in Job Contracting and Construction Business. We can change the order material. A change order is a document used to record an amendment to your original construction contract.

Jobs Job Costs Project Issues Projects Job Orders Sub Contractors Waste Reporting Materials / BOQ Change Orders Analytic Account Invoicing Reports Costing Reports Configuration G3 Mitchell Admin

Change Orders / CO00001 Change Orders

Edit Create Print Action

1 / 1 < >

Create Quotation Draft Confirmed Approved Customer Approved Done

CO00001		Contracts		Sale Orders			
Customer	YourCompany, Mitchell Admin	Create Date	01/04/2019 10:25:29				
Guarantor One	Andrew Smith	Company	YourCompany				
Guarantor Two	Azure Interior	Currency	USD				
Project	Construction of Hypol Heights	Responsible User	Mitchell Admin				
Contract/Analytic Account	Hypol Heights - The Jackson Group	Pricelist	Public Pricelist (USD)				
Job Order	Flooring Works						
Original Job Completion Date	01/04/2019	New Estimation Completion Date	01/04/2019				
Change Order Lines		Additional Information					
Product	Description	Quantity	Unit of Measure	Sale Price	Taxes	Subtotal	Total
Tiles	Tiles	200.000	Unit(s)	\$ 50.00	(Tax 15.00%)	10,000.00	\$ 11,500.00
White Cement	White Cement	50.000	Unit(s)	\$ 10.00	(Tax 15.00%)	500.00	\$ 575.00
Cement	Cement	50.000	Unit(s)	\$ 350.00	(Tax 15.00%)	17,500.00	\$ 20,125.00
Bricks	Bricks	1,000.000	Unit(s)	\$ 35.00	(Tax 15.00%)	35,000.00	\$ 40,250.00
						Untaxed Amount:	\$ 63,000.00
						Taxes:	\$ 9,450.00



❖ **Sale order Created from Change Order:** Sales Quotation is a document created based on change order offering to sell goods or services at a certain price under specified conditions.

Jobs Job Costs Project Issues Projects Job Orders Sub Contractors Waste Reporting Materials / BOQ Change Orders Analytic Account Invoicing Reports Costing Reports Configuration Mitchell Admin

Change Orders / CO00001 / Sales Orders / SO021

Edit Create Print Action ▾

Send by Email Send PRO-FORMA Invoice Print Confirm Preview Cancel Quotation Quotation Sent Sales Order

SO021

Customer	YourCompany, Mitchell Admin 215 Vine St Scranton PA 18503 United States	Validity	Public Pricelist (USD)
Invoice Address	YourCompany, Mitchell Admin	Pricelist	
Delivery Address	YourCompany, Mitchell Admin	Payment Terms	
Quotation Template		Recurring Period	0

Order Lines	Optional Products	Other Information								
Product	Description	Ordered Qty	Unit of Measure	Analytic Tags	Route	Unit Price	Taxes	Discount (%)	Subtotal	Total
Tiles	Tiles	200.000	Unit(s)			50.00	(Tax 15.00%)	0.00	\$ 10,000.00	\$ 11,500.00
White Cement	White Cement	50.000	Unit(s)			10.00	(Tax 15.00%)	0.00	\$ 500.00	\$ 575.00
Cement	Cement	50.000	Unit(s)			350.00	(Tax 15.00%)	0.00	\$ 17,500.00	\$ 20,125.00
Bricks	Bricks	1,000.000	Unit(s)			35.00	(Tax 15.00%)	0.00	\$ 35,000.00	\$ 40,250.00

Untaxed Amount: \$ 63,000.00
Taxes: \$ 9,450.00
Total: \$ 72,450.00



Budget for Job Contracting and Construction Projects

- ❖ Create Budget for multiple job Costsheets and job cost lines.

Job Costing is one of the best ways to develop an accurate budget for any project. Define the budget for material , overhead and labour expenses for that project.

Invoicing Overview Customers Vendors Accounting Reporting Configuration

Mitchell Admin (apps12_jobcosting_bundle)

Budgets / Construction of Hypol Heights

Edit Create Action ▾ 1 / 1 < >

Construction of Hypol Heights															
Responsible		Mitchell Admin		Period		01/01/2019 - 01/09/2019									
				Company		YourCompany									
				Currency		USD									
Budget Lines															
Budgetary Position	Analytic Account	Cost Type	Job Type	Cost Sheet	Job Cost Line	Product	Uom	Description	Reference	Start Date	End Date	Paid Date	Planned Amount	Practical Amount	Theoretical Amount
Cost & Expense	Hypol Heights - The Jackson Group	Material	Site-Preparation-MAT	COST-SHEET/00001	White	White	Unit(s)	White Cement		01/01/2019	12/31/2020		\$ 100,000.00	\$ -6,100.00	\$ 995.18
Cost & Expense	Hypol Heights - The Jackson Group	Labour	Site-Preparation-LAB	COST-SHEET/00001	Ground Floor Wages	Ground Floor Wages		Ground Floor Wages		01/01/2019	01/09/2019		\$ 800.00	\$ -4,500.00	\$ 726.48
Cost & Expense	Hypol Heights - The Jackson Group	Overhead	Site-Preparation-OHD	COST-SHEET/00001	Electricity Bill	Electricity Bill	Unit(s)	Electricity Bill		01/01/2019	01/09/2019		\$ 200.00	\$ -4,500.00	\$ 181.62
101,000.00 -15,100.00 1,903.27															



❖ **Job Costsheets:** Budget lines by Job, Job Cost line which will show you Planned Amounts of Material, Labour and Overheads.

COST-SHEET/00001

Name	New	Create Date	01/01/2019													
Project	Construction of Hypol Heights	Closed Date														
Project Team	Construction of Hypol Heights	Created By	Mitchell Admin													
Tags	(Flooring works) (Painting Works) (Color Estimation)	Company	YourCompany													
Analytic Account	Hypol Heights - The Jackson Group	Currency	USD													
Job Order	Project Initiation	Description														
Customer	Lumber Inc	Sale Reference														
		Customer Invoice	Based On Actual Vendor Bill Qty													
		Billable Method														
<input type="button" value="Materials"/> <input type="button" value="Labours"/> <input type="button" value="Overhead"/>																
Date	Job Type	Product	Description	Reference	Planned Qty	Uom	Cost / Unit	Sale Price / Unit	Actual Requisition Quantity	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Actual Cost Price Sub Total	Manual Inv Qty	Cust Inv Qty



Jobs Dashboard Job Costs Project Issues Inspections Projects Request for Information Job Orders Sub Contractors + C E M S Mitchell Admin (apps12_jobcosting_bundle)

Job Cost Sheets / COST-SHEET/00001

Edit Create Print Action 1 / 4

Materials Labours Overhead																
Date	Job Type	Product	Description	Reference	Planned Qty	Uom	Cost / Unit	Sale Price / Unit	Actual Requisition Quantity	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Cost Price Sub Total	Manual Invoiced Qty	Cust Inv
01/01/2019	Site-Preparation-MAT	Cement	Cement		50.00	Unit(s)	350.00	400.00	50.00	200.00	70,000.00	40.00	800.00	\$ 17,500.00	0.00	
01/02/2019	Site-Preparation-MAT	Bricks	Bricks		2,000.00	Unit(s)	10.00	15.00	2,000.00	2,000.00	20,000.00	30.00	900.00	\$ 20,000.00	0.00	
01/03/2019	Site-Preparation-MAT	Tiles	Tiles		500.00	Unit(s)	40.00	45.00	500.00	570.00	25,400.00	200.00	12,000.00	\$ 20,000.00	0.00	
01/04/2019	Site-Preparation-MAT	Iron	Iron		500.00	kg	35.00	40.00	500.00	500.00	100,000.00	45.00	1,575.00	\$ 17,500.00	0.00	
01/04/2019	Site-Preparation-MAT	White Cement	White Cement		100.00	Unit(s)	35.00	40.00	50.00	45.00	675.00	40.00	800.00	\$ 3,500.00	0.00	
01/08/2019	Site-Preparation-MAT	Door	Door		25.00	Unit(s)	2,000.00	2,500.00	0.00	1.00	2,500.00	25.00	50,000.00	\$ 50,000.00	0.00	
					3,175.00		2,470.00	3,040.00	3,100.00	3,316.00		380.00		128,500.00	0.00	3

Jobs Dashboard Job Costs Project Issues Inspections Projects Request for Information Job Orders Sub Contractors + C E M S Mitchell Admin (apps12_jobcosting_bundle)

Job Cost Sheets / COST-SHEET/00001

Edit Create Print Action 1 / 4

Materials Labours Overhead														
Date	Job Type	Product	Description	Reference	Hours	Cost / Unit	Actual Requisition Quantity	Actual Timesheet Hours	Actual Timesheet Cost	Cost Price Sub Total	Manual Invoiced Hour	Invoiced Is Hour	Billable	
01/09/2019	Site-Preparation-LAB	Ground Floor Wages	Ground Floor Wages		08:00	100.00		0.00	28:00	500.00	\$ 800.00	00:00	26:00	Billable
01/16/2019	Site-Preparation-LAB	Tiles Feeting	Tiles Feeting		08:00	120.00		0.00	08:00	0.00	\$ 960.00	00:00	24:00	Billable
01/18/2019	Site-Preparation-LAB	Waterproofing	Waterproofing		08:00	100.00		0.00	08:00	0.00	\$ 800.00	00:00	08:00	Billable
01/17/2019	Site-Preparation-LAB	Italian Marble Fixing	Italian Marble Fixing		08:00	25.00		0.00	00:00	0.00	\$ 200.00	00:00	00:00	Billable
					32:00	345.00		0.00	44:00		2,760.00	00:00	58:00	
Job Cost Details														
Total Material Cost: \$ 128,500.00														
Total Labour Cost: \$ 2,760.00														
Total Overhead Cost: \$ 640.00														
Total Cost: \$ 131,900.00														



Jobs Dashboard Job Costs Project Issues Inspections Projects Request for Information Job Orders Sub Contractors + C P E S Mitchell Admin (apps12_jobcosting_bundle)

Job Cost Sheets / COST-SHEET/00001

Overhead																
Date	Job Type	Product	Description	Reference	Basis	Planned Qty	Cost / Unit	Sale Price / Unit	Actual Requisition Quantity	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Cost Price Sub Total	Manual Inv Qty	Cust Inv Qty
01/08/2019	Site-Preparation- OHD	Electricity Bill	Electricity Bill			1.00	Unit(s)	200.00	0.00	0.00	1.00	2,500.00	1.00	2,500.00	\$ 200.00	0.00
01/29/2019	Site-Preparation- OHD	[EXP_CT] Car Travel Expenses	Car Travel Expenses			1.00	km	300.00	0.00	0.00	1.00	500.00	1.00	500.00	\$ 300.00	0.00
01/24/2019	Site-Preparation- OHD	Truck Rent	Truck Rent			1.00	Unit(s)	120.00	0.00	0.00	1.00	1,000.00	1.00	1,000.00	\$ 120.00	0.00
01/23/2019	Site-Preparation- OHD	Wiring Works	Wiring Works			1.00	Unit(s)	20.00	0.00	0.00	1.00	500.00	1.00	500.00	\$ 20.00	0.00
						4.00		640.00	0.00	0.00	4.00		4.00	640.00	0.00	

Job Cost Details

Total Material Cost: \$ 128,500.00
 Total Labour Cost: \$ 2,760.00
 Total Overhead Cost: \$ 640.00



❖ Job Costsheet Budget Analysis Report.

Screenshot of the Probuse software interface showing the 'Jobs' module. The top navigation bar includes links for Dashboard, Job Costs, Project Issues, Inspections, Projects, Request for Information, Job Orders, Sub Contractors, and a '+' button. A user profile for 'Mitchell Admin (apps12_jobcosting_bundle)' is visible.

The main content area displays a 'Budget Analysis' report. It shows a table with columns: Actual Purchase Quantity, Actual Vendor Quantity, Actual Cost unit, Material Planned Qty, and Overhead Planned. The table includes rows for 'Total', 'Hypol Heights - The Jackson Group', and a specific 'COST-SHEET/00001'. The total values are 1.00, 1.00, 26.00, 2.00, and 2 respectively.

A context menu is open over the table, listing options such as Request for Information, Budget Report, Budget Analysis, Configuration, Stages, Job Types, Project Issues, Issue Teams, Type of Issue Subject, Issue Types, Issue Stages, RFI Configuration, RFI Subject, RFI Types, RFI Teams, RFI Stages, Transmittal / Submittal Types, Mediums, Instructions, Quality Checklists, Inspection Values, Inspection Results, and Inspection Types.



Equipment and Maintenance Request for Job Work Order

- ❖ Allow you to create and manage equipment related to your job order or task. Allow you to create and manage Maintenance Request related to your job order or task.

Job Orders / CNC Machine

Edit Create Print Action Purchase Re... 10 / 10

Project	CNC Machine	Deadline	01/31/2019																								
Project Phase		Tags	NeedAssistance																								
Assigned to	Mitchell Admin	Website Customer																									
Starting Date	01/04/2019 10:47:33	Website Customer Name																									
Ending Date	02/28/2019 10:47:34	Website Customer Email																									
Job Number	JOB/00008	Website Customer Phone																									
		Job Order Category																									
Description Waste Materials Material Planning Website Purchase Requisitions Subtasks Consumed Materials Material Requisitions Timesheets Extra Info Timesheet Employee Users Maintenance Equipment Maintenance Requests																											
Create Maintenance Equipment <table border="1"> <thead> <tr> <th>Equipment Name</th> <th>Employee</th> <th>Department</th> <th>Serial Number</th> <th>Technician</th> <th>Equipment Category</th> </tr> </thead> <tbody> <tr> <td>CNC Mills</td> <td></td> <td></td> <td>0233</td> <td></td> <td>Machine</td> </tr> <tr> <td>Lathes - Grece</td> <td>Abigail Peterson</td> <td></td> <td>6006</td> <td>Andrew Smith</td> <td>Machine</td> </tr> <tr> <td>Water Jet Cutters</td> <td>Audrey Peterson</td> <td></td> <td>9005</td> <td></td> <td>Machine</td> </tr> </tbody> </table>				Equipment Name	Employee	Department	Serial Number	Technician	Equipment Category	CNC Mills			0233		Machine	Lathes - Grece	Abigail Peterson		6006	Andrew Smith	Machine	Water Jet Cutters	Audrey Peterson		9005		Machine
Equipment Name	Employee	Department	Serial Number	Technician	Equipment Category																						
CNC Mills			0233		Machine																						
Lathes - Grece	Abigail Peterson		6006	Andrew Smith	Machine																						
Water Jet Cutters	Audrey Peterson		9005		Machine																						

Send message Log note Schedule activity

Following 2



❖ Create Maintenance Request from job order or task.

Jobs Job Costs Project Issues Projects Job Orders Sub Contractors Waste Reporting Maintenance Materials / BOQ Change Orders Analytic Account Invoicing Reports + C 2 Mitchell Admin

Job Orders / CNC Machine Edit Create Print Action 10 / 10 Purchase Re... < >

Project	CNC Machine	Deadline	01/31/2019					
Project Phase		Tags	NeedAssistance					
Assigned to	Mitchell Admin							
Starting Date	01/04/2019 10:47:33							
Ending Date	02/28/2019 10:47:34							
Job Number	JOB/00008							
		Website Customer						
		Name						
		Email						
		Website Customer						
		Phone						
		Job Order Category						
Description	Waste Materials	Material Plannings	Website	Purchase Requisitions	Subtasks	Consumed Materials	Material Requisitions	Timesheets
Extra Info	Timesheet Employee Users	Maintenance Equipment		Maintenance Requests				
Create Maintenance Request								
Subjects	Employee	Technician	Category	Stage				
Cutter Sharpness			Machine	New Request				
CNC Mill Sharpening			Machine	New Request				
Send message Log note Schedule activity ✓ Following - 2								



Instruction and Quality Checklist on Job Order

- ❖ Project Manager / Job Manager to set list of instructions to any job order. Define Instructions and quality checklists for job order / task.

Job Orders / CNC Machine

Edit Create Print Action 1 / 1 < >

JOB/0006		CNC Machine																										
Project	CNC Machine	Deadline	01/31/2019																									
Project Phase		Tags	NeedAssistance																									
Assigned to	Mitchell Admin	Website Customer																										
Starting Date	01/04/2019 10:47:33	Name																										
Ending Date	02/28/2019 10:47:34	Email																										
Job Number	JOB/00008	Website Customer																										
		Phone																										
		Job Order Category																										
<table border="1"> <thead> <tr> <th>Description</th> <th>Job Instructions</th> <th>Waste Materials</th> <th>Material Plannings</th> <th>Website</th> <th>Purchase Requisitions</th> <th>Subtasks</th> <th>Consumed Materials</th> <th>Material Requisitions</th> </tr> </thead> <tbody> <tr> <td>Timesheets</td> <td>Extra Info</td> <td>Timesheet Employee Users</td> <td>Maintenance Equipment</td> <td>Maintenance Requests</td> <td></td> <td></td> <td></td> <td></td> </tr> </tbody> </table>					Description	Job Instructions	Waste Materials	Material Plannings	Website	Purchase Requisitions	Subtasks	Consumed Materials	Material Requisitions	Timesheets	Extra Info	Timesheet Employee Users	Maintenance Equipment	Maintenance Requests										
Description	Job Instructions	Waste Materials	Material Plannings	Website	Purchase Requisitions	Subtasks	Consumed Materials	Material Requisitions																				
Timesheets	Extra Info	Timesheet Employee Users	Maintenance Equipment	Maintenance Requests																								
<table border="1"> <thead> <tr> <th>Job Instruction</th> <th>Description</th> <th>Responsible User</th> <th>Supervisor</th> <th>Quality Checklist</th> <th>Date</th> </tr> </thead> <tbody> <tr> <td>Site Cleaning (SC)</td> <td>Site Cleaning</td> <td>Mitchell Admin</td> <td>Mitchell Admin</td> <td>Site Cleaning</td> <td>01/04/2019</td> </tr> <tr> <td>Oil for Machine (Oil For Machine)</td> <td>Oil for Machine</td> <td>Mitchell Admin</td> <td>Mitchell Admin</td> <td>Oil Check</td> <td>01/04/2019</td> </tr> <tr> <td>Mats for Molding (MFM)</td> <td>Mats for Molding</td> <td>Mitchell Admin</td> <td>Mitchell Admin</td> <td>Molding Check</td> <td>01/04/2019</td> </tr> </tbody> </table>					Job Instruction	Description	Responsible User	Supervisor	Quality Checklist	Date	Site Cleaning (SC)	Site Cleaning	Mitchell Admin	Mitchell Admin	Site Cleaning	01/04/2019	Oil for Machine (Oil For Machine)	Oil for Machine	Mitchell Admin	Mitchell Admin	Oil Check	01/04/2019	Mats for Molding (MFM)	Mats for Molding	Mitchell Admin	Mitchell Admin	Molding Check	01/04/2019
Job Instruction	Description	Responsible User	Supervisor	Quality Checklist	Date																							
Site Cleaning (SC)	Site Cleaning	Mitchell Admin	Mitchell Admin	Site Cleaning	01/04/2019																							
Oil for Machine (Oil For Machine)	Oil for Machine	Mitchell Admin	Mitchell Admin	Oil Check	01/04/2019																							
Mats for Molding (MFM)	Mats for Molding	Mitchell Admin	Mitchell Admin	Molding Check	01/04/2019																							



❖ Set Job order reference on Job Instruction.

Job Instructions / INS/0001

INS/0001

Job Instruction	Mats for Molding (MFM)	Date	01/04/2019
Quality Checklist	Molding Check	Responsible User	Mitchell Admin
		Supervisor	Mitchell Admin
		Job	CNC Machine

Description Instruction Photos

Mat Industries - Offering Plastic Plain Concrete Mats and moulding mat.

Send message Log note Schedule activity Following 1

Today

YourCompany, Mitchell Admin - 11 minutes ago
• State: Draft

YourCompany, Mitchell Admin - 11 minutes ago
Job Instruction created



Expense Integration Job Orders for Project

- ❖ Employee can add expense integration on Job Orders for Construction and Contract on Project. Different Expenses are integrate with Job Order for Project. Also Expenses are integrated on job orders.

My Expenses / Painting Works

Action																	
Edit	Create																
Attach Document	Create Report																
2 / 2 < >																	
Description Painiting Works <table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <td style="width: 50%;"> Product Unit Price Quantity Taxes </td> <td style="width: 50%;"> Painting Works \$ 2,000.00 1.000Unit(s) </td> <td style="width: 50%;"> Bill Reference Date Account Employee Currency Analytic Account Analytic Tags Company </td> <td style="width: 50%;"> 12/31/2018 220000 Expenses Mitchell Admin USD Our Super Product - Deco Addict YourCompany </td> </tr> <tr> <td>Total Paid By</td> <td>\$ 2,000.00 Employee (to reimburse)</td> <td>Project Job Order</td> <td>Construction of Hypol Heights Painting Works</td> </tr> <tr> <td colspan="4"> Expense Images <table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <td style="width: 50%; text-align: center;">Photo 1 </td> <td style="width: 50%; text-align: center;">Photo 2 </td> </tr> <tr> <td style="width: 50%; text-align: center;">Photo 3 </td> <td style="width: 50%; text-align: center;">Photo 4 </td> </tr> </table> </td> </tr> </table>		Product Unit Price Quantity Taxes	Painting Works \$ 2,000.00 1.000Unit(s)	Bill Reference Date Account Employee Currency Analytic Account Analytic Tags Company	12/31/2018 220000 Expenses Mitchell Admin USD Our Super Product - Deco Addict YourCompany	Total Paid By	\$ 2,000.00 Employee (to reimburse)	Project Job Order	Construction of Hypol Heights Painting Works	Expense Images <table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <td style="width: 50%; text-align: center;">Photo 1 </td> <td style="width: 50%; text-align: center;">Photo 2 </td> </tr> <tr> <td style="width: 50%; text-align: center;">Photo 3 </td> <td style="width: 50%; text-align: center;">Photo 4 </td> </tr> </table>				Photo 1 	Photo 2 	Photo 3 	Photo 4
Product Unit Price Quantity Taxes	Painting Works \$ 2,000.00 1.000Unit(s)	Bill Reference Date Account Employee Currency Analytic Account Analytic Tags Company	12/31/2018 220000 Expenses Mitchell Admin USD Our Super Product - Deco Addict YourCompany														
Total Paid By	\$ 2,000.00 Employee (to reimburse)	Project Job Order	Construction of Hypol Heights Painting Works														
Expense Images <table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <td style="width: 50%; text-align: center;">Photo 1 </td> <td style="width: 50%; text-align: center;">Photo 2 </td> </tr> <tr> <td style="width: 50%; text-align: center;">Photo 3 </td> <td style="width: 50%; text-align: center;">Photo 4 </td> </tr> </table>				Photo 1 	Photo 2 	Photo 3 	Photo 4 										
Photo 1 	Photo 2 																
Photo 3 	Photo 4 																



Subcontracting in Job Order / Construction / Contracting Industry

- ❖ Allow to Create Subcontractor Job on Job Order for Create Subcontractor job and assign to subcontractor.

Jobs Job Costs Project Issues Projects Job Orders Sub Contractors Waste Reporting Maintenance Materials / BOQ Change Orders Analytic Account Invoicing Reports +

[Edit](#) [Create](#) Print [Action](#) 7 / 10

[Share](#) [Create Subtasks](#) [Create Subcontractor Job](#) [Create Repair Request](#) [Create / Edit Cost Sheet](#)

[Send by Email](#)

0 Sub-tasks	Active	1 Jobcosts
Stock Moves	0 Notes	Subcontractor Jobs
Purchase Re...		
More ▾		

JOB/0004

Flooring Works

Project	Construction of Hypol Heights	Deadline	05/30/2019
Project Phase	Flooring Works	Tags	Flooring
Assigned to	Mitchell Admin	Website Customer	Ready Mat
Starting Date	01/02/2019 11:00:42	Website Customer Name	Ready Mat
Ending Date	03/30/2019 11:30:42	Website Customer Email	ready.mat55@example.com
Job Number	JOB/00006	Website Customer Phone	8989989989
		Job Order Category	New Request

Description Job Instructions Waste Materials Material Planning Website Purchase Requisitions Subtasks Consumed Materials Material Requirements

Timesheets Extra Info Timesheet Employee Users Maintenance Equipment Maintenance Requests

Flooring is any a permanent covering of a floor, or the work of installing such a floor covering.
Floor covering is a term to generically describe any finish material applied over a floor structure to provide a walking surface.
Both terms are used interchangeably but floor covering refers more to loose-laid materials.



- ❖ Create Subcontractor Job Wizard set Responsible User / Subcontractor User, Job Name, Subcontractor (Vendor).

This wizard will create Job Order for Subcontractor.

Responsible User/ Subcontractor User	Camron Grill	Subcontractor
Job	Flooring Works	Job Description <i>Flooring is any a permanent covering of a floor, or the work of installing such a floor covering!</i>

Project

Project Phase	Flooring Works	Tags	Flooring
Assigned to	Mitchell Admin	Website Customer	Ready Mat
Starting Date	01/02/2019 11:00:42	Website Customer Name	Ready Mat
Ending Date	03/30/2019 11:30:42	Website Customer Email	ready.mat55@example.com
Job Number	JOB/00006	Website Customer Phone	8889989989
		Job Order Category	New Request

Description Job Instructions Waste Materials Material Plannings Website Purchase Requisitions Subtasks Consumed Materials Material Requisitions

Flooring is any a permanent covering of a floor, or the work of installing such a floor covering.
Floor covering is a term to generically describe any finish material applied over a floor structure to provide a walking surface.
Both terms are used interchangeably but floor covering refers more to loose-laid materials.



- ❖ Created Subcontractor Jobs on Create Subcontractor Job Wizard on Job Orders.

Screenshot of the Odoo software interface showing a job order record for "JOB/0007 Flooring Works".

The top navigation bar includes: Jobs, Job Costs, Project Issues, Projects, Job Orders, Sub Contractors, Waste Reporting, Maintenance, Materials / BOQ, Change Orders, Analytic Account, Invoicing, Reports, +, and Mitchell Admin.

Subcontractor Jobs / Flooring Works

Buttons: Edit, Create, Print, Action, Share, Create Subtasks, Create Purchase Order, Create Repair Request, Create / Edit Cost Sheet, Send by Email.

Job Details:

- JOB/0007**
- Flooring Works**
- Project:** Construction of Hypol Heights
- Project Phase:** Camron Grill
- Assigned to:** Website Customer
- Starting Date:** 01/04/2019 12:19:37
- Ending Date:** Website Customer
- Job Number:** JOB/00009
- Deadline:** Website Customer
- Tags:** Website Customer
- Stock Moves:** 0
- Notes:** 0
- Job costs:** 1
- Subcontractor Purchases:** 0
- Purchase Re...**

Job Order Category: More

Job Instructions, Waste Materials, Material Plannings, Website, Purchase Requisitions, Subtasks, Consumed Materials, Material Requisitions, Purchase Order Lines, Timesheets, Extra Info, Subcontractor Details, Timesheet Employee Users, Maintenance Equipment, Maintenance Requests.

Flooring is any a permanent covering of a floor, or the work of installing such a floor covering.

Send message, Log note, Schedule activity, Following, 4.



❖ Create Purchase Order on Subcontractor Jobs.

A screenshot of the Odoo software interface. The main window shows a job card for "JOB/00010 Flooring Works". The card displays details like Project (Construction of Hypol Heights), Assigned to (Andrew Smith), Starting Date (01/04/2019 12:26:00), and Job Number (JOB/00010). On the right side of the card, there are tabs for Purchase Requisitions, Subtasks, Consumed Materials, and Material Requirements. A modal window titled "* Create Subcontractor Purchase Order" is open over the card. The modal has a message stating "This wizard will create purchase order for subcontractor." It includes a dropdown for "Vendor / Subcontractor" set to "Azure Interior". At the bottom of the modal are "Create" and "Cancel" buttons. The background of the main window shows other tabs like Projects, Job Orders, Sub Contractors, Waste Reporting, Maintenance, Materials / BOQ, Change Orders, and Analytic Account.



- ❖ Purchase Order Created on Subcontractor Job, Subcontractor purchase some new product for complete jobs.

Purchase Purchase Control Reporting Configuration

Requests for Quotation / PO00020

Edit Create Print Action 2 / 21

Send by Email Print RFQ Confirm Order Cancel RFQ RFQ Sent Purchase Order

PO00020																																																														
Vendor	Azure Interior	Order Date	01/04/2019 05:30:00																																																											
Vendor Reference		Stock Picking																																																												
Sub Contractor Job	Flooring Works	Company	YourCompany																																																											
Currency	USD																																																													
<table border="1"> <thead> <tr> <th colspan="2">Products</th> <th colspan="10">Other Information</th> </tr> <tr> <th>Product</th> <th>Description</th> <th>Job Cost Center</th> <th>Job Cost Line</th> <th>Scheduled Date</th> <th>Company</th> <th>Analytic Account</th> <th>Analytic Tags</th> <th>Quantity</th> <th>Product Unit of Measure</th> <th>Unit Price</th> <th>Taxes</th> <th>Subtotal</th> </tr> </thead> <tbody> <tr> <td>Tiles</td> <td>Tiles</td> <td>COST-SHEET/00001</td> <td>Tiles</td> <td>01/04/2019 14:32:59</td> <td>YourCompany</td> <td></td> <td></td> <td>1.000</td> <td>Unit(s)</td> <td>0.00</td> <td><small>Tax 15.00%</small></td> <td>\$ 0.00</td> </tr> <tr> <td>Cement</td> <td>Cement</td> <td>COST-SHEET/00001</td> <td>Cement</td> <td>01/04/2019 14:33:00</td> <td>YourCompany</td> <td></td> <td></td> <td>1.000</td> <td>Unit(s)</td> <td>350.00</td> <td><small>Tax 15.00%</small></td> <td>\$ 350.00</td> </tr> </tbody> </table>												Products		Other Information										Product	Description	Job Cost Center	Job Cost Line	Scheduled Date	Company	Analytic Account	Analytic Tags	Quantity	Product Unit of Measure	Unit Price	Taxes	Subtotal	Tiles	Tiles	COST-SHEET/00001	Tiles	01/04/2019 14:32:59	YourCompany			1.000	Unit(s)	0.00	<small>Tax 15.00%</small>	\$ 0.00	Cement	Cement	COST-SHEET/00001	Cement	01/04/2019 14:33:00	YourCompany			1.000	Unit(s)	350.00	<small>Tax 15.00%</small>	\$ 350.00
Products		Other Information																																																												
Product	Description	Job Cost Center	Job Cost Line	Scheduled Date	Company	Analytic Account	Analytic Tags	Quantity	Product Unit of Measure	Unit Price	Taxes	Subtotal																																																		
Tiles	Tiles	COST-SHEET/00001	Tiles	01/04/2019 14:32:59	YourCompany			1.000	Unit(s)	0.00	<small>Tax 15.00%</small>	\$ 0.00																																																		
Cement	Cement	COST-SHEET/00001	Cement	01/04/2019 14:33:00	YourCompany			1.000	Unit(s)	350.00	<small>Tax 15.00%</small>	\$ 350.00																																																		
<table border="1"> <tr> <td>Untaxed Amount:</td> <td>\$ 350.00</td> </tr> <tr> <td>Taxes:</td> <td>\$ 52.50</td> </tr> <tr> <td>Total:</td> <td>\$ 402.50</td> </tr> </table>												Untaxed Amount:	\$ 350.00	Taxes:	\$ 52.50	Total:	\$ 402.50																																													
Untaxed Amount:	\$ 350.00																																																													
Taxes:	\$ 52.50																																																													
Total:	\$ 402.50																																																													



Construction Projects on Website

- ❖ Define different category of project like construction project are categories on residential, commercial, industrial.

A screenshot of a web-based project management application. The top navigation bar includes tabs for "Project", "Projects", "All Tasks", "Project Phases", "Reporting", and "Configuration". On the far right of the top bar, there are icons for user profile, notifications, and help, followed by the text "Mitchell Admin (apps12_jobcosting_bundle)". The main content area has a header "Project Categories" with "Create" and "Import" buttons. To the left, there is a sidebar with checkboxes for "Name", "Commercial Building", "Residential", and "Plotted Area". The main panel shows a table with columns for "Settings", "Stages", "Projects", "Tags", "Activity Types", and "Project Categories". A search bar and filter options are at the top of this panel. The bottom right corner of the main panel shows "1-3 / 3" and navigation arrows.



❖ Show Detail Description on Construction Projects.

Screenshot of a project management software interface showing the details of a construction project named "Construction of Hypol Heights".


Project Navigation: Project, Projects, All Tasks, Project Phases, Reporting, Configuration.

Project Details:

- Name:** Construction of Hypol Heights
- Description:** Name of the tasks : Tasks
- Allow timesheets:**
- Statistics:**

0 Documents	7 Tasks	Timesheets
Active	2 Jobcosts	8 Notes
Phases	More ▾	
- Project Structure:** Settings, Description, Brochures, Construction Site Detail, More Project Images, Gallery Images, Project Features And Amenities, Specification, Contact Us.
- Project Data:**

Project Manager	Camron Grill
Privacy	Visible by following customers
Customer	Azure Interior
Analytic Account	Hypol Heights - The Jackson Group
Code	
Price / Rate (Company Currency)	55,000,000.00
Product	[Deposit] Deposit
Reference	No rating
Customer(s) Ratings	
Sub-task Project	Construction of Hypol Heights
- Configuration:** Category (Commercial Building), Sequence (10).
- Time Scheduling:** Working Time (Standard 40 Hours/Week).





- ❖ Define Category on Project. Like Project are in Residential, Industrial or Commercial.

Jobs Job Costs Project Issues Projects Job Orders Sub Contractors Waste Reporting Maintenance Materials / BOQ Change Orders Analytic Account + ⌂ ⌃ ⌁ ⌂ Mitchell Admin (apps12_jobcosting_bundle)

Projects / Construction of Hypol Heights

Edit Create Print Action 2 / 4 Share

Construction of Hypol Heights

Name of the tasks : Tasks Allow timesheets

Documents	Tasks	Timesheets
0	7	8
Active	Jobcosts	Notes
Phases		More ▾

Settings Description Brochures Construction Site Detail More Project Images Gallery Images Project Features And Amenities Specification Contact Us

Project Floor Plan Project Location Plan Timesheet Employee Users

Project Manager	Camron Grill
Privacy	Visible by following customers
Customer	Azure Interior
Analytic Account	Hypol Heights - The Jackson Group
Code	
Price / Rate (Company Currency)	55,000,000.00
Product	[Deposit] Deposit
Reference	
Customer(s) Ratings	No rating
Sub-task Project	Construction of Hypol Heights

Configuration Time Scheduling

Category	Residential Building	Working Time
Sequence	10	Standard 40 Hours/Week



- ❖ Project description document is a general task of the project manager or his/her deputy who is supposed to identify the idea, goals, background, approach, outcomes and other data in a correct and comprehensive manner.

Jobs Job Costs Project Issues Projects Job Orders Sub Contractors Waste Reporting Maintenance Materials / BOQ Change Orders Analytic Account + G 2 * Mitchell Admin (apps12_jobcosting_bundle)

Projects / Construction of Hypol Heights

Edit Create Print Action 2 / 4 < >

Share

 **Construction of Hypol Heights**

Name of the tasks : Tasks Allow timesheets


 0 Documents	 7 Tasks	 Timesheets
 Active	 2 Jobcosts	 8 Notes
 Phases	More ▾	

[Settings](#) [Description](#) [Brochures](#) [Construction Site Detail](#) [More Project Images](#) [Gallery Images](#) [Project Features And Amenities](#) [Specification](#) [Contact Us](#)

[Project Floor Plan](#) [Project Location Plan](#) [Timesheet Employee Users](#)

This project consists of a combined kitchen, dining, living area, study, master suite, art studio, and storage area, with the flexibility to add bedrooms or an apartment. To meet the client's requirement that the house be highly efficient, it is constructed of structural insulated panels (SIPS). This method allows for a faster construction time, less waste generation, tighter construction, and better insulation. All the windows and doors are designed to surpass energy code requirements. The siting and design of the house maximize passive solar benefits to reduce the energy load.

✓ Following Last updated 4 days ago





- ❖ A Project brochure design is some new thing, which has a huge impact on how much interest you are going to get from audience for your respective project.

Jobs Job Costs Project Issues Projects Job Orders Sub Contractors Waste Reporting Maintenance Materials / BOQ Change Orders Analytic Account + C 2 * Mitchell Admin (apps12_jobcosting_bundle)

Projects / Construction of Hypol Heights

Edit Create Print Action Share 2 / 4

Construction of Hypol Heights

Name of the tasks : Tasks
 Allow timesheets

Documents 0 Tasks 7 Timesheets 8 Notes 2 Jobcosts Phases More

Settings Description Brochures Construction Site Detail More Project Images Gallery Images Project Features And Amenities Specification Contact Us

Project Floor Plan Project Location Plan Timesheet Employee Users

Name	Directory Tags	Attachment Users Tags	Number	Directory	Filename	Website	Resource Model	Resource Field	Resource ID Type	Document Version	Company	Created by
Brocher2			DOC/0224		27_cs_overhead.png				0 File	1.0	YourCompany	Mitchell Admin
Brocher1.jpeg					img1.jpeg		ir.module.module		441 URL	1.0	YourCompany	Mitchell Admin

Following 4



❖ A Project with more images of different area or location.

A screenshot of a web-based project management application. At the top, there's a navigation bar with links like "Jobs", "Job Costs", "Project Issues", "Projects", etc. On the right of the nav bar, it shows "Mitchell Admin (apps12_jobcosting_bundle)". Below the nav bar, the main content area has a header "Projects / Construction of Hypol Heights". There are "Edit" and "Create" buttons, and "Print" and "Action" dropdown menus. A "Share" button is also present. The main content area displays a project card for "Construction of Hypol Heights". The card includes a thumbnail image of a building under construction, the project name, and a summary section with "Name of the tasks : Tasks" and a checked "Allow timesheets" option. To the right of the summary are four small boxes showing document counts: 0 Documents, 7 Tasks, 2 Jobcosts, and 8 Notes. Below the summary are tabs for "Settings", "Description", "Brochures", "Construction Site Detail", "More Project Images" (which is selected), "Gallery Images", "Project Features And Amenities", "Specification", and "Contact Us". Under "More Project Images", there are links for "Project Floor Plan", "Project Location Plan", and "Timesheet Employee Users". A table below lists room names and their photo sizes: Bed Room (93.49 Kb), Dining Room (62.08 Kb), and Kitchen Layout (110.53 Kb). At the bottom right of the card, there are "Following" and "4" buttons. The rest of the page is mostly blank white space.



- ❖ Project with Gallery images. An image gallery to your project page, giving your clients a clear idea of your project.

Screenshot of a project management software interface showing a project details page for "Construction of Hypol Heights".

The top navigation bar includes: Jobs, Job Costs, Project Issues, Projects, Job Orders, Sub Contractors, Waste Reporting, Maintenance, Materials / BOQ, Change Orders, Analytic Account, +, and user info (Mitchell Admin (apps12_jobcosting_bundle)).

The main content area shows the project title "Construction of Hypol Heights" with a thumbnail image. Below the title are project settings and links: Name of the tasks : Tasks, Allow timesheets, Settings, Description, Brochures, Construction Site Detail, More Project Images, **Gallery Images**, Project Features And Amenities, Specification, Contact Us, Project Floor Plan, Project Location Plan, Timesheet Employee Users.

The "Gallery Images" section displays a table with four rows:

Name	Photo
Drawing Room Layout	65.03 Kb
Bed Room Layout	66.24 Kb
Floor Plan	66.24 Kb

Below the table, there are status indicators: ✓ Following, 4, and a dropdown menu.



- ❖ Premium project have lots of royal amenities like gym, swimming pool, golf course etc are added to it, apart from this have lots of quality service are added.

Jobs Job Costs Project Issues Projects Job Orders Sub Contractors Waste Reporting Maintenance Materials / BOQ Change Orders Analytic Account + C 2 * Mitchell Admin (apps12_jobcosting_bundle)

Projects / Construction of Hypol Heights

Edit Create Print Action 2 / 4 < >

Construction of Hypol Heights

Name of the tasks : Tasks Allow timesheets

Settings Description Brochures Construction Site Detail More Project Images Gallery Images Project Features And Amenities Specification Contact Us
Project Floor Plan Project Location Plan Timesheet Employee Users

1 Air Condition
2 Washroom
3 Automated homes
4 Entertainment Health
5 Eco-Friendly Environment
6 Gymnasium
7 Children's play area
8 Swimming pool & kids pool
9 Walking & jogging track

0 Documents 7 Tasks 8 Timesheets
Active 2 Jobcosts Notes
Phases More

✓ Following 4



- ❖ Project specification is a detailed. A description of objectives for any given development project.

Screenshot of a software interface showing a project details page for "Construction of Hypol Heights".

The top navigation bar includes links for Jobs, Job Costs, Project Issues, Projects, Job Orders, Sub Contractors, Waste Reporting, Maintenance, Materials / BOQ, Change Orders, Analytic Account, and user information for "Mitchell Admin (apps12_jobcosting_bundle)".

The main content area shows the project title "Construction of Hypol Heights" with a thumbnail image of a building under construction. Below the title, there are sections for "Name of the tasks : Tasks" and "Allow timesheets".

On the right side, there is a summary table with the following data:

0 Documents	7 Tasks	Timesheets
Active	2 Jobcosts	8 Notes
Phases	More ▾	

Below the summary, there are several tabs: Settings, Description, Brochures, Construction Site Detail, More Project Images, Gallery Images, Project Features And Amenities, Specification (which is selected), and Contact Us. Other visible tabs include Project Floor Plan, Project Location Plan, and Timesheet Employee Users.

The "Specification" tab contains the following project details:

- Project :- Completed
- Land Area :- Approx 2.15 acers
- Location :- San Francisco United States
- Drawing Room :- 40 Sqft
- Bed Room :- 45 Sqft
- Kitchen :- 35 Sqft



❖ Project location is define the location of your project.

The screenshot shows a web-based project management application. At the top, there is a navigation bar with links for Jobs, Job Costs, Project Issues, Projects, Job Orders, Sub Contractors, Waste Reporting, Maintenance, Materials / BOQ, Change Orders, Analytic Account, and other system icons. A user profile indicates "Mitchell Admin (apps12_jobcosting_bundle)".

The main content area displays a project titled "Construction of Hypol Heights". The project title is accompanied by a small thumbnail image of a building under construction. Below the title, there are two checkboxes: "Name of the tasks : Tasks" and "Allow timesheets".

To the right of the title, there is a summary table with the following data:

0 Documents	7 Tasks	Timesheets
Active	2 Jobcosts	8 Notes
Phases	More ▾	

Below the summary, there is a horizontal menu bar with links: Settings, Description, Brochures, Construction Site Detail, More Project Images, Gallery Images, Project Features And Amenities, Specification, Contact Us, Project Floor Plan, Project Location Plan, Timesheet Employee Users, and a link to "Oakland".

At the bottom of the page, there are two status indicators: "Following" and "4".



- ❖ Project Floor Plan Contain the detail about floor plan. Explore some potential floor plans available for your new home or remodel.

A screenshot of a web-based project management application. At the top, a navigation bar includes links for Jobs, Job Costs, Project Issues, Projects, Job Orders, Sub Contractors, Waste Reporting, Maintenance, Materials / BOQ, Change Orders, Analytic Account, and user-specific options like Mitchell Admin (apps12_jobcosting_bundle). Below the navigation is a breadcrumb trail: Projects / Construction of Hypol Heights. A toolbar offers Edit, Create, Print, and Action buttons, along with a page number indicator (2 / 4) and navigation arrows. The main content area displays a project titled "Construction of Hypol Heights". It includes a thumbnail image of a building under construction. Below the title, there are sections for "Name of the tasks : Tasks" and "Allow timesheets". To the right, a sidebar provides quick access to project documents, tasks, job costs, notes, and phases. A horizontal menu bar below the title lists various project details. A specific tab for "Project Floor Plan" is selected. The floor plan section contains a table with four rows: Name (Flooring Works, Door and Window Plan, Bed Room Layout, Drawing Room Layout), Description (Flooring Works, Door and Window Plan, Bed Room Layout, Drawing Room Layout), Brochures (Flooring Works, Door and Window Plan, Bed Room Layout, Drawing Room Layout), and Construction Site Detail (Flooring Works, Door and Window Plan, Bed Room Layout, Drawing Room Layout). At the bottom of the page, there are social sharing icons and a footer note indicating the page is part of a larger document (Page 4).



- ❖ Project Location plan. Projects should normally not be spread over a large area covering several districts.

A screenshot of a web-based project management application. At the top, there is a navigation bar with links for Jobs, Job Costs, Project Issues, Projects, Job Orders, Sub Contractors, Waste Reporting, Maintenance, Materials / BOQ, Change Orders, Analytic Account, and user information for 'Mitchell Admin (apps12_jobcosting_bundle)'. Below the navigation bar, the main content area shows a project titled 'Construction of Hypol Heights'. The project title is displayed prominently with a small thumbnail image of a building. Below the title, there are two checkboxes: 'Name of the tasks : Tasks' and 'Allow timesheets'. To the right of the title, there is a summary box containing icons and counts for 'Documents' (0), 'Tasks' (7), 'Timesheets' (8), 'Jobcosts' (2), and 'Notes' (8). Below this summary, there are links for 'Active', 'Phases', and 'More'. A horizontal menu bar follows, with 'Project Floor Plan' and 'Project Location Plan' being the active tabs. The main content area displays a form for 'Project Location Plan' with fields for 'Name' (containing 'Interior Plan', 'Drawing Room Location', and 'Bed Room'), 'Description' (empty), 'Brochures' (empty), 'Construction Site Detail' (empty), 'More Project Images' (empty), 'Gallery Images' (empty), 'Project Features And Amenities' (empty), 'Specification' (empty), and 'Contact Us' (empty). At the bottom of the page, there are status indicators: a green checkmark followed by 'Following', a dropdown arrow, and a link labeled '4'.



❖ Define Project Category on Website or My Account Portal.

Screenshot of a website interface showing project categories:

WEBSITE ▾ Pages Customize Promote

Your logo Create Repair Request My Repair Request Create Workorder My Job Orders Home Projects Machine Repair + Mitchell Admin ▾

Project Categories

Category	Image	Projects
Commercial Building		0
Residential Building		1
Plotted Area		0

Our Products & Services

Home

Connect with us

Contact us
+1 555 123 8069
info@yourcompany.example.com

Facebook Twitter LinkedIn YouTube Google+ GitHub Instagram

YourCompany - About us

We are a team of passionate people whose goal is to improve everyone's life through disruptive products. We build great products to solve your business problems.

Our products are designed for small to medium size companies willing to optimize their performance.



❖ Brief Details of Project by Category.

The screenshot shows a web-based application interface. At the top, there's a navigation bar with links for 'WEBSITE', 'Pages', 'Customize', 'Promote', 'My Website', 'New', and 'Edit'. Below the navigation is a header section with a placeholder for 'Your logo', a search bar, and a user dropdown for 'Mitchell Admin'. The main content area is titled 'Project Details' and displays a project card for 'Construction of Hypoi Heights - Azure Interior'. The card includes a thumbnail image of a modern building, the project name, and category filters for 'Commercial Building', 'Residential Building', and 'Plotted Area'. In the footer, there are sections for 'Our Products & Services' (with a 'Home' link), 'Connect with us' (listing social media icons for Facebook, Twitter, LinkedIn, YouTube, Google+, and Instagram, along with contact info: +1 555 123 8069 and info@yourcompany.example.com), and 'YourCompany - About us' (describing the company as a team of passionate people improving everyone's life through disruptive products). The footer also mentions that products are designed for small to medium size companies.

WEBSITE Pages Customize Promote My Website New Edit

Your logo Create Repair Request My Repair Request Create Workorder My Job Orders Home Projects Machine Repair Mitchell Admin

Search...

Project Details

Commercial Building
Residential Building
Plotted Area

Construction of Hypoi Heights - Azure Interior

Our Products & Services
Home

Connect with us
Contact us
+1 555 123 8069
info@yourcompany.example.com

f t in y g+ i

YourCompany - About us
We are a team of passionate people whose goal is to improve everyone's life through disruptive products. We build great products to solve your business problems.
Our products are designed for small to medium size companies willing to optimize their performance.



- ❖ Project Details on - Website
- ❖ Project Details report shows an overview of the activity of your projects, and a summary of your project's financials and profitability.

WEBSITE ▾ Pages Customize Promote

Your logo Create Repair Request My Repair Request Create Workorder My Job Orders Home Projects Machine Repair + Mitchell Admin ▾

Construction of Hypol Heights

Residential Building/Construction of Hypol Heights
Bed Room

Enquiry Now

Construction of Hypol Heights

This project consists of a combined kitchen, dining, living area, study, master suite, art studio, and storage area, with the flexibility to add bedrooms or an apartment. To meet the client's

Location

Azure Interior
3404 Edgewood Road
Jonesboro AR 72401
United States
(870)-931-0505



- ❖ Project Features and Amenities
- ❖ The Unit Features and Project Amenities displays the comparables selected for analysis.

WEBSITE ▾ Pages Customize Promote

Your logo Create Repair Request My Repair Request Create Workorder My Job Orders Home Projects Machine Repair + Mitchell Admin ▾

are designed to surpass energy code requirements. The siting and design of the house maximize passive solar benefits to reduce the energy load.

Project Features and Amenities Specification Gallery Brochure Floor Plan Location Plan Project Location Contact Us

1 Air Condition
2 Washroom
3 Automated homes
4 Entertainment Health
5 Eco-Friendly Environment
6 Gymnasium
7 Children's play area
8 Swimming pool & kids pool
9 Walking & jogging track



- ❖ A Project Specification is a comprehensive description of objectives for a development project.

WEBSITE Pages Customize Promote My Website + New Edit

Your logo Create Repair Request My Repair Request Create Workorder My Job Orders Home Projects Machine Repair Mitchell Admin

are designed to surpass energy code requirements. The siting and design of the house maximize passive solar benefits to reduce the energy load.

Project Features and Amenities Specification Gallery Brochure Floor Plan Location Plan Project Location Contact Us

Project :- Completed
Land Area :- Approx 2.15 acers
Location :- San Francisco United States
Drawing Room :- 40 Sqft
Bed Room :- 45 Sqft
Kitchen :- 35 Sqft



- ❖ Project Gallery Images: project gallery contain the detail with view level.

Your logo

Create Repair Request My Repair Request Create Workorder My Job Orders Home Projects Machine Repair + Mitchell Admin ▾

are designed to surpass energy code requirements. The siting and design of the house maximize passive solar benefits to reduce the energy load.

Project Features and Amenities Specification **Gallery** Brochure Floor Plan Location Plan Project Location Contact Us

Drawing Room Layout Bed Room Layout Floor Plan Kitchen Plan Layout

Our Products & Services
Home

Connect with us
Contact us
+1 555 123 8069
info@yourcompany.example.com

YourCompany - About us
We are a team of passionate people whose goal is to improve everyone's life through disruptive products. We build great products to solve your business problems.



- ❖ Project Brochure on Website
- ❖ A project brochure design is something, which has a huge impact on how much interest you are going to get from audience for your respective project.

The screenshot shows a website builder interface with a dark blue header bar. The top left has 'WEBSITE' with a dropdown arrow, 'Pages', 'Customize', and 'Promote'. The top right has 'My Website' with a dropdown arrow, '+ New', and 'Edit'.

The main content area displays a brochure page. At the top left is a placeholder for 'Your logo'. To its right is a navigation bar with links: 'Create Repair Request', 'My Repair Request', 'Create Workorder', 'My Job Orders', 'Home', 'Projects', 'Machine Repair', and 'Mitchell Admin' with a dropdown arrow. Below the navigation is a large text box containing the following text:

structural insulated panels (SIPs). This method allows for a faster construction time, less waste generation, tighter construction, and better insulation. All the windows and doors are designed to surpass energy code requirements. The siting and design of the house maximize passive solar benefits to reduce the energy load.

Below this text box is a horizontal navigation bar with tabs: 'Project Features and Amenities', 'Specification', 'Gallery' (which is selected), 'Brochure', 'Floor Plan', 'Location Plan', 'Project Location', and 'Contact Us'. Under the 'Gallery' tab, there are two image thumbnails: 'Brocher2' and 'Brocher1.jpeg'.

At the bottom of the page, there are three columns of information:

- Our Products & Services**
Home
- Connect with us**
Contact us
+1 555 123 8069
info@yourcompany.example.com
Social media icons: Facebook, Twitter, LinkedIn, YouTube, Instagram, etc.
- YourCompany - About us**
We are a team of passionate people whose goal is to improve everyone's life through disruptive products. We build great products to solve your business problems.
Our products are designed for small to medium size companies willing to optimize their performance.



- ❖ Project Floor Plan
- ❖ A floor plan is a drawing to scale, showing a view from above, of the relationships between rooms, spaces, traffic patterns, and other physical features at one level of a structure.

A screenshot of a website interface, likely a project management or repair service platform. The top navigation bar includes links for "WEBSITE", "Pages", "Customize", "Promote", "My Website", "+ New", and "Edit". Below the navigation is a header with a placeholder for "Your logo" and a menu bar with links for "Create Repair Request", "My Repair Request", "Create Workorder", "My Job Orders", "Home", "Projects", "Machine Repair", "Mitchell Admin", and "Floor Plan". The "Floor Plan" link is highlighted. The main content area displays two floor plans. The top floor plan is labeled "Flooring Works" and shows a detailed plan of a room with dimensions and a circular feature. The bottom floor plan shows a larger layout with multiple rooms and dimensions. The rest of the page is mostly blank white space.



- ❖ Project Location Plan
- ❖ A Project plan map, drawn to a suitable scale, showing the proposed mine development, shafts, works, etc., in relation to existing surface features.



❖ Project Location is defined where the project is located.

The screenshot shows a website builder interface with a dark blue header bar. The header includes a 'WEBSITE' dropdown, 'Pages', 'Customize', 'Promote', 'My Website' button, '+ New' button, and an 'Edit' button. Below the header is a main content area with a placeholder for 'Your logo' and a text input field containing 'reduce the energy load.' A navigation bar at the top of the content area has links for 'Create Repair Request', 'My Repair Request', 'Create Workorder', 'My Job Orders', 'Home', 'Projects', 'Machine Repair', and 'Mitchell Admin'. The main content area features a card for 'Azure Interior' with details like address, phone number, email, and a 'Google Maps' link. At the bottom, there are three columns: 'Our Products & Services' (with 'Home' link), 'Connect with us' (with social media icons for Facebook, Twitter, LinkedIn, YouTube, Google+, and Instagram), and 'YourCompany - About us' (with a brief description and 'Our products are designed for small to medium size companies willing to optimize their performance.').



❖ Contact Details of Project



❖ Project Category on Mobile View

The screenshot illustrates a website builder's mobile preview feature. The main workspace shows a homepage layout with sections for 'Project Categories' (featuring a large image of a modern building), 'Our Products & Services' (with a 'Home' link), and 'YourCompany - About us' (with a brief description and 'About us' link). A central modal window titled 'Mobile preview' displays the 'Project Categories' section as it would appear on a mobile device, showing a smaller image of the building and a navigation menu icon.



Payroll for Construction and Contracting Industry

- ❖ Configuration of Work Type Like Overtime, Overnight and Regular.

The screenshot shows the Odoo Timesheets configuration interface. The top navigation bar includes links for Timesheets, Timesheet, To Approve, Invoicing, Reporting, and Configuration. The Configuration tab is selected. On the left, there's a sidebar with 'Work Types' and buttons for 'Create' and 'Import'. The main area displays a list of work types with columns for 'Code' and 'Name'. The data is as follows:

Code	Name
<input type="checkbox"/>	Overtime
<input type="checkbox"/>	Overnight
<input type="checkbox"/>	Regular

At the top right of the main area, there are search, filter, group by, and favorite buttons. The status bar at the bottom right indicates '1-3 / 3'.



❖ Define Work Type Rate on Employee Contract.

Screenshot of the Odoo interface showing the configuration of a Marketing Executive Contract.

The top navigation bar shows "Employees" and sub-options: Employees, Contracts, Departments, Configuration. The top right shows "Mitchell Admin (apps12_jobcosting_bundle)" and various status indicators.

The main content area displays the "Marketing Executive Contract" details:

Employee	Mitchell Admin	Company	YourCompany
Department	Administration	Employee Category	Employee
Job Position	Human Resources Manager	Salary Structure	Marketing Executive
		Social Secretariat	(radio button)

Below the details, there are tabs for "Contract Details", "Work Type Rates" (which is selected), and "Salary Information".

Work Type	Rate
Regular	500.00
Overtime	300.00
Overnight	1,000.00

At the bottom, there are navigation buttons for "New", "Running", "To Renew", "Expired", and "Cancelled". A page number "1 / 2" is also present.



❖ Timesheet detail with work type rate.

Timesheets Timesheet To Approve Timecards To Approve Timecards Invoicing Reporting Configuration G 9 🔍 ⚡ Mitchell Admin (apps12_jobcosting_bundle)

All Timesheet Sheets / Week 1 Edit Create Print Action 1 / 1 < >

Submit to Manager New Open Waiting Approval Approved Paid

Mitchell Admin										Payslip																																																					
Timesheet Period		12/31/2018 to 01/06/2019																																																													
Company		Payslip																																																													
<table border="1"> <thead> <tr> <th colspan="4">Details</th> <th>Work Type</th> <th>Start Time</th> <th>End Time</th> <th>Amount</th> <th>Is Quantity</th> <th>Is Billable</th> <th>Is Paid</th> <th>Task</th> <th>Hours</th> </tr> </thead> <tbody> <tr> <td>01/04/2019</td> <td>Ground Flooring Works</td> <td>Construction of Hypol Heights</td> <td>Flooring Works</td> <td>Overtime</td> <td>10:00</td> <td>06:00</td> <td>-800.00</td> <td>8.00</td> <td><input type="checkbox"/></td> <td><input type="checkbox"/></td> <td>Flooring Works</td> <td>08:00</td> </tr> <tr> <td>01/04/2019</td> <td>For Trial Base</td> <td>Construction of Hypol Heights</td> <td>Flooring Works</td> <td>Regular</td> <td>10:00</td> <td>06:00</td> <td>800.00</td> <td>8.00</td> <td><input type="checkbox"/></td> <td><input type="checkbox"/></td> <td>Flooring Works</td> <td>08:00</td> </tr> <tr> <td>01/04/2019</td> <td>Assembling</td> <td>AGR - SO022</td> <td>[SERV_89744] Senior Architect (Invoice on Timesheets)</td> <td>Overnight</td> <td>10:00</td> <td>06:00</td> <td>-800.00</td> <td>8.00</td> <td><input type="checkbox"/></td> <td><input type="checkbox"/></td> <td>[SERV_89744] Senior Architect (Invoice on Timesheets)</td> <td>08:00</td> </tr> </tbody> </table>										Details				Work Type	Start Time	End Time	Amount	Is Quantity	Is Billable	Is Paid	Task	Hours	01/04/2019	Ground Flooring Works	Construction of Hypol Heights	Flooring Works	Overtime	10:00	06:00	-800.00	8.00	<input type="checkbox"/>	<input type="checkbox"/>	Flooring Works	08:00	01/04/2019	For Trial Base	Construction of Hypol Heights	Flooring Works	Regular	10:00	06:00	800.00	8.00	<input type="checkbox"/>	<input type="checkbox"/>	Flooring Works	08:00	01/04/2019	Assembling	AGR - SO022	[SERV_89744] Senior Architect (Invoice on Timesheets)	Overnight	10:00	06:00	-800.00	8.00	<input type="checkbox"/>	<input type="checkbox"/>	[SERV_89744] Senior Architect (Invoice on Timesheets)	08:00	24.00	24.00
Details				Work Type	Start Time	End Time	Amount	Is Quantity	Is Billable	Is Paid	Task	Hours																																																			
01/04/2019	Ground Flooring Works	Construction of Hypol Heights	Flooring Works	Overtime	10:00	06:00	-800.00	8.00	<input type="checkbox"/>	<input type="checkbox"/>	Flooring Works	08:00																																																			
01/04/2019	For Trial Base	Construction of Hypol Heights	Flooring Works	Regular	10:00	06:00	800.00	8.00	<input type="checkbox"/>	<input type="checkbox"/>	Flooring Works	08:00																																																			
01/04/2019	Assembling	AGR - SO022	[SERV_89744] Senior Architect (Invoice on Timesheets)	Overnight	10:00	06:00	-800.00	8.00	<input type="checkbox"/>	<input type="checkbox"/>	[SERV_89744] Senior Architect (Invoice on Timesheets)	08:00																																																			



❖ Employee Payslip Detail with work type rates.

Payroll Employee Payslips Payslips Batches Configuration

Mitchell Admin (apps12_jobcosting_bundle)

Employee Payslips / Salary Slip of Mitchell Admin for January-2019

Edit Create Print Action

2 / 2 < >

Confirm Compute Sheet Cancel Payslip Draft

Mitchell Admin							
Period	01/01/2019 - 01/31/2019	Contract	Contract For January 2019 - December 2019 Base for new structures				
Reference	SLIP/002	Structure					
Payslip Name	Salary Slip of Mitchell Admin for January-2019	Credit Note					
Worked Days & Inputs	Salary Computation	Details By Salary Rule Category	Accounting Information	Timesheet Line	Work Type Rates		
Name	Code	Category	Quantity	Rate (%)	Rule	Amount	Total
Basic Salary	BASIC	Basic	1.00	100.0000	Basic Salary	5,000.00	5,000.00
House Rent Allowance	HRA	Allowance	1.00	40.0000	House Rent Allowance	5,000.00	2,000.00
Conveyance Allowance	CA	Allowance	1.00	100.0000	Conveyance Allowance	800.00	800.00
Conveyance Allowance For Gravie	CAGG	Allowance	1.00	100.0000	Conveyance Allowance For Gravie	600.00	600.00
Meal Voucher	MA	Allowance	0.00	100.0000	Meal Voucher	10.00	0.00
Get 1% of sales	SALE	Allowance	1.00	100.0000	Get 1% of sales	0.00	0.00
Regular Salary	REG	Allowance	1.00	100.0000	Regular Salary	0.00	0.00
Overtime Salary	OT	Allowance	1.00	100.0000	Overtime Salary	0.00	0.00
Overnight Salary	ON	Allowance	1.00	100.0000	Overnight Salary	0.00	0.00

Probuse Consulting Service PVT Ltd.



Request for Information (Construction and Contracting Business)

- ❖ Request for Information of any Project on Construction.A Request for Information (RFI) is a formal question asked by one party to a contract on a construction project to the other party. Customer/supplier can submit request online from your website and team can response with answers.

The screenshot shows a web-based application interface for creating a Request for Information (RFI). The top navigation bar includes links for WEBSITE, Pages, Customize, Promote, Published, My Website, New, and Edit. The main content area is titled "Create RFI". It contains several input fields: "Your Name" (Mitchell Admin), "Your Email" (admin@yourcompany.example.com), "Your Phone" (+1 555-555-5555), "RFI Category" (Substitution/Construction Modification), "RFI Subject" (About Flooring Material), "RFI Description" (a text area containing a message asking for details about flooring material and quality measurement), "RFI Priority" (Low), and an "Attach Files" section with a "Choose Files" button and a note stating "No file chosen". A "Submit" button is located at the bottom of the form.



- ❖ Request for Information is Created on Website portal My Account.
- ❖ A Request for Information (RFI) document is used to keep the project moving in a cost-effective.

Jobs Dashboard Job Costs Project Issues Inspections Projects Request for Information Job Orders Sub Contractors Waste Reporting Maintenance Transmittals Submittals Materials / BOQ +

Request for Informations / RFI/00001

[Edit](#) [Create](#) [Print](#) [Action](#)

New Assigned Work In Progress Needs More Info Needs Reply Reopened Solution Suggested Closed

[Set To Close](#)

RFI/00001

About Flooring Material

Type	Material Inquiry	Customer/Supplier	Your Company, Mitchell Admin
Subject	Flooring	Phone	+1 555-555-5555
Assign To Company	Andrew Smith Your Company	Email	admin@yourcompany.example.com
		Allow Users	Joe Wiles
RFI Team	Flooring Work Team	Team Leader	Carmon Grill
Project	Construction of Hypol Heights	Analytic Account	Hypol Heights - The Jackson Group
Job Order	Flooring Works	Priority	Low
Job Cost Sheet	COST-SHEET00003	RFI Category	Substitution/Construction Modification
Job Cost Line	Cement		
Create Date	01/07/2019 12:57:22		
Is Closed ?	<input type="checkbox"/>		
Closed Date	01/23/2019 12:58:50		

[Description](#) [Timesheets](#) [Customer/Supplier Rating](#) [RFI Survey](#) [RFI Answer](#)

Dear Team,

Can you provide details about material you are using flooring of third floor? And Please also send quality measurement of that as well.

Thank You.

Follow [▲ 1](#)



❖ Display List of Request for Information on Portal.

WEBSITE Pages Customize Promote My Website + New Edit

Your logo Create Repair Request My Repair Request Create Workorder My Job Orders Home Projects Machine Repair Mitchell Admin

Your Request for Informations

RFI No.	RFI Subject	Date	Priority	Stage
RFI/00001	About Flooring Material	01/07/2019 08:27:22	Low	New

Our Products & Services
[Home](#)

Connect with us
[Contact us](#)
+1 555 123 8069
info@yourcompany.example.com

[Facebook](#) [Twitter](#) [LinkedIn](#) [YouTube](#) [Google+](#) [Pinterest](#) [Instagram](#)

YourCompany - [About us](#)
We are a team of passionate people whose goal is to improve everyone's life through disruptive products. We build great products to solve your business problems.
Our products are designed for small to medium size companies willing to optimize their performance.

Copyright © YourCompany. [English](#) [Add a language](#)



❖ Display Request for Information on Portal My Account.

WEBSITE ▾ Pages Customize Promote

Your logo Create Repair Request My Repair Request Create Workorder My Job Orders Home Projects ▾ Machine Repair + Mitchell Admin ▾

My Requests RFI/00001

RFI/00001 - About Flooring Material

Assigned to : Andrew Smith
Support Team : Flooring Work Team
Project: Construction of Hypol Heights
Job Order: Flooring Works
Job Cost Sheet: COST-SHEET/00003
Create Date: 01/07/2019 08:27:22
Is Closed? :
Close Date: 01/23/2019 08:28:50
Dear Team,

Can you provide details about material you are using flooring of third floor? And Please also send quality measurement of that as well.

Thank You.

Send Message and Attachments

Add a comment...



- ❖ Request for Information Configuration Like RFI Type, RFI Subject, RFI Team, RFI Stages.

A screenshot of a software application window titled "Jobs". The top navigation bar includes links for Dashboard, Job Costs, Project Issues, Inspections, Projects, Request for Information, Job Orders, and Sub Contractors. On the left, a sidebar titled "RFI Subjects" shows a list with "Name" and "Flooring" checked. The main content area displays a search bar, filter options ("Filters", "Group By"), and a list of configuration items. A vertical sidebar on the right lists various configuration categories such as Stages, Job Types, Project Issues, Issue Teams, Type of Issue Subject, Issue Types, Issue Stages, RFI Configuration, RFI Subject, RFI Types, RFI Teams, RFI Stages, Transmittal / Submittal Types, Mediums, Instructions, Quality Checklists, Inspection Values, Inspection Results, Inspection Types, Project Teams, Cost Sheet Tags, Documents, Directory Tags, and Document Tags. The status bar at the bottom right indicates "1-1 / 1".



Jobs Dashboard Job Costs Project Issues Inspections Projects Request for Information Job Orders Sub Contractors Waste Reporting Maintenance + C 9 2 Mitchell Admin

RFI Type

Create Import

Name
 Material Inquiry

Search... Filters Group By Favorites

All Documents My Documents Reports Request for Information Configuration Stages Job Types Project Issues Issue Teams Type of Issue Subject Issue Types Issue Stages RFI Configuration RFI Subject RFI Types RFI Teams RFI Stages Transmittal / Submittal Types Mediums Instructions Quality Checklists Inspection Values Inspection Results Inspection Types

Jobs Dashboard Job Costs Project Issues Inspections Projects Request for Information Job Orders Sub Contractors + C 9 2 Mitchell Admin (apps12_jobcosting_bundle)

RFI Team

Create Import

	Leader
<input type="checkbox"/> Name	OdooBot
<input type="checkbox"/> Direct Sales	OdooBot
<input type="checkbox"/> Website Sales	Cameron Grill
<input type="checkbox"/> Flooring Work Team	

Search... Filters Group By

Configuration Stages Job Types Project Issues Issue Teams Type of Issue Subject Issue Types Issue Stages RFI Configuration RFI Subject RFI Types RFI Teams RFI Stages Transmittal / Submittal Types Mediums Instructions Quality Checklists Inspection Values Inspection Results Inspection Types Project Teams Cost Sheet Tags Documents Directory Tags Document Tags



Jobs Dashboard Job Costs Project Issues Inspections Projects Request for Information Job Orders Sub Contractors

RFI Stages

Create Import

Stage Name
<input type="checkbox"/> New
<input type="checkbox"/> Assigned
<input type="checkbox"/> Work in Progress
<input type="checkbox"/> Needs More Info
<input type="checkbox"/> Needs Reply
<input type="checkbox"/> Reopened
<input type="checkbox"/> Solution Suggested
<input type="checkbox"/> Closed

Search... Filters Group By

Support Team

Stages

Job Types

Project Issues

Issue Teams

Type of Issue Subject

Issue Types

Issue Stages

RFI Configuration

RFI Subject

RFI Types

RFI Teams

RFI Stages

Transmittal / Submittal

Types

Mediums

Instructions

Quality Checklists

Inspection Values

Inspection Results

Inspection Types

Project Teams

Cost Sheet Tags

Documents

Directory Tags

Document Tags

1-8 / 8



Job Order / Task Inspection

- ❖ You have to inspection feature on your Job Orders for Construction and Job Contracting Projects. A task or job for customer that can be scheduled.

Jobs Job Costs Project Issues Inspections Projects Job Orders Sub Contractors Waste Reporting Maintenance + C E S Mitchell Admin (apps12_jobcosting_bundle)

Job Inspections / INSP/0001 Edit Create Print Action 1 / 1 < >

INSP/0001
Formal Inspection

Project	Construction of Hypol Heights	Create Date	01/04/2019
Analytic Account	Hypol Heights - The Jackson Group	Inspection Location	
Job Order	Flooring Works	Inspection	Andrew Smith
Job Cost Sheet	COST-SHEET/00003	Responsible	
Job Cost Sheet Line	Cement	Subcontractor	Camron Grill
		Reference Specification	
Inspection Type	Formal Periodic	Inspection Result	WHC
Inspection Start Date	01/04/2019 18:49:50	Inspection End Date	01/30/2019 18:40:54
Responsible User	Mitchell Admin	Company	YourCompany

Inspection Lines Other Info Internal Note Result Description Inspection Photos

Inspection	Inspection Result	Description
Tiles	Tiles-R1	Tiles-R1
White Cement	WHC	White Cement - WHC1



❖ Job Inspection are integrated with job costsheet.

Jobs Job Costs Project Issues Projects Job Orders Sub Contractors Waste Reporting Maintenance Materials / BOQ Change Orders Analytic Account + Mitchell Admin (apps12_jobcosting_bundle)

Job Cost Sheets / COST-SHEET/00003

Edit Create Print Action 3 / 3

Create Invoice Approve Create Estimation Cancel Draft Confirmed Done

COST-SHEET/00003																	
Name	New	Project	Construction of Hypol Heights	Analytics Account	Hypol Heights - The Jackson Group	Job Order	Flooring Works	Customer	Azure Interior, Nicole Ford	Create Date	01/04/2019						
										Closed Date							
										Created By	Mitchell Admin						
										Company	YourCompany						
										Currency	USD						
										Description	Based On Actual Vendor Bill Qty						
										Sale Reference							
										Customer Invoice							
										Billable Method							
Materials	Labours	Overhead															
Date	Job Type	Product	Description	Reference	Planned Qty	Cost / Unit	Sale Price / Unit	Actual Requisition Quantity	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Actual Vendor Sub Total	Cost Price	Manual Invoiced Qty	Customer Invoiced Qty	Is Billab.
01/21/2019	Site-Preparation-	Cement	Cement		1.00 Unit(s)	0.00	350.00	0.00	0.00	0.00	0.00	0.00	\$ 0.00	0.00	0.00	0.00	Billab.



- ❖ Inspection Results
- ❖ An inspection involves checking something, i.e., examining and assessing something. We may inspect a building or organization to make sure that it meets specific standards.

A screenshot of a software application interface titled "Jobs". The top navigation bar includes links for Job Costs, Project Issues, Inspections, Projects, Job Orders, Sub Contractors, Waste Reporting, Maintenance, and a "+" button. On the far right, it shows "Mitchell Admin (apps12_jobcosting_bundle)". The main content area is titled "Inspection Results". It features a search bar, a "Filters" dropdown menu, and a table with three rows. The first row has checkboxes for "Code", "Name" (containing "WHD"), and "Type" (containing "Tiles-R1"). The second row has checkboxes for "Code", "Name" (containing "WHD-1"), and "Type" (containing "Tiles-R1"). The third row has checkboxes for "Code", "Name" (containing "R1"), and "Type" (containing "Tiles-R1"). To the right of the table is a sidebar with a tree view of inspection-related modules: Issue Types, Issue Stages, Instructions, Quality Checklists, Inspection Values, Inspection Results, and Inspection Types. A "Favorites" dropdown is also present in the sidebar. The bottom right corner of the sidebar shows "1-2 / 2".





❖ Inspection Values

A screenshot of an Odoo application window titled "Jobs". The top navigation bar includes links for Job Costs, Project Issues, Inspections, Projects, Job Orders, Sub Contractors, Waste Reporting, and Maintenance. A search bar and a "Filters" dropdown are also present. The main content area shows a list of "Inspection Values" with columns for "Code" and "Name". The "Name" column lists "Tiles", "White Cement", and "Cement". On the right side, a vertical sidebar displays a hierarchical menu of modules: Change Orders, Analytic Account, Analytic Accounts, Invoicing, Timesheets to Invoice, Reports, Issue Analysis, Costing Reports, Job Costing Volum Trends, Configuration, Stages, Job Types, Project Issues, Issue Teams, Type of Issue Subject, Issue Types, Issue Stages, Instructions, Quality Checklists, Inspection Values, Inspection Results, and Inspection Types. The "Inspection Values" item is highlighted in the menu.



❖ Inspection Types

A screenshot of a software application window titled "Jobs". The main content area is labeled "Inspection Types" and shows a table with two rows of data. The columns are "Code" and "Name". The first row has a checkbox next to "Code" which is unchecked, and "Name" is "Formal Periodic". The second row has a checkbox next to "Code" which is also unchecked. On the far left of the table, there are "Create" and "Import" buttons. To the right of the table are search and filter tools, including a "Search..." field, a "Filters" dropdown menu, and a sidebar with links like "Issue Types", "Issue Stages", "Instructions", "Quality Checklists", "Inspection Values", "Inspection Results", and "Inspection Types". A vertical scrollbar is visible on the right side of the table. The top navigation bar includes links for "Job Costs", "Project Issues", "Inspections", "Projects", "Job Orders", "Sub Contractors", "Waste Reporting", and "Maintenance". The top right corner shows the user "Mitchell Admin (apps12_jobcosting_bundle)".





Project by Phases

- ❖ Each Project different phases. Project phase represents the collection of the project activities aimed to prepare the product. Each project phase is goal-oriented and contains a particular number of the work steps. Each phase ends at a milestone, whose attainment means the project progress.

The screenshot shows the Odoo Project Phases module interface. At the top, there's a navigation bar with tabs: Project, Projects, All Tasks, Project Phases, Reporting, Configuration. On the right, there are notifications for 9 messages, 2 comments, and 1 follower, and a dropdown for 'Mitchell Admin (apps12_jobcosting_bundle)'.

The main content area displays the 'Design Development (DD) phase' details:

Design Development (DD) phase		Tasks	
Project	Construction of Hypol Heights	Sequence	1
Start Date	01/01/2019	End Date	01/01/2019
Responsible User	Mitchell Admin	Company	YourCompany

Below the table, there's a section for 'Internal Note' which is currently empty. At the bottom of the page, there are links for 'Send message', 'Log note', 'Schedule activity', and a 'Following' status with 1 follower. The date 'January 1, 2019' is also visible.



- ❖ Project - Phase
- ❖ Dividing a project into phases makes it possible to lead it in the best possible direction of project.

Project Projects All Tasks Project Phases Reporting Configuration C 9 M 2 S 1 Mitchell Admin (apps12_jobcosting_bundle)

Projects / Construction of Hypol Heights

Edit Create Print Action 4 / 7 < >

Share Create Sales Order

Construction of Hypol Heights

Name of the tasks : Tasks Allow timesheets

0 Documents	7 Tasks	Timesheets
Active	3 Jobcosts	8 Notes
Phases	More ▾	

Settings Description Brochures Construction Site Detail More Project Images Gallery Images Project Features And Amenities Specification Contact Us

Project Floor Plan Project Location Plan Timesheet Employee Users

Project Manager	Camron Grill
Privacy	Visible by following customers
Customer	Azure Interior
Analytic Account	Hypol Heights - The Jackson Group
Code	
Price / Rate (Company Currency)	55,000.00.00
Product	[Deposit] Deposit
Reference	



Meeting Minutes for Construction and Contracting Projects

- ❖ Meeting Minutes for construction project are a tangible record of the meeting for its participants and source of information for members who were unable to attend project meeting.

Calendar

Meetings / Meeting for Project Floor Planing

Edit Create Print Action 9 / 9 < >

Meeting for Project Floor Planing

Andrew Smith Azure Interior Camron Grill

Meeting Details Options Meeting Additional Info Invitations Misc

Presenter	Andrew Smith
Facilitator	Azure Interior
Note Taker	Azure Interior
Time Keeper	Deco Addict
Agenda Topics	Flooring Works
Action Items	
Conclusion	

Send message Log note ✓ Following Today

YourCompany, Mitchell Admin - 6 minutes ago

- Start Date: January 5, 2019
- End Date: January 5, 2019



- ❖ Project Meeting
- ❖ Project requires periodic meetings where the project member get together to discuss the project's goals, assigned tasks, and progress.

Jobs Job Costs Project Issues Inspections Projects Job Orders Sub Contractors Waste Reporting Maintenance +

Mitchell Admin (apps12_jobcosting_bundle)

Projects / Construction of Hypol Heights

Edit Create Print Action 4 / 7 < >

Share Create Sales Order



Construction of Hypol Heights

Name of the tasks : Tasks
 Allow timesheets

Settings Description Brochures Construction Site Detail More Project Images Gallery Images Project Features And Amenities Specification Contact Us

Project Floor Plan Project Location Plan Timesheet Employee Users

Project Manager	Camron Grill
Privacy	Visible by following customers
Customer	Azure Interior
Analytic Account	Hypol Heights - The Jackson Group
Code	
Price / Rate (Company Currency)	55,000,000.00
Product	[Deposit] Deposit
Reference	No rating
Customer(s) Ratings	
Sub-task Project	Construction of Hypol Heights

 0 Documents	 7 Tasks	 Timesheets
 Active	 3 Jobcosts	 8 Notes
	 Phases	More ▾



Issue Tracking System for Construction and Contracting

- ❖ Create Request for Issue of construction contracting on website portal My account.

WEBSITE Pages Customize Promote

Your logo Create Repair Request My Repair Request Create Workorder My Job Orders Home Projects Machine Repair + Mitchell Admin

Create Issue

Your Project Issues

Issue No	Title	Date	Priority	Stage
ISSUE-00001	Damage Bricks and Low Quality Cement	01/05/2019 06:14:28	High	New

Our Products & Services

Home

Connect with us

Contact us
+1 555 123 8069
info@yourcompany.example.com

Facebook Twitter LinkedIn YouTube Google+ Instagram

YourCompany - About us

We are a team of passionate people whose goal is to improve everyone's life through disruptive products. We build great products to solve your business problems.

Our products are designed for small to medium size companies willing to optimize their performance.

Copyright © YourCompany 2019 Artis Template



WEBSITE Pages Customize Promote

Your logo Create Repair Request My Repair Request Create Workorder My Job Orders Home Projects Machine Repair + Mitchell Admin ▾ Published My Website + New Edit

Customer
Mitchell Admin

Email
admin@yourcompanyexample.com

Phone
+1 555-555-5555


Category
Design Deficiencies

Subject
Damage Tiles and Low Quality Cement

Description
For Flooring work use low quality cement and damage tiles.

Priority
Low

Attach Files
 No file chosen
Multiple files can be attach





- ❖ Create Project Related Issues Request. On Issue Create task, Create Invoice, and also filling timesheet.

Issues Project Issues Analytic Account Invoicing Reports Configuration

Project Issues / ISSUE-00002 Mitchell Admin (apps12_jobcosting_bundle)

[Edit](#) [Create](#) Print [Action](#)

[Set To Close](#) 1 / 2

ISSUE-00002		Active		Create Invoice	Create Task
Damage Tiles and Low Quality Cement				Analytic Account	
Type of Issue	Flooring Issue	Customer	YourCompany, Mitchell Admin		
Type of Issue Subject	Commercial Construction	Phone	+1 555-555-5555		
Assign To	Cameron Grill	Allow Users	Andrew Smith Joel Willis		
Email	admin@yourcompany.example.com	Team Leader	Cameron Grill		
Company	YourCompany	Analytic Account	Hypol Heights - The Jackson Group		
Construction Team	Painting Team	Priority	Low		
Project	Construction of Hypol Heights	Category	Design Deficiencies		
Job Order	Flooring works				
Job Cost Sheet	COST-SHEET00004				
Job Cost Line	Tiles				
Department	Sales				
Create Date	01/05/2019 11:12:28	Close Date	00:00		
Is Issue Closed ?	<input type="checkbox"/>	Total Hours Spent			
		To View Current Status of Customer Prepaid Support Hours,Please Click Analytic Account Button.			
		Total Consumed Hours	509:00		
		Total Purchase Hours	00:00		
		Remaining Hours	-509:00		
Description Timesheets Add Invoice Lines General Information Customer Rating					



- ❖ Project Issues configuration on Issue Teams, Types of Issue Subject, Issue Types, Issue Stages.

A screenshot of the Odoo software interface, specifically the 'Issues' module. The top navigation bar includes links for 'Project Issues', 'Analytic Account', 'Invoicing', 'Reports', and 'Configuration'. The 'Configuration' tab is selected. On the left, there's a sidebar with 'Issue Teams' and buttons for 'Create' and 'Import'. The main area shows a list of issue teams with columns for 'Name', 'Leader', and 'Is Default Team?'. The data includes:

Name	Leader	Is Default Team?
Direct Sales	Cameron Grill	<input type="checkbox"/>
Website Sales	John Abraham	<input type="checkbox"/>
Painting Team	Cameron Grill	<input checked="" type="checkbox"/>
Construction Team	Joel Willis	<input type="checkbox"/>



The screenshot shows two identical web application interfaces side-by-side, both titled "Issues".

The top navigation bar includes links for "Project Issues", "Analytic Account", "Invoicing", "Reports", and "Configuration". On the far right, it shows "Mitchell Admin (apps12_jobcosting_bundle)".

The main content area has a search bar at the top right and three filter buttons: "Filters", "Group By", and "Favorites".

Left Panel (Top): Type of Issue Subject

- Name
- Commercial Construction
- Residential Construction
- Industry Construction

Left Panel (Bottom): Issue Types

- Name
- Flooring Issue
- Painting Issue

The bottom of each panel shows page navigation controls: "1-3 / 3" and "1-2 / 2" respectively.



Issues Project Issues Analytic Account Invoicing Reports Configuration

Issue Stages

<input type="checkbox"/> Stage Name
<input type="checkbox"/> + New
<input type="checkbox"/> + Assigned
<input type="checkbox"/> + Work in Progress
<input type="checkbox"/> + Needs More Info
<input type="checkbox"/> + Needs Reply
<input type="checkbox"/> + Reopened
<input type="checkbox"/> + Solution Suggested
<input type="checkbox"/> + Closed

Construction Team

search... Filters Group By Favorites

1-8 / 8

❖ Invoice Created on Project Issue.

Issues Project Issues Analytic Account Invoicing Reports Configuration

Project Issues / ISSUE-00002 / Invoices / Invoice ISSUE-00002

Edit Create Print Action

Validate Preview Draft Open Paid

Draft Invoice

Customer	Your Company, Mitchell Admin 215 Vine St Scranton, PA 18503 United States	Invoice Date	01/05/2019
Delivery Address		Due Date	
Payment Terms		Salesperson	Cameron Grill
Progress Billing Title		Job Cost Sheet	
Project		Sales Team	Europe
Cash Rounding		Currency	USD
Method			

Invoice Lines Other Info

Product	Description	Account	Analytic Account	Analytic Tags	Quantity	Unit of Measure	Price	Disc (%)	Taxes	Subtotal	Total
Tiles	Tiles	220000 Expenses	Hypol Heights - The Jackson Group		500.000	Unit(s)	50.00	0.00	\$ 25,000.00	\$ 25,000.00	
Cement	Cement	220000 Expenses	Hypol Heights - The Jackson Group		50.000	Unit(s)	350.00	0.00	\$ 17,500.00	\$ 17,500.00	

Untaxed Amount: \$ 42,500.00
Tax: \$ 0.00
Total: \$ 42,500.00

Progress Billing Information

Total Progress Billing	\$ 0.00	Previously Invoiced	\$ 0.00
Invoice To Date	\$ 0.00	Previously Invoiced	\$ 0.00
Remaining Progress Billing	\$ 0.00	Due	
		Current Invoiced	\$ 42,500.00



Job Drawing Construction and Contracting Business

❖ Added Google Drawing Document on Job Order or Task.

Jobs Job Costs Project Issues Inspections Projects Job Orders Sub Contractors Waste Reporting Maintenance Materials / BOQ Change Orders + Mitchell Admin (apps12_jobcosting_bundle)

Job Orders / Flooring Works Print Action

[Edit](#) [Create](#)

Description		Job Instructions	Waste Materials	Material Plannings	Website	Purchase Requisitions	Subtasks	Consumed Materials	Material Requisitions															
Timesheets	Extra Info	Timesheet Employee Users	Maintenance Equipment	Maintenance Requests	Work Duration	Customer Signature																		
Google Drawing Document																								
Create a Google Drawings <table border="1"> <thead> <tr> <th>Drawing Name</th> <th>Description</th> <th>Google Drawing Url</th> </tr> </thead> <tbody> <tr> <td>Home Plan</td> <td>A house plan is a set of construction or working drawings (sometimes still called blueprints) that define all the construction specifications of a residential house such as dimensions, materials, layouts, installation methods and techniques.</td> <td>https://www.google.co.in/search?q=Home+Plan+Description&source=lms&tbo=isch&sa=X&ved=0ahUKEwipu8-thdbfAhUGbo8KHd4rCvkQ_AUDigB&cshid=1546670797476003&bih=1183&bth=583#imgrc=frXRZGlyHoHRIM</td> <td>Open</td> </tr> <tr> <td>Living Room Design</td> <td>The living room is the place where friends and family gather to spend quality time in a home, so it's important for it to be well-designed</td> <td>https://www.google.co.in/search?bih=1183&bth=583&tbo=isch&sa=1&ei=ilmwXPrGL4zPvgT-jHqCq&q=Living+Room+Plan&sq=Living+Room+Plan&gs_l=img.3..0i10.148294.153067..153373...0.0.0.146.1635.9j7.....1....1.gws-wiz-img.....3539j067.IDEgi4Jwr7o#imgrc=bD_MTGv6IepDZM</td> <td>Open</td> </tr> <tr> <td>Kitchen Plan</td> <td>The kitchen layout is the shape that is made by the arrangement of the countertop, major appliances and storage areas.</td> <td>https://www.edrawsoft.com/template/kitchen-design-diagram.png</td> <td>Open</td> </tr> </tbody> </table>										Drawing Name	Description	Google Drawing Url	Home Plan	A house plan is a set of construction or working drawings (sometimes still called blueprints) that define all the construction specifications of a residential house such as dimensions, materials, layouts, installation methods and techniques.	https://www.google.co.in/search?q=Home+Plan+Description&source=lms&tbo=isch&sa=X&ved=0ahUKEwipu8-thdbfAhUGbo8KHd4rCvkQ_AUDigB&cshid=1546670797476003&bih=1183&bth=583#imgrc=frXRZGlyHoHRIM	Open	Living Room Design	The living room is the place where friends and family gather to spend quality time in a home, so it's important for it to be well-designed	https://www.google.co.in/search?bih=1183&bth=583&tbo=isch&sa=1&ei=ilmwXPrGL4zPvgT-jHqCq&q=Living+Room+Plan&sq=Living+Room+Plan&gs_l=img.3..0i10.148294.153067..153373...0.0.0.146.1635.9j7.....1....1.gws-wiz-img.....3539j067.IDEgi4Jwr7o#imgrc=bD_MTGv6IepDZM	Open	Kitchen Plan	The kitchen layout is the shape that is made by the arrangement of the countertop, major appliances and storage areas.	https://www.edrawsoft.com/template/kitchen-design-diagram.png	Open
Drawing Name	Description	Google Drawing Url																						
Home Plan	A house plan is a set of construction or working drawings (sometimes still called blueprints) that define all the construction specifications of a residential house such as dimensions, materials, layouts, installation methods and techniques.	https://www.google.co.in/search?q=Home+Plan+Description&source=lms&tbo=isch&sa=X&ved=0ahUKEwipu8-thdbfAhUGbo8KHd4rCvkQ_AUDigB&cshid=1546670797476003&bih=1183&bth=583#imgrc=frXRZGlyHoHRIM	Open																					
Living Room Design	The living room is the place where friends and family gather to spend quality time in a home, so it's important for it to be well-designed	https://www.google.co.in/search?bih=1183&bth=583&tbo=isch&sa=1&ei=ilmwXPrGL4zPvgT-jHqCq&q=Living+Room+Plan&sq=Living+Room+Plan&gs_l=img.3..0i10.148294.153067..153373...0.0.0.146.1635.9j7.....1....1.gws-wiz-img.....3539j067.IDEgi4Jwr7o#imgrc=bD_MTGv6IepDZM	Open																					
Kitchen Plan	The kitchen layout is the shape that is made by the arrangement of the countertop, major appliances and storage areas.	https://www.edrawsoft.com/template/kitchen-design-diagram.png	Open																					

Send message Log note Schedule activity Following 3



❖ Google Drawing Image on Job Order or Task on My Account.

A screenshot of a customer portal interface. At the top, there's a navigation bar with "WEBSITE", "Pages", "Customize", "Promote", "My Website", "New", and "Edit" buttons. A message says "This is a preview of the customer portal. Back to edit mode". The main area shows a task titled "Flooring Works" (ID 37). The task details are as follows:

Start Date/Time	01/05/2019 08:00:06	Start Time	08:00:06
Stop Date/Time		Pause Time	
Status	In Progress	Stop Time	
Total Duration	00:01	Duration	00:01

Below the timeline, there are two buttons: "Pause" (green) and "Stop" (red).

A "Drawings" section lists three items:

Drawing Name	Drawing Description	Action
Home Plan	A house plan is a set of construction or working drawings (sometimes still called blueprints) that define all the construction specifications of a residential house such as dimensions, materials, layouts, installation methods and techniques.	Open
Living Room Design	The living room is the place where friends and family gather to spend quality time in a home, so it's important for it to be well-designed.	Open
Kitchen Plan	The kitchen layout is the shape that is made by the arrangement of the countertop, major appliances and storage areas.	Open



❖ My Portal Account to See Layout Plan on Job Orders.

A screenshot of a web-based portal interface. At the top, there is a navigation bar with links for "WEBSITE", "Pages", "Customize", "Promote", "My Website", "+ New", and "Edit". Below the navigation bar is a header section with a placeholder for "Your logo" and links for "Create Repair Request", "My Repair Request", "Create Workorder", "My Job Orders", "Home", "Projects", "Machine Repair", and "Mitchell Admin". The main content area displays a detailed floor plan of a house. The plan includes various rooms labeled with their dimensions: Dining Room (20' x 12'), Kitchen (10'9" x 20'11"), Living Room (17'4" x 20'3"), Master Suite (19'8" x 30'9"), Bedroom (12'11" x 14'9"), Bedroom (22'7" x 11'2"), Bedroom (22'7" x 11'2"), Library (11'3" x 12'6"), and a Covered Porch (20' x 18'9"). There is also a Deck and a Pool area. The entire layout is shown in a light gray background with black outlines for the rooms and furniture.



Employee Portal for Issue Tracking System

- ❖ Employee Portal See List of Project Issue in My Account.



- ❖ Display details of the issue and able to send reply of the customers reply of the posted issue.

SITE WEBSITE ▾ Pages Customize Promote

My Website ▾ + New Edit

Your logo Create Repair Request My Repair Request Create Workorder My Job Orders Home Projects Machine Repair + Mitchell Admin ▾

Your Issues ISSUE-00002

ISSUE-00002 - Damage Tiles and Low Quality Cement

Assigned to : Mitchell Admin
Email : admin@yourcompany.example.com
Issue Team : Painting Team
Department : Sales
Project: Construction of Hypol Heights
Create Date: 01/05/2019 06:42:28
Is Issue Closed?:
For Flooring work use low quality cement and damage tiles.
Send Message and Attachments

Customer: YourCompany, Mitchell Admin
Phone : +1 555-555-5555
Team Leader : Camron Grill
Analytic Account : Hypol Heights - The Jackson Group
Priority: Low
Close Date: 01/05/2019 08:29:51
Total Hours Spent: 0.0

Add a comment...
Choose Files No file chosen Send Now

Message and communication history

YourCompany, Mitchell Admin on 01/05/2019 08:29:55



Notes on My Account / Portal / Mobile / Tablets

❖ List of Project Notes on My Account.

The screenshot shows a web-based application interface for managing project notes. At the top, there's a navigation bar with links like 'WEBSITE', 'Pages', 'Customize', 'Promote', 'My Website', '+ New', and 'Edit'. Below the navigation is a header section with a placeholder 'Your logo' and a search bar. The main content area is titled 'Your Notes' and displays a table of notes. The table has columns for 'Note', 'Tags', 'Project', and 'Task'. There are four rows of data:

Note	Tags	Project	Task
Painting Layout	Painting	Construction of Hypol Heights	Painting Works
Interior Architect	Interior Architecture	Construction of Hypol Heights	Electrification
Project Initiation	Room Architecture	Construction of Hypol Heights	Project Initiation

At the bottom of the page, there are footer sections for 'Our Products & Services', 'Connect with us', and 'Your Company - About us'.



❖ Create or Modify Project Notes on My Account.

Screenshot of a web application interface for managing project notes. The top navigation bar includes links for WEBSITE, Pages, Customize, Promote, My Website, New, and Edit. The main content area shows a form titled 'My Notes' with fields for 'Project' (set to 'Construction of Hypol Heights') and 'Task' (set to 'Painting Works'). The 'Notes' section contains a rich text editor with a toolbar and the text 'Painting Layout'. Below the editor are 'Save', 'Delete', and 'Back' buttons. At the bottom, there's a footer with sections for 'Our Products & Services' (Home), 'Connect with us' (Contact us, phone +1 555 123 8069, email info@yourcompany.example.com, social media icons for Facebook, Twitter, LinkedIn, YouTube, Google+, and Instagram), and 'YourCompany - About us' (describing the company as a team of passionate people solving business problems). There's also a note about products being designed for small to medium size companies.




Job Drawing Image Construction and Contracting Business

- ❖ Project manager and project user to add Drawings image on Job Order. Add your drawings or layout of project part image on job order form. You can add multiple drawing image on job order form.

Job Orders / Flooring Works

	Starting Date	01/02/2019 11:00:42	Name	ready.mat55@example.com
	Ending Date	03/30/2019 11:30:42	Website Customer	
	Job Number	JOB/00006	Email	8989989989
			Website Customer	
			Phone	
			Job Order Category	New Request
Edit	Create	Print Action		
	Description	Job Instructions	Waste Materials	Material Plannings
	Timesheets	Extra Info	Timesheet Employee Users	Maintenance Equipment
	Google Drawing Document	Contract Drawing	Purchase Requisitions	Subtasks
	Drawing Name	Description	Drawing Image	
	Bed Room Plan	Bed Room Plan	66.24 Kb	Open
	Drawing Room Plan	Drawing Room Detail Layout	65.03 Kb	Open
	Kitchen Plan Layout	Kitchen Layout Description	65.03 Kb	Open

Send message [Log note](#) [Schedule activity](#) [Following](#) [3](#) [January 1, 2019](#)





❖ My Account Portal - Job Drawing on Job Orders

WEBSITE Pages Customize Promote My Website + New Edit

Your logo Create Repair Request My Repair Request Create Workorder My Job Orders Home Projects Machine Repair + Mitchell Admin

This is a preview of the customer portal. [Back to edit mode](#)

[Tasks / Flooring Works](#)

Flooring Works (437)		Status	
Start Date/Time	01/05/2019 08:00:06	Start Time	08:00:06
Stop Date/Time		Pause Time	08:17:54
Status	Paused	Stop Time	
Total Duration	00:24	Duration	00:24
Details Edit			

Contracting Drawings

Drawing Name	Drawing Description	Action
Bed Room Plan	Bed Room Plan	Open
Drawing Room Plan	Drawing Room Detail Layout	Open
Kitchen Plan Layout	Kitchen Layout Description	Open

WEBSITE Pages Customize Promote My Website + New Edit

Your logo Create Repair Request My Repair Request Create Workorder My Job Orders Home Projects Machine Repair + Mitchell Admin

Copyright © YourCompany [English](#) [Add a language...](#)



Dashboard for Project for Construction and Job Contracting

- ❖ Project dashboard provides glance data and metrics about the current status of your project with full details. A project management dashboard is a data dashboard that displays key performance indicators pertaining to specific projects.

Screenshot of the Odoo Project Management Dashboard:

The dashboard shows various project modules and their status:

- Project Dashboard:** A central area with search, filters, and group by options.
- Project Modules:**
 - AGR - SO022:** Documents, Settings, New Job Cost Sheets, New Job Orders, Job Cost Sheets, Job Orders, Timesheets, Material Cost Lines, Vendor Invoices, Overhead Cost Lines, Purchase Orders, Labour Cost Lines.
 - After-Sales Services:** Documents, Settings, New Job Cost Sheets, New Job Orders, Job Cost Sheets, Job Orders, Timesheets, Material Cost Lines, Vendor Invoices, Overhead Cost Lines, Purchase Orders, Labour Cost Lines.
 - CNC Machine:** Documents, Settings, New Job Cost Sheets, New Job Orders, Job Cost Sheets, Job Orders, Timesheets, Material Cost Lines, Vendor Invoices, Overhead Cost Lines, Purchase Orders, Labour Cost Lines.
 - Construction of Hypol Heights:** Documents, Settings, New Job Cost Sheets, New Job Orders, Job Cost Sheets, Job Orders, Timesheets, Material Cost Lines, Vendor Invoices, Overhead Cost Lines, Purchase Orders, Labour Cost Lines.
 - DPC - SO023:** Documents, Settings, New Job Cost Sheets, New Job Orders, Job Cost Sheets, Job Orders, Timesheets, Material Cost Lines, Vendor Invoices, Overhead Cost Lines, Purchase Orders, Labour Cost Lines.
 - Office Design:** Documents, Settings, New Job Cost Sheets, New Job Orders, Job Cost Sheets, Job Orders, Timesheets, Material Cost Lines, Vendor Invoices, Overhead Cost Lines, Purchase Orders, Labour Cost Lines.
 - Research & Development:** Documents, Settings, New Job Cost Sheets, New Job Orders, Job Cost Sheets, Job Orders, Timesheets, Material Cost Lines, Vendor Invoices, Overhead Cost Lines, Purchase Orders, Labour Cost Lines.




Project Team for Construction and Contracting

❖ Define Several Project Team with Different Members.

The screenshot shows the Odoo Job costing module interface. On the left, there's a list of 'Project Teams' with two entries: 'Construction of Himalaya Team' and 'Construction of Hypol Heights'. Each entry has a checkbox next to it and columns for 'Name', 'Code', and 'Project Manager'. The 'Code' column shows 'CHT' and '123' respectively. The 'Project Manager' column shows 'Andrew Smith' and 'Mitchell Admin'. At the top, there's a navigation bar with links like 'Jobs', 'Dashboard', 'Job Costs', etc. A search bar and filter options are also at the top. On the right, a sidebar menu is open, showing various reporting and configuration options. The 'Analytic Account' option is currently selected. Other visible items in the sidebar include 'Change Orders', 'Invoicing', 'Timesheets to Invoice', 'Reports', 'Issue Analysis', 'Costing Reports', 'Job Costing Column Trends', and 'Configuration'.



❖ Several Job Costsheet Related Values.

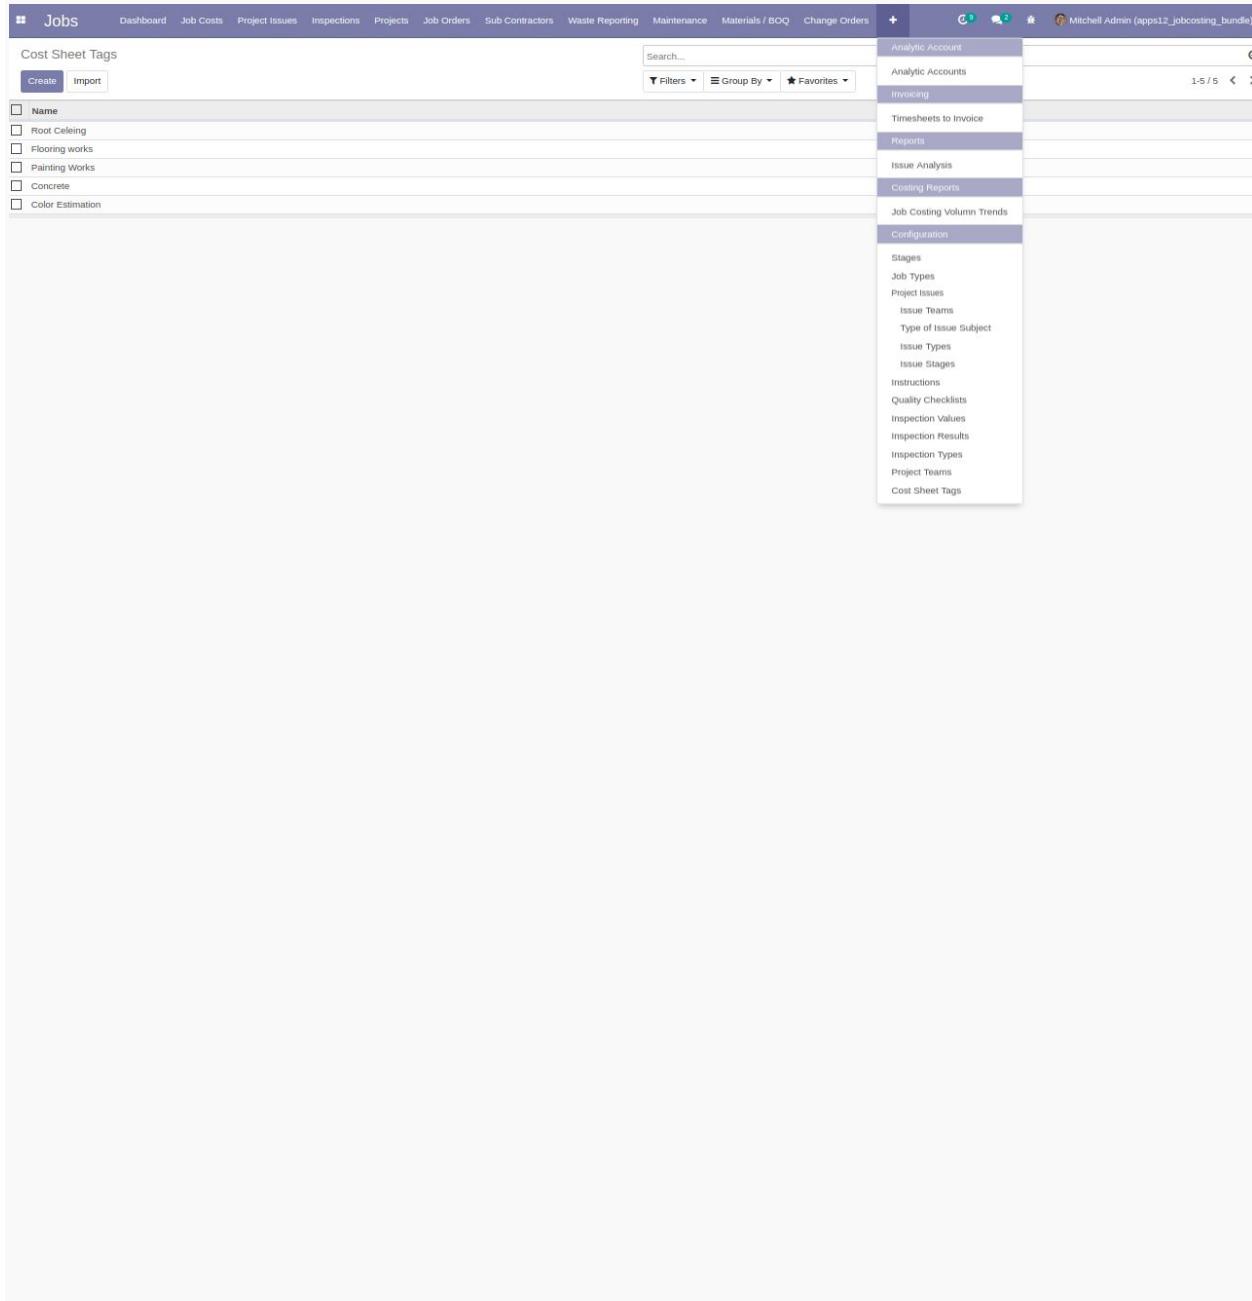

The screenshot shows the Odoo Job Costsheet Tags module. The top navigation bar includes links for Dashboard, Job Costs, Project Issues, Inspections, Projects, Job Orders, Sub Contractors, Waste Reporting, Maintenance, Materials / BOQ, Change Orders, and a plus sign for creating new entries. The user is identified as "Mitchell Admin (apps12_jobcosting_bundle)".

The main content area displays a list of "Cost Sheet Tags" with columns for Name, Type, and Description. A search bar and filter options are available at the top of the list. To the right, a sidebar lists various related modules and values:

- Analytic Account
- Analytic Accounts
- Invoicing
- Timesheets to Invoice
- Reports
- Issue Analysis
- Costing Reports
- Job Costing Column Trends
- Configuration
- Stages
- Job Types
- Project Issues
- Issue Teams
- Type of Issue Subject
- Issue Types
- Issue Stages
- Instructions
- Quality Checklists
- Inspection Values
- Inspection Results
- Inspection Types
- Project Teams
- Cost Sheet Tags



- ❖ Project - Project Team
- ❖ The people who participate actively in the project work. A successful project management team takes preparation and planning. Project team members are persons who work on one or multiple stages of a project. Team member roles will vary depending on the individual project with team members, security guards.

Jobs Dashboard Job Costs Project Issues Inspections Projects Job Orders Sub Contractors Waste Reporting Maintenance Materials / BOQ + Mitchell Admin (apps12_jobcosting_bundle)

Projects / Construction of Hypol Heights Print Action 4 / 7

[Edit](#) [Create](#)

[Share](#) [Create Sales Order](#)

Construction of Hypol Heights

Name of the tasks : Tasks
Allow timesheets

0 Documents	8 Tasks	Timesheets
Active	4 Jobcosts	8 Notes
Phases	More ▾	

[Settings](#) [Description](#) [Brochures](#) [Construction Site Detail](#) [More Project Images](#) [Gallery Images](#) [Project Features And Amenities](#) [Specification](#) [Contact Us](#)

[Project Floor Plan](#) [Project Location Plan](#) [Timesheet Employee Users](#) [Project Team](#)

Project Team	Construction of Himalaya Team
Project Manager	Andrew Smith
Privacy	Visible by following customers
Customer	Azure Interior
Analytic Account	Hypol Heights - The Jackson Group
Code	
Price / Rate	55,000,000.00
(Company Currency)	[Deposit] Deposit
Product	
Reference	No rating
Customer(s) Ratings	
Sub-task Project	Construction of Hypol Heights



Jobs Dashboard Job Costs Project Issues Inspections Projects Job Orders Sub Contractors Waste Reporting Maintenance Materials / BOQ Change Orders +

C 3 2 1 * Mitchell Admin (apps12_jobcosting_bundle)

Projects / Construction of Hypol Heights

Edit Create Print Action

4 / 7 < >

Settings	Description	Brochures	Construction Site Detail	More Project Images	Gallery Images	Project Features And Amenities	Specification	Contact Us
Project Floor Plan	Project Location Plan	Timesheet	Employee Users	Project Team				
Site Engineer / Supervisor	John Abraham							
Team Members								
Name	Login	Language	Latest connection					
Camron Grill	camron.grill	English						
John Abraham	john.abraham	English						
Mikal Jakson	mikal.jakson	English						
Store Officers								
Name	Login	Language	Latest connection					
Marc Demo	demo	English						
Mikal Jakson	mikal.jakson	English						
Willim Johns	willim.johns	English						
Security Guards								
Name	Login	Language	Latest connection					
Joel Willis	portal	English						
John Abraham	john.abraham	English						
Peter Parker	peter.parker	English						



- ❖ Job Costsheet Tags
- ❖ Job cost sheet is prepared for each job on which direct material, direct labour and overhead expenses.

Jobs Dashboard Job Costs Project Issues Inspections Projects Job Orders Sub Contractors Waste Reporting Maintenance Materials / BOQ Change Orders + C E M * Mitchell Admin (apps12_jobcosting_bundle)

Job Cost Sheets / COST-SHEET/00001

[Edit](#) [Create](#) [Print](#) [Action](#)

[Confirm](#) [Create Estimation](#) [Cancel](#) [Draft](#) [Confirmed](#) [Done](#)

COST-SHEET/00001

Name		New	Create Date		01/01/2019										
Project	Construction of Hypol Heights	Project Team	Construction of Hypol Heights	Created By	Mitchell Admin										
Tags	Flooring works, Painting Works, Color Estimation	Analytic Account	Hypol Heights - The Jackson Group	Company	YourCompany										
Job Order	Project Initiation	Currency	USD	Description	Sale Reference										
Customer	Lumber Inc	Customer Invoice		Purchased	Customer Invoice										
				Billable Method											
				Based On Actual Vendor Bill Qty											
Materials		Labours		Overhead											
Date	Job Type	Product	Description	Reference	Planned Qty Uom	Cost / Unit	Sale Price / Unit	Actual Requisition Quantity	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Actual Cost Price	Manual Invoiced Sub Total	Cut Qty
01/01/2019	Site-Preparation-MAT	Cement	Cement		50.00 Unit(s)	350.00	400.00	50.00	200.00	70,000.00	40.00	800.00	\$ 17,500.00	0.00	
01/02/2019	Site-Preparation-MAT	Bricks	Bricks		2,000.00 Unit(s)	10.00	15.00	2,000.00	2,000.00	20,000.00	30.00	900.00	\$ 20,000.00	0.00	
01/03/2019	Site-	Tiles	Tiles		500.00 Unit(s)	40.00	45.00	500.00	570.00	25,400.00	200.00	12,000.00	\$ 20,000.00	0.00	



- ❖ Job Order / Task - Project Team
- ❖ Resolves issues escalated by the project manager or project team leads.

Jobs Dashboard Job Costs Project Issues Inspections Projects Job Orders Sub Contractors Waste Reporting Maintenance Materials / BOQ Change Orders + C 1 2 * Mitchell Admin (apps12_jobcosting_bundle)

Job Orders / Flooring Works

Edit Create Print Action Share Create Subtasks Create Subcontractor Job Create Repair Request Create / Edit Cost Sheet Send by Email 10 / 13 < >

JOB/0004

Flooring Works

Project Construction of Hypol Heights Project Phase Flooring Works Assigned to Mitchell Admin Project Team Construction of Hypol Heights Sales Order Item Starting Date 01/02/2019 11:00:42 Ending Date 03/30/2019 11:30:42 Job Number JOB/00006	Deadline 05/30/2019 Tags Flooring Website Customer Ready Mat Website Customer Name ready.matt5@example.com Website Customer Email 8989989989 Website Customer Phone Job Order Category New Request	0 Sub-tasks Active 2 Jobcosts 0 Stock Moves 0 Notes Subcontractor Jobs 0 Purchase Re... More ▾
--	---	---

[Description](#) [Job Instructions](#) [Waste Materials](#) [Material Planning](#) [Website](#) [Purchase Requisitions](#) [Subtasks](#) [Consumed Materials](#) [Material Requisitions](#)
[Timesheets](#) [Extra Info](#) [Timesheet Employee Users](#) [Maintenance Equipment](#) [Maintenance Requests](#) [Work Duration](#) [Customer Signature](#)
[Google Drawing Document](#) [Contract Drawing](#) [Project Team](#)

Flooring is any permanent covering of a floor, or the work of installing such a floor covering.
Floor covering is a term to generically describe any finish material applied over a floor structure to provide a walking surface.
Both terms are used interchangeably but floor covering refers more to loose-laid materials.



Document Management for Job Contracting and Construction

- ❖ To Define Parent Directories for manage documents and file.

The screenshot shows the Odoo interface for managing documents. On the left, a list of 'Parent Directories' is displayed with columns for 'Directory Name' and 'Model'. The list includes:

Directory Name	Model
Painting Works - Hypol Heights	Job Instruction
Flooring works Hypol Heights	Task
Other Documents	

On the right, a sidebar menu is open, showing a tree structure of document management categories. The 'Documents' category is currently selected. Other visible categories include Timesheets to Invoice, Reports, Issue Analysis, Costing Reports, Job Costing Volumn Trends, and Configuration. Under Configuration, further sub-options like Stages, Job Types, Project Issues, and Issue Teams are listed.



- ❖ Define Directories for maintaining documents of different construction activity.

A screenshot of the Odoo application interface, specifically the 'Jobs' module. The top navigation bar includes links for Dashboard, Job Costs, Project Issues, Inspections, Projects, Job Orders, and Sub Contractors. A sidebar on the right shows a user profile for 'Mitchell Admin (apps12_jobcosting_bundle)'. The main content area displays a table titled 'Directories' with columns for Directory Name, Model, Parent Directory, and Tags. Two entries are listed: 'Hypol Heights' (Project, Other Documents, Tags: Electrical Works, Painting Works, Roofing) and 'Himalya Elanza' (Job Costing, Other Documents, Tags: Electrical Works, Painting Works, Lab). A search bar and filter dropdown are also visible. A vertical sidebar on the right lists various configuration options under 'Configuration', such as Timesheets to Invoice, Reports, Issue Analysis, Costing Reports, Job Costing Volumn Trends, Documents, Directories, Parent Directories, Directories, All Documents, My Documents, Stages, Job Types, Project Issues, Issue Teams, Type of Issue Subject, Issue Types, Issue Stages, Instructions, and Quality Checklists.



❖ My Documents Related System.

Screenshot of a document management system interface:

The top navigation bar includes: Jobs, Dashboard, Job Costs, Project Issues, Inspections, Projects, Job Orders, Sub Contractors, +, C (with notifications), a message icon, a star icon, and Mitchell Admin (apps12_jobcosting_bundle).

The main area shows three document lists:

- Hypol Heights**:
 - laboursheet.jpeg (Message : ISSUE-00002, 01/05/2019)
 - costsheet12.jpg (Message : ISSUE-00002, 01/05/2019)
 - 27_cs_overhead.png (01/04/2019)
 - Electrical Work (Module : Timesheets Sheet for Employee, 12/31/2018)
 - Overhead Work (Module : Employee Portal for Issue Tracking, 12/31/2018)
- Painting Works - Hypol Heights**:
 - Painting Work (Module : Customer Invoice from Job Order, 12/31/2018)
 - Construction Report.pdf (Message : ISSUE-00002, 01/05/2019)
- Undefined**:
 - 17_pr_mptab.png (01/05/2019)
 - image.jpg (Module : Meeting Minutes for Construction, 12/31/2018)
 - img1.png (Module : Project by Phases, 12/31/2018)
 - img1.jpeg (Module : Issue Tracking System for Construction, 12/31/2018)
 - img1.jpg (Module : Job Order / Work Order Integration, 12/31/2018)

Buttons at the top right include: Directory, Search, Filters, Group By, Favorites, Add a Column, and a grid/list view switcher.



❖ All Documents Related System.

The screenshot shows a document management interface with three main categories:

- Hypol Heights:**
 - laboursheet.jpeg (Message : ISSUE-00002, 01/05/2019)
 - costsheet12.jpg (Message : ISSUE-00002, 01/05/2019)
 - 27_cs_overhead.png (01/04/2019)
 - Electrical Work (Module : Timesheets Sheet for Emplo..., 12/31/2018)
 - Overhead Work (Module : Employee Portal for Issue T..., 12/31/2018)
- Painting Works - Hypol Heights:**
 - Construction Report.pdf (Message : ISSUE-00002, 01/05/2019)
 - Painting Work (Module : Customer Invoice from Job ..., 12/31/2018)
- Undefined:**
 - web.assets_backend.js (View, 01/05/2019)
 - web.assets_backend.1.css (View, 01/05/2019)
 - web.assets_backend.0.css (View, 01/05/2019)
 - web.assets_frontend.js (View, 01/05/2019)
 - web.assets_frontend.1.css (View, 01/05/2019)

❖ Job Costsheet Related Documents are linked.

The screenshot shows a document management interface for a specific job cost sheet:

Job Cost Sheets / COST-SHEET/00001 / Attachments

File	Description	Date
11.jpg	Job Costing : COST-SHEET/00001	01/05/2019
costsheet12.jpg	Job Costing : COST-SHEET/00001	01/05/2019
costsheet12.jpg	Job Costing : COST-SHEET/00001	01/05/2019



❖ List of Directory in Portal My Account.

Screenshot of a website interface showing a "Directory" section. The top navigation bar includes "WEBSITE ▾", "Pages", "Customize", "Promote", "My Website ▾", "+ New", and "Edit".

The "Directory" section has a "No title" header and a search bar labeled "Search for name...".

Content items listed under "Directory":

- #
- [Hypol Heights](#)
- [Painting Works - Hypol Heights](#)
- [Flooring works Hypol Heights](#)
- [Himalaya Blanza](#)
- [Other Documents](#)

Footer links include "Our Products & Services", "Connect with us", and "Your Company ▾ About us".



Transmittals / Submittals for Construction and Contracting

❖ Transmittal and Submittal Type Configuration.

The screenshot displays the Probuse software interface for managing construction and contracting. The top navigation bar includes links for Jobs, Dashboard, Job Costs, Project Issues, Inspections, Projects, Job Orders, Sub Contractors, Waste Reporting, and Maintenance. A user profile for 'Mitchell Admin' is shown on the right, along with notifications for 9 messages and 2 comments. The main content area is titled 'Transmittals / Submittals for Construction and Contracting'. On the left, a 'Types' section allows users to create or import new entries, with checkboxes for 'Name', 'Bill', 'Contract', 'Agreement', and 'Statement of Work'. On the right, a detailed configuration menu is open, listing various submittal types and related settings. The configuration menu includes sections for Stages, Job Types, Project Issues, Issue Teams, Type of Issue Subject, Issue Types, Issue Stages, Transmittal / Submittal (with sub-options for Types, Mediums, Instructions, Quality Checklists, Inspection Values, Inspection Results, Inspection Types, Project Teams, Cost Sheet Tags, Documents, Directory Tags, and Document Tags), and a search bar at the top right.



❖ Transmittal and Submittal Medium Configuration.

Screenshot of the Probuse software interface showing the "Mediums" configuration screen.

The top navigation bar includes: Jobs, Dashboard, Job Costs, Project Issues, Inspections, Projects, Job Orders, Sub Contractors, Waste Reporting, Maintenance, a plus sign for creating new items, a search bar, a notifications icon (0), a user profile for Mitchell Admin, and a dropdown menu for Configuration.

The main content area displays a list of Mediums:

Name
Courier
Email
Post
Transport

Below the list are buttons for Create and Import, and filter options: Search..., Filters, Group By, and Favorites.

The right sidebar lists various configuration categories:

- Configuration
- Stages
- Job Types
- Project Issues
- Issue Teams
- Type of Issue Subject
- Issue Types
- Issue Stages
- Transmittal / Submittal
 - Types
 - Mediums
 - Instructions
 - Quality Checklists
 - Inspection Values
 - Inspection Results
 - Inspection Types
 - Project Teams
 - Cost Sheet Tags
 - Documents
 - Directory Tags
 - Document Tags



- ❖ A transmittal document is a kind of packing slip for a document or collection of documents that are transferred from one company to another.

Jobs Dashboard Job Costs Project Issues Inspections Projects Job Orders Sub Contractors Waste Reporting Maintenance + G 9 2 Mitchell Admin

Transmittals / TRANSMITTAL/00001

[Edit](#) [Create](#) [Print](#) [Action](#)

[Send by Email](#)

[New](#)

TRANSMITTAL/00001

Contract Agreement

Project	Construction of Hypol Heights	Date of Sending	01/05/2019
Analytic Account	Hypol Heights - The Jackson Group	Deadline	
Job Order	Project Initiation	Sender Company	Camron Grill
Job Costsheet	COST-SHEET/00001	Receiver Company	
Document Type	Transmittal	Responsible User	Mitchell Admin
		Company	YourCompany

Information	Reason for Sending	Description Taken by Recipient	
Contract Detail	Contract	Courier	Send Contract Detail of Project
Flooring works	Agreement	Transport	Send Flooring related materials
Painting Works	Bill	Courier	Send Painting Bill and Booklet through Transport.

Transmittals
Submittals
Materials
Change Orders
Analytic Accounts
Timesheets to Invoice
Issue Analysis
Job Costing Volumn
Directories

1 / 1 [New](#) [Sent](#) [Refused](#)



- ❖ Submittals Documents are required primarily for the submitting the document to verify.

Screenshot of a software interface titled "Jobs". The top navigation bar includes links for Dashboard, Job Costs, Project Issues, Inspections, Projects, Job Orders, Sub Contractors, Waste Reporting, Maintenance, and user "Mitchell Admin".

The main content area shows a submittal titled "SUBMITTAL/00001" for an "Architectural Layout Plan".

Details for the submittal:

Project	Construction of Hypol Heights	Date of Sending	01/05/2019
Analytic Account	Hypol Heights - The Jackson Group	Deadline	01/31/2019
Job Order	Project Initiation	Sender Company	Andrew Smith
Job Costsheet	COST-SHEET/00001	Receiver Company	Mitchell Admin
Document Type	Submittal	Responsible User	YourCompany

Below the details is a table showing the "Reason for Sending" and "Description Taken by Recipient" for different layout types:

Name	Type	Channel	Description
Plan Layout	Statement of Work	Email	Send Plan Layout
Flooring Work Layout	Contract	Courier	Send Flooring Related Docs
Painting Layout	Agreement	Post	Send Painting Color Docs.



Construction and Contracting with Equipment & Maintenance

❖ Equipment Quality Checklist.

A screenshot of a software application window titled "Jobs". The main content area displays a list of "Quality Checklists" with columns for "Name" and "Code". The "Name" column lists tasks like "Molding Check", "Oil Check", "Site Cleaning", etc., each preceded by a checkbox. The "Code" column lists corresponding codes: "Molding Check", "Oil Checking", "SC", "FW", "PW", and "ELE-WRK". On the right side of the screen, a vertical sidebar menu is open, showing a list of configuration options such as "Parent Directories", "Directories", "All Documents", "My Documents", "Configuration" (which is highlighted in blue), "Stages", "Job Types", "Project Issues", "Issue Teams", "Type of Issue Subject", "Issue Types", "Issue Stages", "Transmittal / Submittal", "Types", "Mediums", "Instructions", "Quality Checklists", "Inspection Values", "Inspection Results", "Inspection Types", "Project Teams", "Cost Sheet Tags", "Documents", "Directory Tags", and "Document Tags".

Name	Code
<input type="checkbox"/> Molding Check	Molding Check
<input type="checkbox"/> Oil Check	Oil Checking
<input type="checkbox"/> Site Cleaning	SC
<input type="checkbox"/> Flooring Works	FW
<input type="checkbox"/> Painting Works	PW
<input type="checkbox"/> Electrical Works	ELE-WRK



❖ Maintenance Equipment with maintenance material plan.

Screenshot of a software interface showing a 'Floor Removal Surface Tools' maintenance equipment record.

Header: Jobs, Dashboard, Job Costs, Project Issues, Inspections, Projects, Job Orders, Sub Contractors, Waste Reporting, Maintenance, +, Mitchell Admin.

Breadcrumbs: Equipments / Floor Removal Surface Tools

Buttons: Edit, Create, Action ▾, 13 / 13, < >

Section Header: Floor Removal Surface Tools

Equipment Category: Painting

Maintenance Team: Subcontractor

Company: YourCompany

Technician: Mitchell Admin

Used By: Employee

Used in location: Job Order

Employee: Eli Lambert

Status: 0 Maintenance, Active

Product Details:

Product	Quantity	UOM
Tiles	56.00	Unit(s)
Cement	35.00	Unit(s)
White Cement	50.00	Unit(s)

Actions: Send message, 1 no note, 0 Schedule activity, ✓ Following, 1 user



❖ Maintenance Request with maintenance equipment checklists.

Maintenance Requests / Floor Removal Surface Tools

Created By	Mitchell Admin	Team	Internal Maintenance																		
Company	YourCompany	Responsible	Marc Demo																		
Equipment	HP Laptop/PLP/303/28292090	Scheduled Date																			
Category	Computers	Duration	00:00 hours																		
Request Date	01/05/2019	Priority	☆☆☆																		
Maintenance Type	Corrective	Job Order																			
		Destination Location	Partner Locations/Vendors																		
		Material Requisition	Audrey Peterson																		
	<th>Employee</th> <td></td>	Employee																			
<input type="button" value="Edit"/> <input type="button" value="Create"/> <input type="button" value="Print"/> <input type="button" value="Action"/> 6 / 6																					
<input type="button" value="Cancel"/> <input type="button" value="Create Job Order"/> <input type="button" value="Create Material Requisition"/>		<input type="button" value="New Request"/> <input type="button" value="In Progress"/> <input type="button" value="Repaired"/> <input type="button" value="Scrap"/>																			
Floor Removal Surface Tools <table border="1"> <thead> <tr> <th>Maintenance Plan Materials</th> <th>Maintenance Equipment Checklists</th> </tr> </thead> <tbody> <tr> <th>Product</th> <th>Description</th> <th>Quantity</th> <th>UOM</th> </tr> <tr> <td>Chair floor protection</td> <td>Chair floor protection</td> <td>2.00</td> <td>Unit(s)</td> </tr> <tr> <td>Hammer</td> <td>Hammer</td> <td>5.00</td> <td>Unit(s)</td> </tr> <tr> <td>Dust Collection</td> <td>Dust Collection</td> <td>5.00</td> <td>Unit(s)</td> </tr> </tbody> </table>				Maintenance Plan Materials	Maintenance Equipment Checklists	Product	Description	Quantity	UOM	Chair floor protection	Chair floor protection	2.00	Unit(s)	Hammer	Hammer	5.00	Unit(s)	Dust Collection	Dust Collection	5.00	Unit(s)
Maintenance Plan Materials	Maintenance Equipment Checklists																				
Product	Description	Quantity	UOM																		
Chair floor protection	Chair floor protection	2.00	Unit(s)																		
Hammer	Hammer	5.00	Unit(s)																		
Dust Collection	Dust Collection	5.00	Unit(s)																		



Work Package for Construction and Contracting

- ❖ Send Work Package to your customers for your construction and contracting business. Packaging is normally associated with general contractors who split a large project into a series of work packages suitable for obtaining tenders.

Screenshot of a software interface for managing work packages in a construction environment:

The top navigation bar includes: Jobs, Dashboard, Job Costs, Project Issues, Inspections, Projects, Job Orders, Sub Contractors, Waste Reporting, +, and user information (Mitchell Admin (apps12_jobcosting_bundle)).

The main title is "Work Packages / Ground Flooring Works". Below it are buttons for Edit, Create, Send by Email, Confirm, and Cancel.

A dropdown menu shows options: Job Orders, Job Notes, Job Instructions, and Work Packages (selected).

On the right, status indicators show 1/1 Draft, Confirmed, and Sent.

The central area displays a "JOB/PACKAGE/0001" card with the following details:

Name	Ground Flooring Works	Date	01/05/2019
Project	Construction of Hypol Heights	Responsible User	Mitchell Admin
Customer	Andrew Smith	Company	YourCompany

Below this is a table titled "Work Package Lines" showing the following data:

Number	Name	Assigned to	Starting Date	Ending Date	Planned Hours	Remaining Hours
Project Initiation	Mitchell Admin	12/25/2018 18:13:23	01/31/2019 11:12:56		40.00	16.00
JOB/00006	Flooring Works	Mitchell Admin	01/02/2019 11:00:42	03/30/2019 11:30:42	0.00	-16.00
JOB/00005	Electrification	Mitchell Admin	01/01/2019 11:00:22	02/28/2019 12:00:41	0.00	0.00
JOB/00004	Painting Works	Mitchell Admin	01/01/2019 10:59:34		0.00	-8.00

At the bottom of the card are buttons for Send message, Log note, Schedule activity, Following, and a user count of 1.

The footer of the page includes a "Today" button and other navigation links.



Repair App for Construction and Contracting

- ❖ We Create Repair Request for any equipment/machine/item for job order of your construction and job contracting business on job order / task / work order.

Jobs Dashboard Job Costs Project Issues Inspections Projects Job Orders Sub Contractors Waste Reporting + C ⏱ 📁 ⚙ Mitchell Admin (apps12_jobcosting_bundle)

Job Orders / Flooring Works Edit Create Print Action 10 / 13 < >

Share Create Subtasks Create Subcontractor Job Create Repair Request Create / Edit Cost Sheet Send by Email

JOB/0004		Flooring Works											
Project	Construction of Hypol Heights	Deadline	05/30/2019										
Project Phase	Flooring Works	Tags	Flooring										
Assigned to	Mitchell Admin	Website Customer	Ready Mat										
Project Team	Construction of Hypol Heights	Website Customer Name	Ready Mat										
Sales Order Item		Email	ready.mat55@example.com										
Starting Date	01/02/2019 11:00:42	Website Customer Phone	8989989989										
Ending Date	03/30/2019 11:30:42	Job Order Category	New Request										
Job Number	JOB/00006												
<table border="1"> <tr> <td>0 Sub-tasks</td> <td>Active</td> <td>2 Jobcosts</td> </tr> <tr> <td>Stock Moves</td> <td>0 Notes</td> <td>Subcontractor Jobs</td> </tr> <tr> <td colspan="2">Purchase Re...</td> <td>More ▾</td> </tr> </table>					0 Sub-tasks	Active	2 Jobcosts	Stock Moves	0 Notes	Subcontractor Jobs	Purchase Re...		More ▾
0 Sub-tasks	Active	2 Jobcosts											
Stock Moves	0 Notes	Subcontractor Jobs											
Purchase Re...		More ▾											
Description Job Instructions Waste Materials Material Plannings Website Purchase Requisitions Subtasks Consumed Materials Material Requisitions Timesheets Extra Info Timesheet Employee Users Maintenance Equipment Maintenance Requests Work Duration Customer Signature													



- ❖ Need to create repair request for some equipment on wizard from Job Order.

Create Repair Request

This wizard will Create Repair Requests for Job Order.

Customer: Azure Interior

Product	Repair Description	Repair Team	Repair Responsible	Nature of Service	Repair Type	Lot	Problem
Tiles Cutting	Tiles Cutter	Flooring works	Andrew Smith	Cutting	(Cutting)	LOT-000001	Cutting Work
Paint Brush	Brush	Paint Brush	Camron Grill	Paint Brush	(Brush)	LOT-000001	Brush Shining
Handheld Machine	Handheld Machine	Flooring works	John Abraham	Cutting	(Cutting)	LOT-000001	Handheld Machine

Add a line


Buttons: Create Repair Request or Cancel

Job Order Details:

Starting Date	01/02/2019 11:00:42	Email	
Ending Date	03/30/2019 11:30:42	Website Customer	8989989989
Job Number	JOB/00006	Phone	
		Job Order Category	New Request

Job Order Lines:

Description	Job Instructions	Waste Materials	Material Plannings	Website	Purchase Requisitions	Subtasks	Consumed Materials	Material Requisitions
Timesheets	Extra Info	Timesheet Employee Users	Maintenance Equipment	Maintenance Requests	Work Duration	Customer Signature		





❖ Created Repair Request on Job Order.

Screenshot of a software interface showing a list of Job Orders under the "Machine Repair" category. The interface includes a navigation bar with links like Jobs, Dashboard, Job Costs, Project Issues, Inspections, Projects, Job Orders, Sub Contractors, Waste Reporting, and a user profile for "Mitchell Admin (apps12_jobcosting_bundle)".

The main content area displays three job orders:

- RO-00007**
Handheld Machine
John Abraham
01/05/2019 18:14:33
New :
- RO-00006**
Brush
Cameron Grill
01/05/2019 18:14:33
New :
- RO-00005**
Tiles Cutter
Andrew Smith
01/05/2019 18:14:33
New :

At the top of the list view, there are search and filter options, as well as a page navigation indicator showing "1-3 / 3".



Waste Management for Construction and Contracting

- ❖ Job order user to add Waste Materials on Job Order form and based on that create Internal Picking or Stock Scrap based on waste method selected.

Jobs Dashboard Job Costs Project Issues Inspections Projects Job Orders Sub Contractors Waste Reporting Maintenance Transmittals + Mitchell Admin (apps12_jobcosting_bundle)

Job Orders / Flooring Works Print Action 10 / 13

JOB/0004		Flooring Works								
	Project	Construction of Hypol Heights	Deadline	05/30/2019		0 Sub-tasks		Active		2 Jobcosts
	Project Phase	Flooring Works	Tags	Flooring		0 Stock Moves		0 Notes		Subcontractor
	Assigned to	Mitchell Admin	Website Customer	Ready Mat		Jobs				
	Project Team	Construction of Hypol Heights	Name	Ready Mat						
	Sales Order Item		Email	ready.mat55@example.com						
	Starting Date	01/02/2019 11:00:42	Website Customer							
	Ending Date	03/30/2019 11:30:42	Phone	8989898989						
	Job Number	JOB/00006	Job Order Category	New Request						
		Description	Job Instructions	Waste Materials	Material Planning	Website	Purchase Requisitions	Subtasks	Consumed Materials	Material Requisitions
		Timesheets	Extra Info	Timesheet Employee Users	Maintenance Equipment		Maintenance Requests	Work Duration	Customer Signature	
		Google Drawing	Document	Contract Drawing	Project Team					
		Waste Method	Product	Quantity	UOM	Source Location	Destination Location	Picking Type		
		Reuse Material	Cement	25	Unit(s)	Partner Locations/Customers	Partner Locations/Vendors	Chicago Warehouse: Receipts	Create	
		Scrap Material	Tiles	50	Unit(s)	Partner Locations/Customers	Partner Locations/Vendors	Chicago Warehouse: Receipts	Create	
		Scrap Material	Bricks	40	Unit(s)	Partner Locations/Customers	Partner Locations/Vendors	Chicago Warehouse: Receipts	Create	



❖ Scraps Material are generated from Job Orders.

Jobs Dashboard Job Costs Project Issues Inspections Projects Job Orders Sub Contractors Waste Reporting Maintenance Transmittals +

Job Orders / Flooring Works / Scrap Orders

Create Import Search... Filters Group By Favorites 1-2 / 2


Reference	Create Date	Product	Quantity	Unit of Measure	Location	Scrap Location	Status
SP/00002	01/05/2019 18:26:21	Bricks	40.00	Unit(s)	WH/Stock	Virtual Locations/Scrapped	Draft
SP/00001	01/05/2019 18:26:17	Tiles	50.00	Unit(s)	WH/Stock	Virtual Locations/Scrapped	Draft



❖ Internal Picking are Generated from Job Order

Screenshot of a software interface showing a list of job orders. The top navigation bar includes links for Jobs, Dashboard, Job Costs, Project Issues, Inspections, Projects, Job Orders, Sub Contractors, Waste Reporting, Maintenance, Transmittals, and a user profile for Mitchell Admin. The main content area shows a table with the following data:

Reference	Destination Location	Partner	Scheduled Date	Source Document	Back Order of	Status
ChicIN/00006	Partner Locations/Vendors	Azure Interior	01/05/2019 18:26:12			Draft





- ❖ Generate the Waste Material Reports During Construction Cost sheets.

Material Wastes											Waste Reporting		
	Name	Project	Job Order	Product	Quantity	UOM	Source Location	Destination Location	Waste Method	Stock Scrap	Picking	User	Company
<input type="checkbox"/>	CONSTRUCTION/WASTE/00009	Construction of Hypol Heights	Electrification	Circuits	40	Unit(s)	Partner Locations/Customers	Partner Locations/Vendors	Reuse Material			Mitchell Admin	YourCompa
<input type="checkbox"/>	CONSTRUCTION/WASTE/00008	Construction of Hypol Heights	Electrification	Switch Borad	50	Unit(s)	Partner Locations/Customers	Partner Locations/Vendors	Reuse Material			Mitchell Admin	YourCompa
<input type="checkbox"/>	CONSTRUCTION/WASTE/00007	Construction of Hypol Heights	Electrification	Wires	50	Unit(s)	Partner Locations/Customers	Partner Locations/Vendors	Scrap Material			Mitchell Admin	YourCompa
<input type="checkbox"/>	CONSTRUCTION/WASTE/00006	Construction of Hypol Heights	Flooring Works	Cement	25	Unit(s)	Partner Locations/Customers	Partner Locations/Vendors	Reuse Material			ChicIN/00006	Mitchell Admin YourCompa
<input type="checkbox"/>	CONSTRUCTION/WASTE/00005	Construction of Hypol Heights	Flooring Works	Tiles	50	Unit(s)	Partner Locations/Customers	Partner Locations/Vendors	Scrap Material	SP/00001		Mitchell Admin	YourCompa
<input type="checkbox"/>	CONSTRUCTION/WASTE/00004	Construction of Hypol Heights	Flooring Works	Bricks	40	Unit(s)	Partner Locations/Customers	Partner Locations/Vendors	Scrap Material	SP/00002		Mitchell Admin	YourCompa
<input type="checkbox"/>	CONSTRUCTION/WASTE/00003	Construction of Hypol Heights	Project Initiation	Bricks	1	Unit(s)	Partner Locations	Partner Locations/Vendors	Scrap Material			Mitchell Admin	YourCompa
<input type="checkbox"/>	CONSTRUCTION/WASTE/00002	Construction of Hypol Heights	Project Initiation	Iron	1	Unit(s)	Partner Locations/Customers	Partner Locations/Vendors/IT Vendors	Scrap Material			Mitchell Admin	YourCompa
<input type="checkbox"/>	CONSTRUCTION/WASTE/00001	Construction of Hypol Heights	Project Initiation	Bricks	1	Unit(s)	Partner Locations/Customers	Partner Locations/Vendors	Reuse Material			Mitchell Admin	YourCompa



Job Costing / Contracting Volumn Trends Report.


❖ Cost Reporting of Job Costing Cost Trends.

Screenshot of the Probuse software interface showing the 'Job Costing Column Trends' report. The report displays a detailed breakdown of costs across various categories like Bricks, Cement, Door, Electricity Bill, etc., comparing Actual Purchased Cost, Actual Timesheet Cost, and Actual Vendor Bill Cost. The interface includes a navigation bar with 'Jobs', 'Dashboard', 'Job Costs', 'Project Issues', 'Inspections', 'Projects', 'Job Orders', 'Sub Contractors', 'Waste Reporting', 'Maintenance', and 'Transmittals'. On the right, there are several tabs: 'Costing Reports', 'Documents', 'Directories', 'Configuration', and others. A sidebar on the right lists various configuration items with their values.

	+ Total	Count	Actual Purchased Cost	Actual Timesheet Cost	Actual Vendor Bill Cost	Planned Quantity	Purchase Quantity	Requisition
- Total	47	1,038,375.00	3,000.00	306,650.00	15,730.00	8,487.00		
- January 2019	47	1,038,375.00	3,000.00	306,650.00	15,730.00	8,487.00		
- COST-SHEET/00001	46	1,038,375.00	3,000.00	306,650.00	15,729.00	8,487.00		
+ [EXP_C1] Car Travel Expenses	1	500.00	0.00	500.00	1.00	1.00		
+ Bricks	2	40,000.00	0.00	1,800.00	4,000.00	4,000.00		
+ Cement	4	280,000.00	0.00	3,200.00	200.00	402.00		
+ Door	1	2,500.00	0.00	50,000.00	25.00	1.00		
+ Electricity Bill	1	2,500.00	0.00	2,500.00	1.00	1.00		
+ Ground Floor Wages	6	0.00	3,000.00	0.00				
+ Iron	2	200,000.00	0.00	3,150.00	1,000.00	1,000.00		
+ Tiles	20	508,000.00	0.00	240,000.00	10,000.00	2,855.00		
+ Tiles Feeling	1	0.00	0.00	0.00				
+ Truck Rent	1	1,000.00	0.00	1,000.00	1.00	1.00		
+ Waterproofing	1	0.00	0.00	0.00				
+ White Cement	5	3,375.00	0.00	4,000.00	500.00	225.00		
+ Wiring Works	1	500.00	0.00	500.00	1.00	1.00		
- COST-SHEET/00003	1	0.00	0.00	0.00	1.00			
+ Cement	1	0.00	0.00	0.00	1.00			



❖ Pie Chart or Graph View in Report.

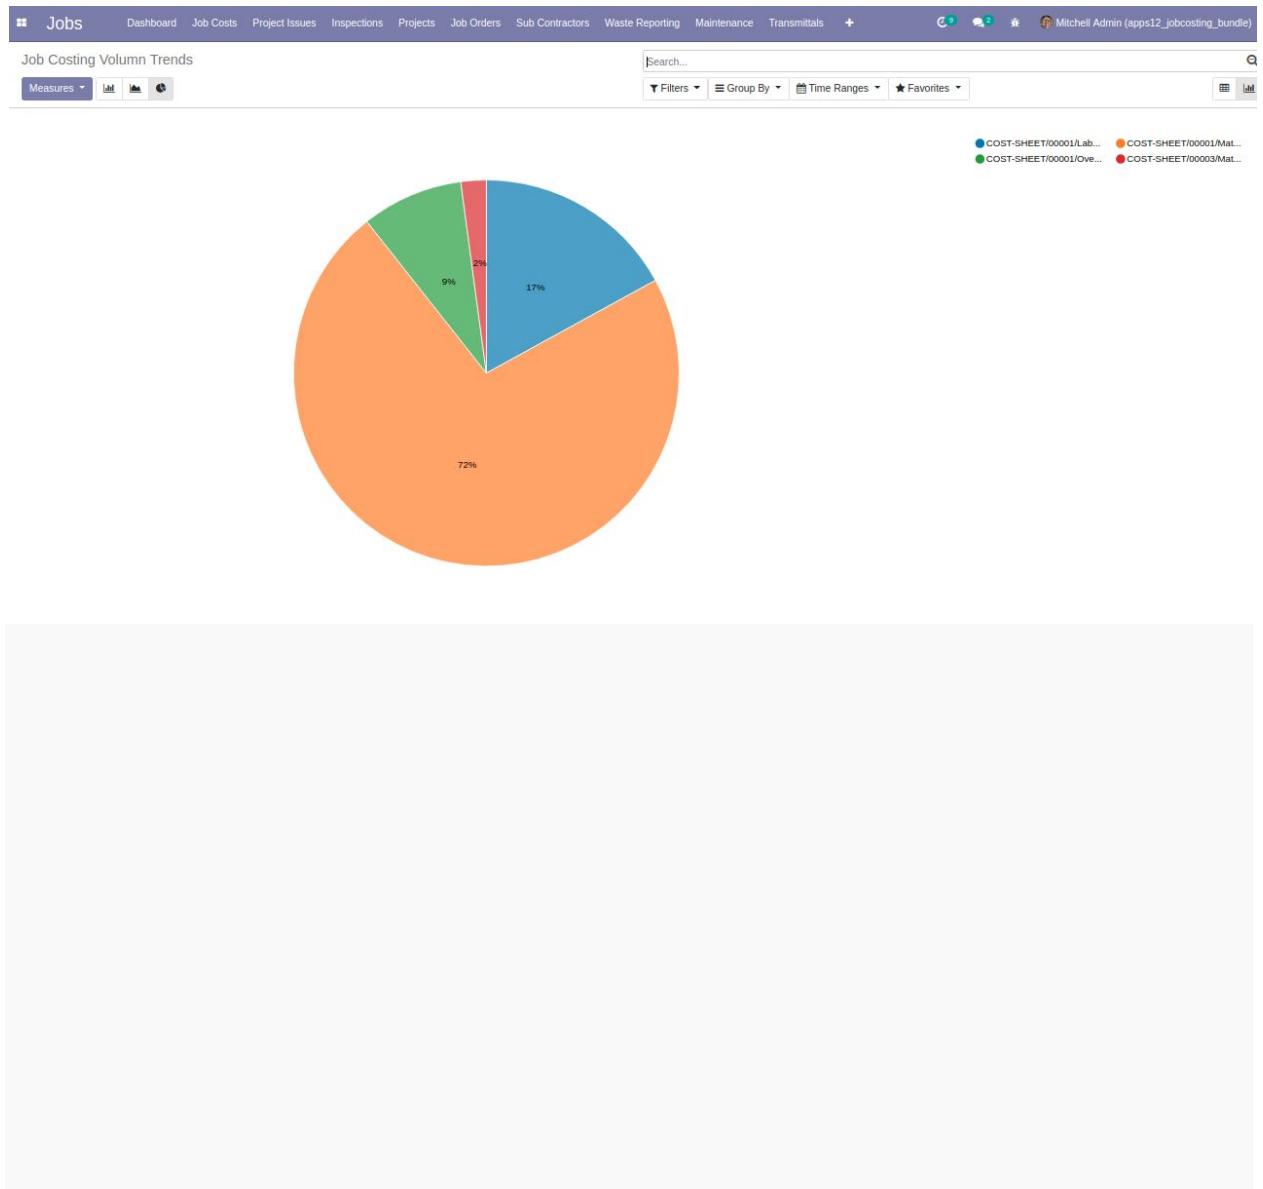



Actual Cost on Job Cost Sheet

❖ A job cost sheet is a compilation of the actual costs of a job. This is typically formatted and distributed for consumption by the management team. Allow you to see real actual cost of Purchase, Vendor bill on Cost sheet.

COST-SHEET/00001																																																																																																																										
12 Purchase Or... 8 HR Timeshe... 21 Vendor Invo... Issues Job Estimations																																																																																																																										
Name	New	Project	Construction of Hypol Heights	Create Date	01/01/2019																																																																																																																					
Project	Construction of Hypol Heights	Created Date																																																																																																																								
Analytic Account	Hypol Heights - The Jackson Group	Created By	Mitchell Admin																																																																																																																							
Job Order	Project Initiation	Company	Your Company																																																																																																																							
Customer	Lumber Inc	Currency	USD																																																																																																																							
		Description	Sale Reference																																																																																																																							
<table border="1"> <thead> <tr> <th>Materials</th><th>Labours</th><th>Overhead</th><th>Date</th><th>Job Type</th><th>Product</th><th>Description</th><th>Reference</th><th>Planned Qty</th><th>Uom</th><th>Cost / Unit</th><th>Actual Purchased Quantity</th><th>Actual Purchased Cost</th><th>Actual Vendor Bill Quantity</th><th>Actual Vendor Bill Cost</th><th>Cost Price Sub Total</th></tr> </thead> <tbody> <tr> <td>01/01/2019</td><td>Site-Preparation-MAT</td><td>Cement</td><td>Cement</td><td>50.00</td><td>Unit(s)</td><td>350.00</td><td></td><td>200.00</td><td></td><td>70,000.00</td><td>40.00</td><td>800.00</td><td>\$ 17,500.00</td><td></td><td></td></tr> <tr> <td>01/02/2019</td><td>Site-Preparation-MAT</td><td>Bricks</td><td>Bricks</td><td>2,000.00</td><td>Unit(s)</td><td>10.00</td><td></td><td>2,000.00</td><td></td><td>20,000.00</td><td>30.00</td><td>900.00</td><td>\$ 20,000.00</td><td></td><td></td></tr> <tr> <td>01/03/2019</td><td>Site-Preparation-MAT</td><td>Tiles</td><td>Tiles</td><td>500.00</td><td>Unit(s)</td><td>40.00</td><td></td><td>570.00</td><td></td><td>25,400.00</td><td>200.00</td><td>12,000.00</td><td>\$ 20,000.00</td><td></td><td></td></tr> <tr> <td>01/04/2019</td><td>Site-Preparation-MAT</td><td>Iron</td><td>Iron</td><td>500.00</td><td>kg</td><td>35.00</td><td></td><td>500.00</td><td></td><td>100,000.00</td><td>45.00</td><td>1,575.00</td><td>\$ 17,500.00</td><td></td><td></td></tr> <tr> <td>01/04/2019</td><td>Site-Preparation-MAT</td><td>White Cement</td><td>White Cement</td><td>100.00</td><td>Unit(s)</td><td>35.00</td><td></td><td>45.00</td><td></td><td>675.00</td><td>40.00</td><td>800.00</td><td>\$ 3,500.00</td><td></td><td></td></tr> <tr> <td>01/08/2019</td><td>Site-Preparation-MAT</td><td>Door</td><td>Door</td><td>25.00</td><td>Unit(s)</td><td>2,000.00</td><td></td><td>1.00</td><td></td><td>2,500.00</td><td>25.00</td><td>50,000.00</td><td>\$ 50,000.00</td><td></td><td></td></tr> </tbody> </table>											Materials	Labours	Overhead	Date	Job Type	Product	Description	Reference	Planned Qty	Uom	Cost / Unit	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Cost Price Sub Total	01/01/2019	Site-Preparation-MAT	Cement	Cement	50.00	Unit(s)	350.00		200.00		70,000.00	40.00	800.00	\$ 17,500.00			01/02/2019	Site-Preparation-MAT	Bricks	Bricks	2,000.00	Unit(s)	10.00		2,000.00		20,000.00	30.00	900.00	\$ 20,000.00			01/03/2019	Site-Preparation-MAT	Tiles	Tiles	500.00	Unit(s)	40.00		570.00		25,400.00	200.00	12,000.00	\$ 20,000.00			01/04/2019	Site-Preparation-MAT	Iron	Iron	500.00	kg	35.00		500.00		100,000.00	45.00	1,575.00	\$ 17,500.00			01/04/2019	Site-Preparation-MAT	White Cement	White Cement	100.00	Unit(s)	35.00		45.00		675.00	40.00	800.00	\$ 3,500.00			01/08/2019	Site-Preparation-MAT	Door	Door	25.00	Unit(s)	2,000.00		1.00		2,500.00	25.00	50,000.00	\$ 50,000.00		
Materials	Labours	Overhead	Date	Job Type	Product	Description	Reference	Planned Qty	Uom	Cost / Unit	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Cost Price Sub Total																																																																																																											
01/01/2019	Site-Preparation-MAT	Cement	Cement	50.00	Unit(s)	350.00		200.00		70,000.00	40.00	800.00	\$ 17,500.00																																																																																																													
01/02/2019	Site-Preparation-MAT	Bricks	Bricks	2,000.00	Unit(s)	10.00		2,000.00		20,000.00	30.00	900.00	\$ 20,000.00																																																																																																													
01/03/2019	Site-Preparation-MAT	Tiles	Tiles	500.00	Unit(s)	40.00		570.00		25,400.00	200.00	12,000.00	\$ 20,000.00																																																																																																													
01/04/2019	Site-Preparation-MAT	Iron	Iron	500.00	kg	35.00		500.00		100,000.00	45.00	1,575.00	\$ 17,500.00																																																																																																													
01/04/2019	Site-Preparation-MAT	White Cement	White Cement	100.00	Unit(s)	35.00		45.00		675.00	40.00	800.00	\$ 3,500.00																																																																																																													
01/08/2019	Site-Preparation-MAT	Door	Door	25.00	Unit(s)	2,000.00		1.00		2,500.00	25.00	50,000.00	\$ 50,000.00																																																																																																													



❖ Allow you to see actual cost of timesheet on Labour Cost sheet.

Screenshot of Odoo Job Costing module showing a Labour Cost Sheet.

Job Cost Sheets / COST-SHEET/00001

COST-SHEET/00001

Name	New	Create Date	01/01/2019							
Project	Construction of Hypol Heights	Closed Date								
Analytic Account	Hypol Heights - The Jackson Group	Created By	Mitchell Admin							
Job Order	Project Initiation	Company	YourCompany							
Customer	Lumber Inc	Currency	USD							
Description	Sale Reference									
Materials		Labour								
Date	Job Type	Product	Description	Reference	Hours	Cost / Unit	Actual Timesheet Hours	Actual Timesheet Cost	Cost Price	Sub Total
01/09/2019	Site-Preparation-LAB	Ground Floor Wages	Ground Floor Wages		08:00	100.00	26:00	1,800.00	\$ 800.00	
01/16/2019	Site-Preparation-LAB	Tiles Fixing	Tiles Fixing		08:00	120.00	24:00	1,800.00	\$ 960.00	
01/18/2019	Site-Preparation-LAB	Waterproofing	Waterproofing		08:00	100.00	08:00	0.00	\$ 800.00	
01/17/2019	Site-Preparation-LAB	Italian Marble Fixing	Italian Marble Fixing		08:00	25.00	00:00	0.00	\$ 200.00	
					32:00	345.00	56:00		2,760.00	

Job Cost Details

Total Material Cost:	\$ 128,500.00
Total Labour Cost:	\$ 2,760.00
Total Overhead Cost:	\$ 640.00
Total Cost:	\$ 131,900.00



- ❖ Overhead With Actual Costing Details
- ❖ Actual overhead costs incurred, allocated using the actual quantity.

Job Cost Sheets / COST-SHEET/00001

[Edit](#) [Create](#)

[Print](#) [Action](#)

[Done](#) [Create Estimation](#) [Cancel](#)

1 / 1 < >

COST-SHEET/00001																
<table border="1"> <tr> <td>12 Purchase Or...</td> <td>8 HR Timeshe...</td> <td>21 Vendor Invol...</td> </tr> <tr> <td>Issues</td> <td>Job Estimations</td> <td></td> </tr> </table>											12 Purchase Or...	8 HR Timeshe...	21 Vendor Invol...	Issues	Job Estimations	
12 Purchase Or...	8 HR Timeshe...	21 Vendor Invol...														
Issues	Job Estimations															
Name	New	Create Date	01/01/2019													
Project	Construction of Hypol Heights	Closed Date														
Analytic Account	Hypol Heights - The Jackson Group	Created By	Mitchell Admin													
Job Order	Project Initiation	Company	YourCompany													
Customer	Lumber Inc	Currency	USD													
Description	Sale Reference															
Materials	Labours	Overhead														
Date	Job Type	Product	Description	Reference	Basis	Planned Qty	Uom	Cost / Unit	Actual Purchased Quantity	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Cost Price Sub Total			
01/08/2019	Site-Preparation-OHD	Electricity Bill	Electricity Bill			1.00	Unit(s)	200.00	1.00	2,500.00	1.00	2,500.00	\$ 200.00			
01/29/2019	Site-Preparation-OHD	[EXP_CTD] Car Travel Expenses	Car Travel Expenses			1.00	km	300.00	1.00	500.00	1.00	500.00	\$ 300.00			
01/24/2019	Site-Preparation-OHD	Truck Rent	Truck Rent			1.00	Unit(s)	120.00	1.00	1,000.00	1.00	1,000.00	\$ 120.00			
01/23/2019	Site-Preparation-OHD	Wiring Works	Wiring Works			1.00	Unit(s)	20.00	1.00	500.00	1.00	500.00	\$ 20.00			
						4.00		640.00	4.00	4.00	4.00	640.00				
Job Cost Details Total Material Cost: \$ 128,500.00 Total Labour Cost: \$ 2,760.00																




Job Costing / Contracting Costing Report

❖ Allow you to view Job Costing Values Analysis for Job Costsheets.

Job Costing Column Trends									
Measures	=	+ ▲	Search...	▼ Filters	≡ Group By	Time Ranges	★ Favorites	Print	Export
♦ Total									
Count	Actual Purchased Cost	Actual Timesheet Cost	Actual Vendor Bill Cost	Planned Quantity	Purchase Quantity	Timesheet Quantity	Vendor Quantity / Hours		
- Total	39	771,375.00	12,000.00	245,050.00	13,129.00	8,480.00	58.00	1,506.00	64.00
- COST-SHEET/00001	39	771,375.00	12,000.00	245,050.00	13,129.00	8,480.00	58.00	1,506.00	64.00
- Site-Preparation-LAB	8	0.00	12,000.00	0.00			58.00		64.00
+ Ground Floor Wages	4	0.00	7,200.00	0.00			24.00		32.00
+ Tiles Feeding	3	0.00	4,800.00	0.00			24.00		24.00
+ Waterproofing	1	0.00	0.00	0.00			8.00		8.00
- Site-Preparation-MAT	27	766,875.00	0.00	240,550.00	13,125.00	8,476.00		1,502.00	
+ Bricks	2	40,000.00	0.00	1,800.00	4,000.00	4,000.00		30.00	
+ Cement	2	140,000.00	0.00	1,600.00	100.00	400.00		40.00	
+ Door	1	2,500.00	0.00	50,000.00	25.00	1.00		25.00	
+ Iron	2	200,000.00	0.00	3,150.00	1,000.00	1,000.00		45.00	
+ Tiles	15	381,000.00	0.00	180,000.00	7,500.00	2,850.00		1,212.00	
+ White Cement	5	8,375.00	0.00	4,000.00	500.00	225.00		150.00	
- Site-Preparation-OHD	4	4,500.00	0.00	4,500.00	4.00	4.00			
+ [EXP_CST] Car Travel Expenses	1	500.00	0.00	500.00	1.00	1.00			
+ Electricity Bill	1	2,500.00	0.00	2,500.00	1.00	1.00			
+ Truck Rent	1	1,000.00	0.00	1,000.00	1.00	1.00			
+ Wiring Works	1	500.00	0.00	500.00	1.00	1.00			



- ❖ Pie charts are useful when comparing the size of individual data elements of Costsheets.

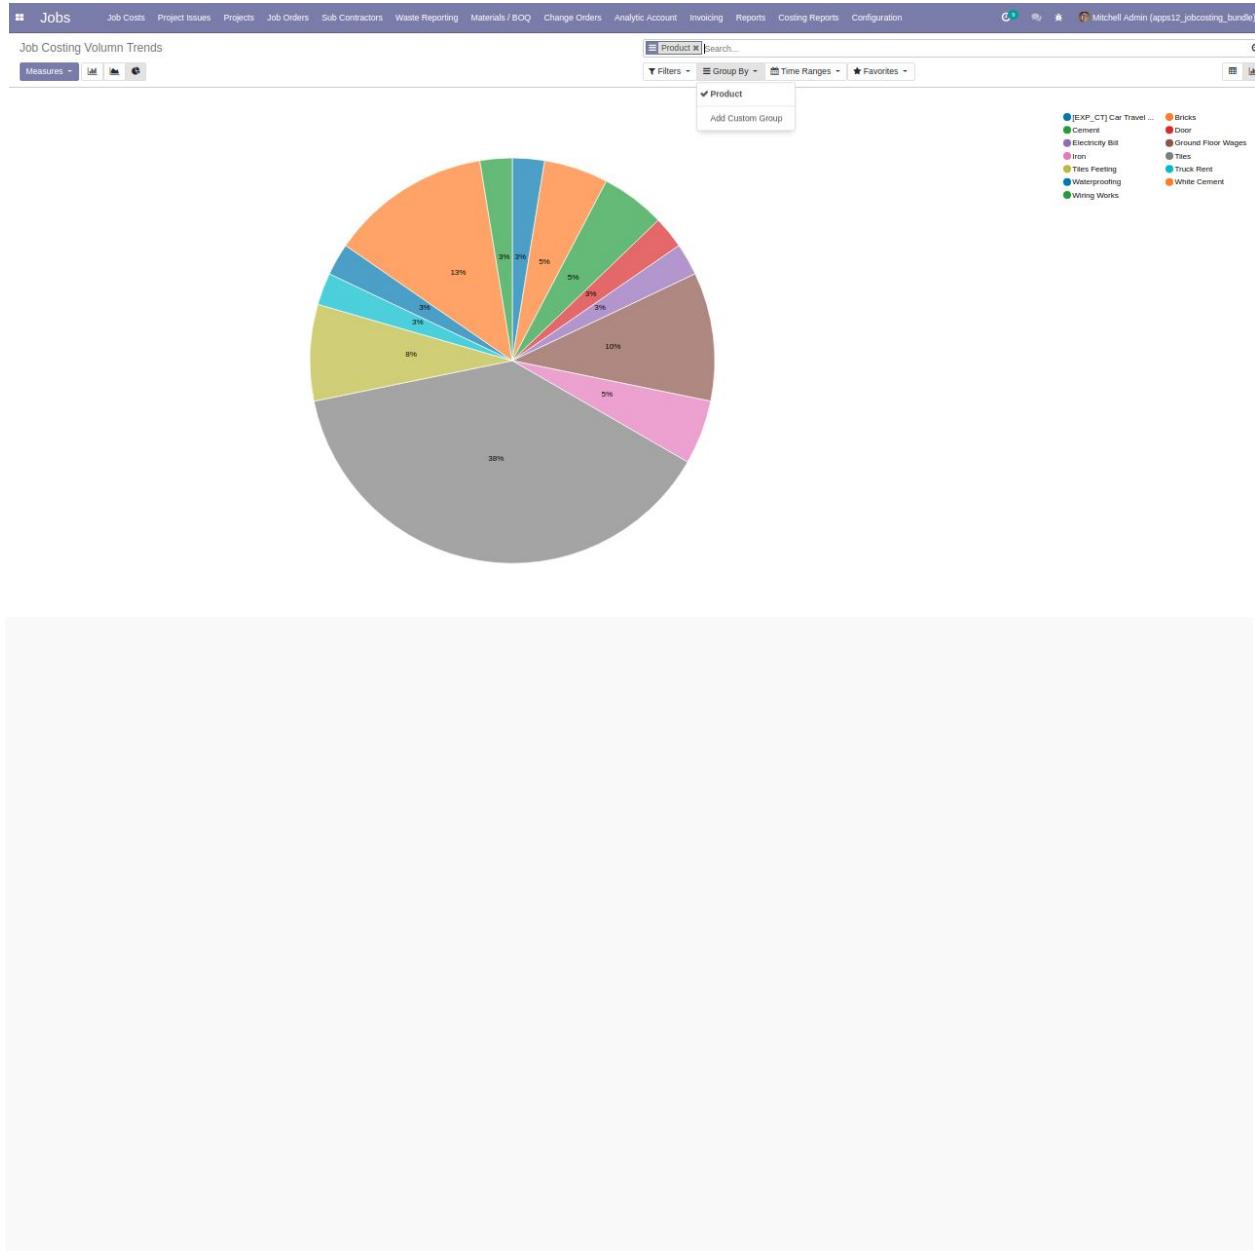



Profit and Loss Report Job Costing

- ❖ Customer Invoice - Job Costsheets and Job Costsheets Line.

Invoices / INV/2019/0004

Edit Create Print Action 6 / 10 Draft Open Paid

Send & Print Register Payment Add Credit Note Preview

INV/2019/0004																																																																																													
Customer	Lumber Inc 3202 Hannah Street Asheville NC 28801 United States			Invoice Date	01/25/2019																																																																																								
Delivery Address	Andrew Smith			Due Date	02/24/2019																																																																																								
Payment Terms	30 Net Days			Salesperson	Mitchell Admin																																																																																								
Progress Billing Title	Residential Construction			Job Cost Sheet	COST-SHEET/00001																																																																																								
Project				Sales Team	Europ																																																																																								
Cash Rounding Method				Currency	USD																																																																																								
<table border="1"> <thead> <tr> <th colspan="2">Invoice Lines</th> <th colspan="10">Other Info</th> </tr> <tr> <th>Product</th> <th>Description</th> <th>Job Cost Center</th> <th>Job Cost Line</th> <th>Account</th> <th>Analytic Account</th> <th>Analytic Tags</th> <th>Quantity</th> <th>Unit of Measure</th> <th>Price</th> <th>Disc (%)</th> <th>Taxes</th> <th>Subtotal</th> <th>Total</th> </tr> </thead> <tbody> <tr> <td>Cement</td> <td>Cement</td> <td>COST-SHEET/00001</td> <td>Cement</td> <td>200000 Product Sales</td> <td></td> <td></td> <td>40.000</td> <td>Unit(s)</td> <td>350.00</td> <td>0.00</td> <td>(Tax 15.00%)</td> <td>\$ 14,000.00</td> <td>\$ 16,100.00</td> </tr> <tr> <td>Bricks</td> <td>Bricks</td> <td>COST-SHEET/00001</td> <td>Bricks</td> <td>200000 Product Sales</td> <td></td> <td></td> <td>30.000</td> <td>Unit(s)</td> <td>35.00</td> <td>0.00</td> <td>(Tax 15.00%)</td> <td>\$ 1,050.00</td> <td>\$ 1,207.50</td> </tr> <tr> <td>Tiles</td> <td>Tiles</td> <td>COST-SHEET/00001</td> <td>Tiles</td> <td>200000 Product Sales</td> <td></td> <td></td> <td>200.000</td> <td>Unit(s)</td> <td>50.00</td> <td>0.00</td> <td>(Tax 15.00%)</td> <td>\$ 10,000.00</td> <td>\$ 11,500.00</td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> <td>~~~~~</td> <td></td> <td></td> <td>~~~~~</td> <td>~~~~~</td> <td>~~~~~</td> <td>~~~~~</td> <td>~~~~~</td> <td>~~~~~</td> <td>~~~~~</td> </tr> </tbody> </table>												Invoice Lines		Other Info										Product	Description	Job Cost Center	Job Cost Line	Account	Analytic Account	Analytic Tags	Quantity	Unit of Measure	Price	Disc (%)	Taxes	Subtotal	Total	Cement	Cement	COST-SHEET/00001	Cement	200000 Product Sales			40.000	Unit(s)	350.00	0.00	(Tax 15.00%)	\$ 14,000.00	\$ 16,100.00	Bricks	Bricks	COST-SHEET/00001	Bricks	200000 Product Sales			30.000	Unit(s)	35.00	0.00	(Tax 15.00%)	\$ 1,050.00	\$ 1,207.50	Tiles	Tiles	COST-SHEET/00001	Tiles	200000 Product Sales			200.000	Unit(s)	50.00	0.00	(Tax 15.00%)	\$ 10,000.00	\$ 11,500.00					~~~~~			~~~~~	~~~~~	~~~~~	~~~~~	~~~~~	~~~~~	~~~~~
Invoice Lines		Other Info																																																																																											
Product	Description	Job Cost Center	Job Cost Line	Account	Analytic Account	Analytic Tags	Quantity	Unit of Measure	Price	Disc (%)	Taxes	Subtotal	Total																																																																																
Cement	Cement	COST-SHEET/00001	Cement	200000 Product Sales			40.000	Unit(s)	350.00	0.00	(Tax 15.00%)	\$ 14,000.00	\$ 16,100.00																																																																																
Bricks	Bricks	COST-SHEET/00001	Bricks	200000 Product Sales			30.000	Unit(s)	35.00	0.00	(Tax 15.00%)	\$ 1,050.00	\$ 1,207.50																																																																																
Tiles	Tiles	COST-SHEET/00001	Tiles	200000 Product Sales			200.000	Unit(s)	50.00	0.00	(Tax 15.00%)	\$ 10,000.00	\$ 11,500.00																																																																																
				~~~~~			~~~~~	~~~~~	~~~~~	~~~~~	~~~~~	~~~~~	~~~~~																																																																																



## ❖ Job Costsheet Material Tab - Actual Invoice Subtotal

Job Cost Sheets / COST-SHEET/00001

Name		Project		Project Team		Tags		Analytic Account		Job Order		Customer		Job Costing		Job Costing Profit & Loss		Company		Currency		Description		Safe Reference		Customer Invoice		Billable Method			
New		Construction of Hypol Heights		Construction of Hypol Heights		Flooring works Painting Works Color Estimation		Hypol Heights - The Jackson Group		Project Initiation		Lumber Inc		01/01/2019		01/01/2019		Mitchell Admin		Your Company		USD									
						</td																									



## ❖ Job Costsheet Overhead Tab - Actual Invoice Subtotal


Jobs    Dashboard    Job Costs    Project Issues    Inspections    Projects    Request for Information    Job Orders    Sub Contractors    Waste Reporting    Maintenance    Transmittals    +    Mitchell Admin (apps12_jobcosting_bundle)

Job Cost Sheets / COST-SHEET/00001    Print    Action    1 / 4

Name	NEW	Create Date	01/01/2019													
Project	Construction of Hypol Heights	Closed Date														
Project Team	Construction of Hypol Heights	Created By	Mitchell Admin													
Tags	Flooring works, Painting Works, Color Estimation	Company	Your Company													
Analytic Account	Hypol Heights - The Jackson Group	Currency	USD													
Job Order	Project Initiation	Description														
Customer	Lumber Inc	Sale Reference														
		Customer Invoice	Based On Actual Vendor Bill Qty													
		Billable Method														
Materials	Labours	Overhead														
Date	Job Type	Product	Description	Reference	Basis	Planned Qty	Uom	Sale Price	Cost / Unit	Actual Requisition	Actual Purchased	Actual Purchased Cost	Actual Vendor Bill Quantity	Actual Vendor Bill Cost	Actual Invoice Subtotal	Cost Pri Sub To
01/08/2019	Site-Preparation- OHD	Electricity Bill	Electricity Bill			1.00	Unit(s)	49,000.00	0.00	0.00	1.00	2,500.00	1.00	2,500.00	96,995.00	\$ 49,000.
01/29/2019	Site-Preparation- OHD	[EXP_C1] Car Travel Expenses	Car Travel Expenses			1.00	km	55,000.00	0.00	0.00	1.00	500.00	1.00	500.00	96,995.00	\$ 55,000.
01/24/2019	Site-Preparation- OHD	Truck Rent	Truck Rent			1.00	Unit(s)	58,000.00	0.00	0.00	1.00	1,000.00	1.00	1,000.00	97,145.00	\$ 58,000.
01/23/2019	Site-Preparation- OHD	Wiring Works	Wiring Works			1.00	Unit(s)	59,000.00	0.00	0.00	1.00	500.00	1.00	500.00	97,175.00	\$ 59,000.
						4.00		221,000.00	0.00	0.00	4.00		4.00		221,000.	

Job Cost Details





## Material Consumption on Job Order / Work Order

- ❖ Your inventory or internal picking staff can choose job order and type during inventory picking and transfer so it can be link with your jobs.

Screenshot of Odoo Inventory module showing a Work Order (WH/IN/00011) details page.

**Header:**

- Inventory
- Overview
- Operations
- Master Data
- Reporting
- Configuration
- Mitchell Admin (apps12_jobcosting_bundle)

Buttons: Print, Action, Mark as Todo, Cancel, Draft, Waiting, Ready, Done.

Page Number: 1 / 29

**Work Order Details:**

Partner	Andrew Smith	Scheduled Date	01/31/2019 10:40:47
Operation Type	YourCompany: Receipts	Source Document	
Project	Construction of Hypol Heights	Owner	
Job Order	Flooring Works		
Destination Location	WH/Stock		

**Operations:**

Product	Initial Demand	Done	Unit of Measure	Consumption Type	Job Order
Cement	50.000	0.000	Unit(s)	Raw Material	Flooring Works
White Cement	50.000	0.000	Unit(s)	Raw Material	Flooring Works
Tiles	500.000	0.000	Unit(s)	Requisition Consumption	Flooring Works
Bricks	200.000	0.000	Unit(s)	Job Consumption	Flooring Works

Buttons at the bottom: Send message, Log note, Schedule activity, Following, 1.

Today

YourCompany, Mitchell Admin - now



- ❖ Job Orders with stock moves also material consumption types on consumed materials.

Jobs    Dashboard    Job Costs    Project Issues    Inspections    Projects    Request for Information    Job Orders    Sub Contractors    Waste Reporting    Maintenance    +    G 3 11 *    Mitchell Admin (apps12_jobcosting_bundle)


Job Orders / Flooring Works    Print ▾    Action ▾    10 / 13


JOB/0004		Flooring Works																																
		0 Sub-tasks	Active	2 Jobcosts																														
		Stock Moves	0 Notes	Subcontractor Jobs																														
			0 Purchase Re...	More ▾																														
Project	Construction of Hypol Heights	Deadline	05/30/2019																															
Project Phase	Flooring Works	Tags	Flooring																															
Assigned to	Mitchell Admin	Website Customer	Ready Mat																															
Project Team	Construction of Hypol Heights	Website Customer Name	Ready Mat																															
Sales Order Item		Website Customer Email	ready.mat55@example.com																															
Starting Date	01/02/2019 11:00:42	Website Customer Phone	8989989989																															
Ending Date	03/30/2019 11:30:42	Job Order Category	New Request																															
Job Number	JOB/00006																																	
<table border="1"> <thead> <tr> <th>Description</th> <th>Job Instructions</th> <th>Waste Materials</th> <th>Material Plannings</th> <th>Website</th> <th>Purchase Requisitions</th> <th>Subtasks</th> <th>Consumed Materials</th> <th>Material Requisitions</th> </tr> </thead> <tbody> <tr> <td>Timesheets</td> <td>Extra Info</td> <td>Timesheet Employee Users</td> <td>Maintenance Equipment</td> <td></td> <td>Maintenance Requests</td> <td>Work Duration</td> <td>Customer Signature</td> <td></td> </tr> <tr> <td>Google Drawing Document</td> <td>Contract Drawing</td> <td>Project Team</td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> </tbody> </table>								Description	Job Instructions	Waste Materials	Material Plannings	Website	Purchase Requisitions	Subtasks	Consumed Materials	Material Requisitions	Timesheets	Extra Info	Timesheet Employee Users	Maintenance Equipment		Maintenance Requests	Work Duration	Customer Signature		Google Drawing Document	Contract Drawing	Project Team						
Description	Job Instructions	Waste Materials	Material Plannings	Website	Purchase Requisitions	Subtasks	Consumed Materials	Material Requisitions																										
Timesheets	Extra Info	Timesheet Employee Users	Maintenance Equipment		Maintenance Requests	Work Duration	Customer Signature																											
Google Drawing Document	Contract Drawing	Project Team																																
Product	Description	Initial Demand	Unit of Measure	Consumption Type																														
Cement	Cement	50.000	Unit(s)	Raw Material																														
White Cement	White Cement	50.000	Unit(s)	Raw Material																														
Tiles	Tiles	500.000	Unit(s)	Requisition Consumption																														
Bricks	Bricks	200.000	Unit(s)	Job Consumption																														



- ❖ Material Consumption Types: Consumption is known as direct or final consumption, when the goods satisfy human wants directly and immediately complete the jobs.

A screenshot of a software application window titled "Jobs". The menu bar includes "Dashboard", "Job Costs", "Project Issues", "Inspections", "Projects", "Request for Information", "Job Orders", "Sub Contractors", "Waste Reporting", "Maintenance", and "Budget Analysis". A sidebar on the right lists various configuration options like "Stages", "Job Types", and "RFI Configuration". The main content area shows a list titled "Material Consumption Types" with checkboxes for items such as "Name", "Job Consumption", "Project Consumption", etc. A search bar and filter buttons are at the top of the list table.





## Job Order Material Requisition

- ❖ Create Material Requisition from Job Orders with different material planning.

Job Orders / Flooring Works

[Edit](#) [Create](#) [Print](#) [Action](#)

[Share](#) [Create Subtasks](#) [Create Material Requisition](#) [Create Subcontractor Job](#) [Create Repair Request](#) [Create / Edit Cost Sheet](#)

[Send by Email](#)

10 / 13 [<](#) [>](#)

**JOB/0004**  
Flooring Works

Sub-tasks	Active	Jobcosts
0	2	0
Stock Moves	Notes	Subcontractor Jobs
0	0	0
Purchase Re...	More ▾	

**Project** Construction of Hypol Heights  
**Project Phase** Flooring Works  
**Assigned to** Mitchell Admin  
**Project Team** Construction of Hypol Heights  
**Sales Order Item**  
**Starting Date** 01/02/2019 11:00:42  
**Ending Date** 03/30/2019 11:30:42  
**Job Number** JOB/00006

**Deadline** 05/30/2019  
**Tags** Flooring  
**Website Customer** Ready Mat  
**Website Customer Name** Ready Mat  
**Website Customer Email** ready.mat55@example.com  
**Website Customer Phone** 8989989989  
**Job Order Category** New Request

[Description](#) [Job Instructions](#) [Waste Materials](#) [Material Plannings](#) [Website](#) [Purchase Requirements](#) [Subtasks](#) [Consumed Materials](#) [Material Requisitions](#)

[Timesheets](#) [Extra Info](#) [Timesheet Employee Users](#) [Maintenance Equipment](#) [Maintenance Requests](#) [Work Duration](#) [Customer Signature](#)

[Google Drawing Document](#) [Contract Drawing](#) [Project Team](#)


Product	Description	Quantity	Unit of Measure	Requisition Action	Requisition Line	Job Cost Sheet
Bricks	Bricks	50	Unit(s)	Internal Picking		COST-SHEET/00002
Cement	Cement	20	Unit(s)	Internal Picking		COST-SHEET/00002
Tiles	Tiles	50	Unit(s)	Internal Picking		COST-SHEET/00002



- ❖ Create new Material Requisition or Update Existing Material Requisition from Job Order.

Screenshot of the Odoo Job Orders module showing a Material Purchase Requisition for a Flooring Works project. The requisition is for an existing item, and the details include:

Product	Description	Quantity	Unit of Measure	Requisition Action	Requisition Line	Job Cost Sheet
Bricks	Bricks	50	Unit(s)	Internal Picking		COST-SHEET/00002
Cement	Cement	20	Unit(s)	Internal Picking		COST-SHEET/00002
Tiles	Tiles	50	Unit(s)	Internal Picking		COST-SHEET/00002
Iron	Iron	40	kg	Internal Picking		COST-SHEET/00002





- ❖ Created New Material Requisition from Job Order with Material Planning.

**Requisitions** Purchase Requisition

Purchase Requisitions / EPR00004

Print Action

Edits Create Confirm Cancel

New Waiting Department Approval Waiting IR Approved Purchase Order Created Received

**EPR00004**

Employee	Mitchell Admin	Requisition Date	01/31/2019
Department	Management	Received Date	
Company	YourCompany	Requisition Deadline	
Requisition Responsible		Analytic Account	
Maintenance Request			
Job Order			
Project	Construction of Hypol Heights		
Task / Job Order	Flooring Works		
Task / Job Order User	Mitchell Admin		
Project	Construction of Hypol Heights		

Requisitions Lines Picking Details Other Information Materials / BOQ Cost

Requisition Action	Product	Job Cost Center	Job Cost Line	Description	Quantity	Unit of Measure	Vendors
Internal Picking	Bricks			Bricks	50.00	Unit(s)	
Internal Picking	Cement			Cement	20.00	Unit(s)	
Internal Picking	Tiles			Tiles	50.00	Unit(s)	
Internal Picking	Iron			Iron	40.00	kg	
Internal Picking	White Cement			White Cement	50.00	kg	

Reason for Requisitions





## Scan & Capture Photo for Job Task / Issue

- ❖ On Job Issue with Scan/Capture Photo in My Account Portal.

The screenshot shows a web-based account portal interface. At the top, there's a navigation bar with "WEBSITE", "Pages", "Customize", "Promote", "My Website", "+ New", and "Edit". The main content area displays a job issue record:

<b>Assigned to :</b> Mitchell Admin	<b>Customer:</b> Deco Addict
<b>Email :</b> deco.addict82@example.com	<b>Phone:</b> (603)-996-3829
<b>Issue Team :</b> Construction Team	<b>Team Leader :</b> Joel Willis
<b>Department :</b>	<b>Analytic Account :</b> Transcube Plaza Construction
<b>Project :</b> Transcube Plaza Construction	<b>Priority :</b> High
<b>Create Date :</b> 01/29/2019 14:53:48	<b>Close Date :</b> 01/29/2019 15:05:39
<b>Is Issue Closed? :</b>	<b>Total Hours Spent :</b> 0.0

Below this, there's a large gray box labeled "Scan & Upload Photo" with "Scan" and "Submit" buttons. Underneath, a section titled "Captured Photos" shows three thumbnail images, each labeled "ISSUE-00002".



## ❖ View Captured Photos in My Account Portal

WEBSITE ▾ Pages Customize Promote

My Website ▾ + New Edit

Home Contact us Mitchell Admin ▾

Your Issues ISSUE-00002

ISSUE-00002 - Damage Brick and Low Quality Cement (#2) Status: Work in Progress

Assigned to : Mitchell Admin  
 Email : deco.addict82@example.com  
 Issue Team : Construction Team  
 Department :  
 Project : Transcube Plaza Construction  
 Create Date : 01/29/2019 14:53:48  
 Is Issue Closed? :

Customer: Deco Addict  
 Phone: (603)-996-3829  
 Team Leader : Joel Willis  
 Analytic Account : Transcube Plaza Construction  
 Priority : High  
 Close Date : 01/29/2019 15:05:39  
 Total Hours Spent : 0.0



Scan Submit

Captured Photos

WEBSITE ▾ Pages Customize Promote

My Website ▾ + New Edit

Assigned to : Mitchell Admin  
 Email : deco.addict82@example.com  
 Issue Team : Construction Team  
 Department :  
 Project : Transcube Plaza Construction  
 Create Date : 01/29/2019 14:53:48  
 Is Issue Closed? :

Customer: Deco Addict  
 Phone: (603)-996-3829  
 Team Leader : Joel Willis  
 Analytic Account : Transcube Plaza Construction  
 Priority : High  
 Close Date : 01/29/2019 15:05:39  
 Total Hours Spent : 0.0

Scan & Upload Photo

Scan Submit

Captured Photos

 ISSUE-00002
 ISSUE-00002
 ISSUE-00002



## ❖ Created Issue in Backend.

Issues      Project Issues    Analytic Account    Invoicing    Reports    Configuration      Mitchell Admin

Project Issues "/" ISSUE-00002

Print ▾ Action ▾ 2 / 3 Set To Close New Assigned Work in Progress Needs More Info Needs Reply Reopened Solution Suggested Closed

ISSUE-00002			
Damage Brick and Low Quality Cement		<input checked="" type="checkbox"/> Active <input type="checkbox"/> Create Invoice <input type="checkbox"/> Create Task <input type="checkbox"/> Task <input type="checkbox"/> Analytic Account	
Type of Issue	Low Quality Material	Customer	Deco Addict
Type of Issue Subject	Machines are not Good	Phone	(603)-996-3829
Assign To	Mitchell Admin	Allow Users	<a href="#">Joel Willis</a> (Mitchell Admin)
Email	deco.addict82@example.com		
Company	Probuse Consulting Service Pvt. Ltd.		
Construction Team	Construction Team	Team Leader	Joel Willis
Project	Transcube Plaza Construction	Analytic Account	Transcube Plaza Construction
Job Order		Priority	High
Job Cost Sheet	COST-SHEET/00002	Category	Material Deficiencies
Job Cost Line	Ciment		
Department			



## ❖ Captured Photos Tab on Project Issue backend

Screenshot of the Odoo Project Issues module showing the 'Capture Photos' tab.

**Project Issues "/" ISSUE-00002**

**General Information:**

- Create Date: 01/29/2019 19:23:48
- Is Issue Closed?:
- Close Date: 01/29/2019 19:35:39
- Total Hours Spent: 0:00
- Total Consumed Hours: 0:00
- Total Purchase Hours: 0:00
- Remaining Hours: 0:00

**Capture Photos:**

Name	Filename	Website	Resource Model	Resource Field	Resource ID	Type	Company	Created by	Created on
ISSUE-00002	ISSUE-00002	My Website	construction.ticket		2	File	Probuse Consulting Service Pvt. Ltd.	OdooBot	01/31/2019 17:24:16
ISSUE-00002	ISSUE-00002	My Website	construction.ticket		2	File	Probuse Consulting Service Pvt. Ltd.	OdooBot	01/30/2019 11:11:43
ISSUE-00002	ISSUE-00002	My Website	construction.ticket		2	File	Probuse Consulting Service Pvt. Ltd.	OdooBot	01/30/2019 11:05:44

**Buttons:** Description, Timesheets, Add Invoice Lines, General Information, Customer Rating, Capture Photos.

**Log:** Send message, Log note, Today, (3) Following, 2.

## ❖ View Photo in Chatter on Project Issue.

Screenshot of the Odoo Project Issues module showing Chatter feed.

**Project Issues "/" ISSUE-00002**

**Chatter Feed:**

- YourCompany, Mitchell Admin - 15 minutes ago: 
- YourCompany, Joel Willis - a day ago: 
- YourCompany, Joel Willis - a day ago: 



## ❖ On Task Capture Photo in My Account Portal

This is a preview of the customer portal. [Back to edit mode](#)

Tasks: Machine Failure

Machine Failure (#43)

Project: CNC Machine

Date: 01/29/2019

Deadline: 02/08/2019

Assigned to

Mitchell Admin  
+1 555-555-5555  
admin@yourcompany.example.com

Description

Scan & Upload Photo

Scan Submit

## ❖ View Captured Photos in My Account Portal

This is a preview of the customer portal. [Back to edit mode](#)

Tasks: Machine Failure

Machine Failure (#43)

Project: CNC Machine

Date: 01/29/2019

Deadline: 02/08/2019

Assigned to

Mitchell Admin  
+1 555-555-5555  
admin@yourcompany.example.com

Description





- ❖ Capture Photos Tab on Project Task Backend also Photos on task chatter.

Screenshot of the Odoo Project Task Backend and Chatter interface:

**Backend Task View:**

- Project: Machine Failure
- Assigned to: Mitchell Admin
- Deadline: 02/08/2019
- Tags: None
- Sub-tasks: 0
- Active: 1
- Jobcosts: 0

Name	Filename	Website	Resource Model	Resource Field	Resource ID	Type	Company	Created by	Created on
Machine Failure	Machine Failure	My Website	project.task		43	File	Probuse Consulting Service Pvt. Ltd.	OdooBot	01/31/2019 17:44:34

**Chatter View:**

- Send message
- Log note
- Schedule activity
- Today
- 1 message from YourCompany, Mitchell Admin - 6 minutes ago

YourCompany, Mitchell Admin - 6 minutes ago



## ❖ Project Issue - Mobile View

A screenshot of a mobile application interface for managing project issues. At the top, there is a navigation bar with a home icon, a search icon, and a menu icon. The main content area shows a list of issues under the heading "Your Issues". The first item in the list is "ISSUE-00002". Below the list, detailed information about this issue is displayed. The information includes:

**Assigned to :** Mitchell Admin  
**Customer:** Deco Addict  
**Email :** deco.addict82@example.com  
**Phone:** (603)-996-3829  
**Issue Team :** Construction Team  
**Team Leader :** Joel Willis  
**Department :**  
**Analytic Account :** Transcube Plaza Construction  
**Project :** Transcube Plaza Construction



The screenshot shows a mobile application interface for Probuse. At the top, there is a header bar with the Probuse logo on the left and a menu icon (three horizontal lines) on the right. Below the header, the word "Construction" is displayed. Underneath, several details are listed: "Priority : High", "Create Date : 01/29/2019", "14:53:48", "Close Date : 01/29/2019 15:05:39", "Is Issue Closed? : (checkbox)", and "Total Hours Spent : 0.0".

In the center, there is a large gray rectangular area with the text "Scan & Upload Photo" in black. Below this area are two blue buttons labeled "Scan" and "Submit".

At the bottom, there is a section titled "Captured Photos" which contains a thumbnail image of a document and the text "ISSUE-00002".



A screenshot of a mobile application interface for Probuse. At the top, there is a header bar with the Probuse logo on the left and a menu icon (three horizontal lines) on the right. Below the header, there are two blue buttons labeled "Scan" and "Submit". The main content area is titled "Captured Photos" and contains three items, each with a small thumbnail image and the text "ISSUE-00002". Below this section, there is a title "Message and communication history" followed by a subtitle "4 comments". At the bottom, there is a text input field with a placeholder "Write a message..." and a small profile picture of a person on the left.



## ❖ Project Task - Mobile View

A screenshot of a mobile application interface showing a project task. At the top, there's a navigation bar with icons for home, tasks, and search, followed by the text "/ Tasks" and "Machine Failure". Below this is a header section with the title "Machine Failure (#43)" and a "Status:" field. Underneath, detailed information is provided: "Project: CNC Machine", "Date: 01/29/2019", and "Deadline: 02/08/2019". The "Assigned to" section shows a profile picture of a man named "Mitchell Admin" and his contact information: "+1 555-555-5555" and "admin@yourcompany.example.com". At the bottom, there is a "Description" section which is currently empty.



A screenshot of a mobile application interface. At the top left is the PROBUSE logo. A menu icon is at the top right. Below is a large grey box with the text "Scan &amp; Upload Photo". Underneath are two blue buttons labeled "Scan" and "Submit". Below these buttons is a section titled "Captured Photos" containing a thumbnail image of a machine part with a red circle on it, labeled "Machine Failure". At the bottom of the screen, there is a section titled "Message and communication history" with a sub-section for "1 comment". On the far left of this section is a small profile picture of a person. To the right is a text input field with the placeholder "Write a message...".



## Risk Management for Construction and Contracting Projects

- ❖ Create Incident from Project and also added risk registers on project.

Screenshot of the Probuse Project Management software interface showing the Risk Register for the 'Construction of Hypol Heights' project.

The top navigation bar includes: Project, Projects, All Tasks, Project Phases, Reporting, Configuration, and a user profile for 'Mitchell Admin (apps12_jobcosting_bundle)'.

The main page title is 'Projects / Construction of Hypol Heights'. Below it are buttons for Edit, Create, Print, Action, Share, Create Sales Order, and Create Incident.

The Risk Register section displays the following details:

- Project Title:** Construction of Hypol Heights
- Name of the tasks:** Tasks
- Allow timesheets:**
- Document Count:** 0 Documents
- Task Count:** 8 Tasks
- Timesheet Count:** 8 Timesheets
- Status:** Active
- Jobcosts:** 4 Jobcosts
- Notes:** 8 Notes
- Phases:** 8 Phases
- More:** More ▾

The Risk Register table has the following columns: Risk, Description, Category, Risk Response, Risk Type, and Probability(%).

Risk	Description	Category	Risk Response	Risk Type	Probability(%)
The laborers glass was rolled out	The laborers glass was rolled out	Financial Risk	Transfer	Safety Hazards that lead to worker accidents and injures	10.00
During Flooring Works hands are crack	During Flooring Works hands are crack	Management Related Risk	Transfer	Safety Hazards that lead to worker accidents and injures	30.00
Low margin and profit risk	Low margin and profit risk	Organizational Risks	Reject	Managing Change Orders	40.00
Loss of reputation of future business	Loss of reputation of future business	Migrate the Risk	Transfer	Unknown Site Conditions	50.00
During floor footing lags are fatured and injured	During floor footing lags are fatured and injured	Management Related Risk	Reduce	Safety Hazards that lead to worker accidents and injures	25.00



❖ Create Risk Incident from Project.

The screenshot shows the Odoo Project module interface. A modal window titled "Create Incident" is open, showing fields for "Risk Incident Description" (Inadequate Wiring and Overhead Circuits), "Assigned to" (Mitchell Admin), and "Project" (Construction of Hypol Heights). An "Incident Photo" is attached, showing a photograph of electrical wiring. Below the modal, a table displays a risk matrix:

Risk	Description	Category	Risk Response	Risk Type	Probability(%)
The laborers glass was rolled out	The laborers glass was rolled out	Financial Risk	Transfer	Safety Hazards that lead to worker accidents and injures	10.00
During Flooring Works hands are crack	During Flooring Works hands are crack	Management Related Risk	Transfer	Safety Hazards that lead to worker accidents and injures	30.00
Low margin and profit risk	Low margin and profit risk	Organizational Risks	Reject	Managing Change Orders	40.00
Loss of reputation of future business	Loss of reputation of future business	Migrate the Risk	Transfer	Unknown Site Conditions	50.00
During floor footing lags are fatured and injured	During floor footing lags are fatured and injured	Management Related Risk	Reduce	Safety Hazards that lead to worker accidents and injures	25.00



## ❖ Created Risk Incident from Project.

The screenshot shows the Odoo Risk Management module. At the top, there's a navigation bar with links for Risks, Projects, Risk Incidents, Reporting, and Configuration. On the right, it shows the user "Mitchell Admin (apps12_jobcosting_bundle)" and some system icons. Below the navigation is a toolbar with buttons for Edit, Create, Share, Create Subtasks, Create Material Requisition, Create Subcontractor Job, Create Repair Request, Create / Edit Cost Sheet, Create Incident, and Send by Email. The main content area displays a risk incident for project "JOB/0023" titled "Inadequate Wiring and Overhead Circuits". The project details include: Project (Construction of Hypol Heights), Project Phase (Not specified), Assigned to (Mitchell Admin), Project Team (Sales Order Item), Starting Date (02/02/2019 15:52:43), Ending Date (Not specified), and Job Number (JOB/0023). To the right of the project details is a summary table:

Sub-tasks	Active	Jobcosts
Stock Moves	Notes	Subcontractor Jobs
Purchase Re...	More ▾	

Below the project details, there's a horizontal menu with tabs: Description, Job Instructions, Waste Materials, Risk Management (which is selected), Material Planning, Website, Purchase Requisitions, Subtasks, Consumed Materials, Material Requisitions, Timesheets, Extra Info, Timesheet Employee Users, Maintenance Equipment, Maintenance Requests, Work Duration, Customer Signature, Google Drawing Document, Contract Drawing, Project Team, and Capture Photos. A sidebar on the left lists Task Incident?, Risk Line, Original Task, and Incident Photo, with a thumbnail image of a photo showing overhead wiring.



❖ Create Incident from Task / Job Order also define risk register.

Screenshot of the Probuse software interface showing a Job Order details page for 'JOB/0004 Flooring Works'.

The top navigation bar includes: Jobs, Dashboard, Job Costs, Project Issues, Inspections, Projects, Request for Information, Job Orders, Sub Contractors, Waste Reporting, Maintenance, Transmittals, Submittals, Materials / BOQ, +, and user info (Mitchell Admin).

Sub-navigation tabs include: Share, Create Subtasks, Create Material Requisition, Create Subcontractor Job, Create Repair Request, Create / Edit Cost Sheet, and Create Incident.

Buttons for Print, Action, and Send by Email are present.

The main content area shows:

- Job Details:** Project: Construction of Hypol Heights, Phase: Flooring Works, Assigned to: Mitchell Admin, Team: Construction of Hypol Heights.
- Timeline:** Starting Date: 01/02/2019 11:00:42, Ending Date: 03/30/2019 11:30:42, Job Number: JOB/00006.
- Customer:** Website Customer Name: Ready Mat, Email: ready.mat55@example.com, Phone: 8989989989.
- Deadline:** 05/30/2019, Tags: Flooring.
- Sub-tasks:** 0 Sub-tasks, 2 Active, 2 Jobcosts.
- Stock Moves:** 0 Stock Moves, 0 Notes, 0 Subcontractor Jobs.
- Purchase Requests:** 0 Purchase Re... More.

Below the main details, there are tabs for Job Instructions, Waste Materials, Material Plannings, Website, Purchase Requisitions, Subtasks, Consumed Materials, and Material Requisitions.

Below these tabs, there are links for Timesheets, Extra Info, Risk Register, Timesheet Employee Users, Maintenance Equipment, Maintenance Requests, Work Duration, and Customer Signature.

At the bottom, there are links for Google Drawing Document, Contract Drawing, Project Team, and Capture Photos.

**Risk Register:**

Risk	Description	Category	Risk Response	Risk Type	Probability(%)
The laborers glass was rolled out	The laborers glass was rolled out	Financial Risk	Transfer	Safety Hazards that lead to worker accidents and injures	25.00
During Flooring Works hands are crack	During Flooring Works hands are crack	Management Related Risk	Transfer	Safety Hazards that lead to worker accidents and injures	40.00
During floor feeling lags are fatigued and injured	During floor feeling lags are fatigued and injured	Management Related Risk	Reduce	Safety Hazards that lead to worker accidents and injures	50.00



## ❖ Create Risk Incident from Task or Job Order.

Screenshot of the Probuse software interface showing the 'Create Incident' dialog box over a 'Job Orders / Flooring Works' project page.

**Create Incident Dialog Box:**

Risk Incident Description	During Flooring work Short Circuits During flooring work short circuits.	Assigned to Project	Mitchell Admin Construction of Hypol Heights
		Incident Photo	

**Job Orders / Flooring Works Project Page:**

Project: Flooring Works  
Assigned to: Mitchell Admin  
Project Team: Construction of Hypol Heights  
Sales Order Item: 01/02/2019 11:00:42  
Starting Date: 03/30/2019 11:30:42  
Job Number: JOB00006

Tags: Flooring, Ready Mat  
Website Customer: ready.mat55@example.com  
Email: 8889898989  
Phone: New Request

Job Instructions, Waste Materials, Material Plannings, Website, Purchase Requisitions, Subtasks, Consumed Materials, Material Requisitions, Timesheets, Extra Info, Risk Register, Timesheet Employee Users, Maintenance Equipment, Maintenance Requests, Work Duration, Customer Signature, Google Drawing Document, Contract Drawing, Project Team, Capture Photos

**Risk Register Table:**

Risk	Description	Category	Risk Response	Risk Type	Probability(%)
The laborers glass was rolled out	The laborers glass was rolled out	Financial Risk	Transfer	Safety Hazards that lead to worker accidents and injuries	25.00
During Flooring Works hands are crack	During Flooring Works hands are crack	Management Related Risk	Transfer	Safety Hazards that lead to worker accidents and injuries	40.00
During floor feeling lags are fatened and injured	During floor feeling lags are fatened and injured	Management Related Risk	Reduce	Safety Hazards that lead to worker accidents and injuries	50.00



❖ Created Risk Incident on Task / Job Order.

Risk Management   Risks Projects Risk Incidents Reporting Configuration

Risk Incidents / During Flooring work Short Circuits

Edit Create Print Action 1 / 2

0 Sub-tasks	Active	1 Jobcosts
Stock Moves	0 Notes	Subcontractor Jobs
Purchase Re...		
More ▾		

**JOB/0024**

★ During Flooring work Short Circuits

Project	Construction of Hypol Heights	Deadline
Project Phase		Tags
Assigned to	Mitchell Admin	Website Customer
Project Team	Construction of Himalaya Team	Website Customer Name
Sales Order Item		Website Customer Email
Starting Date	02/02/2019 16:07:29	Website Customer Phone
Ending Date		Job Order Category
Job Number	JOB/00026	

Description Job Instructions Waste Materials Risk Management Material Planning Website Purchase Requisitions Subtasks Consumed Materials

Material Requisitions Timesheets Extra Info Timesheet Employee Users Maintenance Equipment Maintenance Requests Work Duration Customer Signature

Google Drawing Document Contract Drawing Project Team Capture Photos

Task Incident? Risk Line Original Task Incident Photo

Flooring Works



❖ Define Risk Types on Risk Register on Incidents.

A screenshot of a software application titled "Risk Management". The top navigation bar includes links for Risks, Projects, Risk Incidents, Reporting, Configuration, and a user profile for "Mitchell Admin (apps12_jobcosting_bundle)". The main content area is divided into sections: "Risk Types" (with "Create" and "Import" buttons), "Risk Types" (listing categories like Name, Safety Hazards, etc.), and "Risk Response" (listing responses like R001, R003, R006). A search bar and filter options are also present.

Name	Code
Safety Hazards that lead to worker accidents and injures	R001
Managing Change Orders	R003
Unknown Site Conditions	R006



## ❖ Define Risk Categories on Risk Incidents.

Screenshot of the Odoo Risk Management module showing the 'Risk Category' configuration screen. The interface includes a search bar, filters, and a list of risk categories with their corresponding codes.

Name	Code
Financial Risk	FR
Management Related Risk	R003
Organizational Risks	R004
Migrate the Risk	R005

## ❖ Define Risk Response on Risk Incidents.

Screenshot of the Odoo Risk Management module showing the 'Risk Response' configuration screen. The interface includes a search bar, filters, and a list of risk responses with their corresponding codes.

Name	Code
Transfer	R001
Reject	R005
Reduce	R007



## ❖ Project Risk Analysis List View.

Risk Management						Risks	Projects	Risk Incidents	Reporting	Configuration	G 9	U 11	Mitchell Admin (apps)		
Project Risk Analysis			Project Risk Analysis			Task Risk Analysis						Search...	▼ Filters ▾	Group By ▾	★ Favorites ▾
Create		Import											1-5 / 5		
Project	Risk	Category	Risk Type	Risk Response											
<input type="checkbox"/> Construction of Hypol Heights	The laborers glass was rolled out	Financial Risk	Safety Hazards that lead to worker accidents and injures	Transfer											
<input type="checkbox"/> Construction of Hypol Heights	During Flooring Works hands are crack	Management Related Risk	Safety Hazards that lead to worker accidents and injures	Transfer											
<input type="checkbox"/> Construction of Hypol Heights	Low margin and profit risk	Organizational Risks	Managing Change Orders	Reject											
<input type="checkbox"/> Construction of Hypol Heights	Loss of reputation of future business	Migrate the Risk	Unknown Site Conditions	Transfer											
<input type="checkbox"/> Construction of Hypol Heights	During floor feeting lags are fatured and injured	Management Related Risk	Safety Hazards that lead to worker accidents and injures	Reduce											

## ❖ Task Risk Analysis List View.

Risk Management						Risks	Projects	Risk Incidents	Reporting	Configuration	G 9	U 11	Mitchell Admin (apps)		
Task Risk Analysis			Project Risk Analysis			Task Risk Analysis						Search...	▼ Filters ▾	Group By ▾	★ Favorites ▾
Create		Import											1-3 / 3		
Task	Category	Risk Response	Risk	Risk Type	Probability(%)	Project									
<input type="checkbox"/> Flooring Works	Financial Risk	Transfer	The laborers glass was rolled out	Safety Hazards that lead to worker accidents and injures	25.00	Construction									
<input type="checkbox"/> Flooring Works	Management Related Risk	Transfer	During Flooring Works hands are crack	Safety Hazards that lead to worker accidents and injures	40.00	Construction									
<input type="checkbox"/> Flooring Works	Management Related Risk	Reduce	During floor feeting lags are fatured and injured	Safety Hazards that lead to worker accidents and injures	50.00	Construction									



## Job Cost Sheet Import from Excel

- This app will allow you to import Job Cost Sheet from excel.

❖ Sample Excel File for Import Job Cost Sheet

Job Cost Sheet							
1	A	B	C	D	E	F	G
2	Name	Construction Project for Himalaya	Description	Construction Project for Himalaya	Elanzza		
3	Project	Construction of Himalaya Project	Sale Reference	SO0055			
4	Analytic Account	Construction of Himalaya Project					
5	Job Order	Electrification					
6	Customer	Mickle Jackson					
7							
8	Job Cost Details	A cost estimate is the approximation of the cost of a program, project, or operation. Labor burdens, material costs, construction equipment costs, and, if applicable, subcontractor costs are also extended on the estimate detail form.					
9							
10	Materials						
11	Date	Job Type	Product	Description	Reference	Planned Qty	
12	21/05/2019	Material	Cement	Siddhi Cement	WH001	50	
13	22/05/2019	Material	Tiles	Cerra Tiles	CT005	60	
14	23/05/2019	Material	Bricks	Dark Bricks	DB256	2000	
15	24/05/2019	Material	White Cement	White Cement For Tiles Feeting	WHC52	1000	
16	25/05/2019	Material	Sent		SP89	1200	
17	26/05/2019	Material	Iron Stick	Iron Sticks	IS26	1000	
18	28/05/2019	Material	Door	Door	D523	400	
19	29/05/2019	Material	Window	Window	WD653	500	
20	Labours						
21	Date	Job Type	Product	Description	Reference	Hours	
22	21/05/2019	Labour	Wages	Wages	LWG	20	
23	22/05/2019	Labour	Labour for Polishing	Labour for Polishing	CT005	16	
24	23/05/2019	Labour	Labour for Painting	Labour for Painting	DF225	25	
25	24/05/2019	Labour	Electric Work	Labour for Electric Work	LEW	35	
26	25/05/2019	Labour	Door Feeting	Door Feeting	DF225	40	



## ❖ Import Job Cost Sheet Menu

Number	Name	Project	Create Date	Closed Date	Total Cost
COST-SHEET/00229	new	Construction of Himalaya Project	05/07/2019	05/07/2019	0
COST-SHEET/00265	new	Construction of Himalaya Project	05/07/2019		1,540
COST-SHEET/00376	Construction Project for Himalaya	Construction of Himalaya Project	05/08/2019		948,130

## ❖ Wizard for Import Job Cost Sheet from Excel

Date	Job Type	Product	Description	Reference	Basis	Planned Qty	Cost / Unit	Actual Purchased Quantity	Actual Vendor Bill Quantity	Cost Price Sub Total
05/21/2019	Overhead	Electricity Bill	Electricity Bill	EB		10.00 Unit(s)	1,000.00	0.00	0.00	\$ 10,000.00
05/22/2019	Overhead	Truck Rent	Truck Rent	TR		60.00 Unit(s)	500.00	0.00	0.00	\$ 30,000.00
05/23/2019	Overhead	GEB Charges	GEB Charges	GEB56		1.00 Unit(s)	50.00	0.00	0.00	\$ 50.00
05/24/2019	Overhead	Advertising	Advertising	ADVT		10.00 Unit(s)	30.00	0.00	0.00	\$ 300.00
05/25/2019	Overhead	Accounting Fees	Accounting Fees	AFC		20.00 Unit(s)	40.00	0.00	0.00	\$ 800.00
05/26/2019	Overhead	Legal fees	Legal fees	LAF		1.00 Unit(s)	60.00	0.00	0.00	\$ 60.00
05/28/2019	Overhead	Stamp Duty	Stamp Duty	SD		1.00 Unit(s)	70.00	0.00	0.00	\$ 70.00
05/29/2019	Overhead	Travel Expenditures	Travel Expenditures	TE		15.00 Unit(s)	90.00	0.00	0.00	\$ 1,350.00
05/25/2019	Overhead	Employee Salary	Employee Salary	ES		20.00 Unit(s)	500.00	0.00	0.00	\$ 10,000.00
						138.00	2,340.00	0.00	0.00	52,630.00



## ❖ After Imported Customer Job Cost Sheet

Jobs    Job Costs    Projects    Job Orders    Sub Contractors    Materials / BOQ    Configuration

Job Cost Sheets / Job Cost Sheets / COST-SHEET/00377

Edit    Create    Print    Action

Confirm    Cancel    Draft    Confirmed    Done

**COST-SHEET/00377**

Name	Construction Project for Himalaya	Create Date	05/08/2019							
Project	Construction of Himalaya Project	Closed Date								
Analytic Account	Construction of Himalaya Project	Created By	Mitchell Admin							
Job Order	Electrification	Company	Probuse Consulting Service Pvt. Ltd.							
Customer	Mickle Jackson	Currency	USD							
		Description	Construction Project for Himalaya Elanza							
		Sale Reference	SO0055							
<input type="button" value="Purchase Or..."/> <input type="button" value="HR Timeshe..."/> <input type="button" value="Vendor Invoi..."/>										
<input type="button" value="Materials"/> <input type="button" value="Labours"/> <input type="button" value="Overhead"/>										
Date	Job Type	Product	Description	Reference	Planned Qty	Uom	Cost / Unit	Actual Purchased Quantity	Actual Vendor Bill Quantity	Cost Price Sub Total
05/21/2019	Material	Cement	Cement	WH001	50.00	Unit(s)	300.00	0.00	0.00	\$ 15,000.00
05/22/2019	Material	Tiles	Tiles	CT005	60.00	Unit(s)	100.00	0.00	0.00	\$ 6,000.00
05/23/2019	Material	Bricks	Bricks	DB256	2,000.00	Unit(s)	100.00	0.00	0.00	\$ 200,000.00
05/24/2019	Material	White Cement	White Cement	WHC52	1,000.00	Unit(s)	40.00	0.00	0.00	\$ 40,000.00
05/25/2019	Material	Sent	Sent	SP89	1,200.00	kg	100.00	0.00	0.00	\$ 120,000.00
05/26/2019	Material	Iron Stick	Iron Stick	IS26	1,000.00	kg	70.00	0.00	0.00	\$ 70,000.00
05/28/2019	Material	Door	Door	D523	400.00	Unit(s)	400.00	0.00	0.00	\$ 160,000.00
05/29/2019	Material	Window	Window	WD653	500.00	Unit(s)	500.00	0.00	0.00	\$ 250,000.00
					6,210.00		1,610.00	0.00	0.00	<b>\$ 861,000.00</b>

**Job Cost Details**  
A cost estimate is the approximation of the cost of a program, project, or operation.  
Labor burdens, material costs, construction equipment costs, and, if applicable,  
subcontractor costs are also extended on the estimate detail form.

Total Material Cost:	\$ 861,000.00
Total Labour Cost:	\$ 34,500.00
Total Overhead Cost:	\$ 52,630.00
<b>Total Cost:</b>	<b>\$ 948,130.00</b>
